



Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC				Plant: 100 5/19/2026 1:01:06 PM		Tech: J. Horsley PC: C. Golf						
Structure ID: SSMH BB-1-DROP												
P3 MH048RS48S-D				MH RISER w/DROP T/G								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 48" - MH RISER w/DROP T/G - 48" P2) 48" - MH RISER w/DROP T/G - 48" P1) 48" - MH BASE w/DROP Custom Ht T/n - 25" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 14) MH Step ML-10-TDS-NCR - 10"						0 lb 3200 lb 3329 lb 3353 lb 4291 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total: 15935 lb												
Rim: 858'		Rim to Invert: 14.02'		Slack: 0.24"		Sump: 2"		Step Position: 0°				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌵)	Offset		
Invert 1												
Invert 2												
Invert 3	852'	232°	117.375"	8" PVC SDR35	8.5"	Drop Tee 8" PVC	8.5"	8.545"	20.75"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

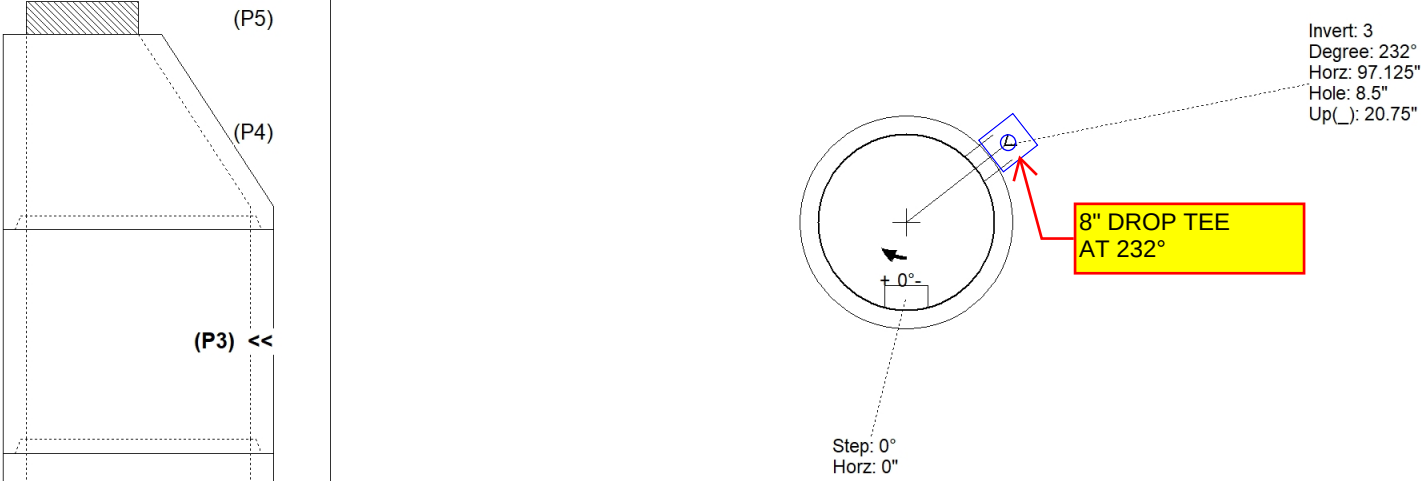

INSIDE WALL DIMENSIONS

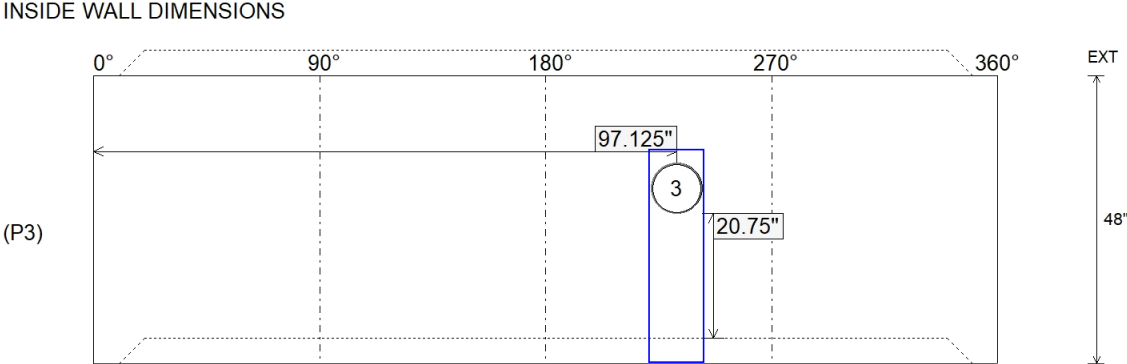

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3329 lb Volume (Net): 0.85cu.yd
----------------------------------	------------------------------------	--	--	--
