


Contractor: Scotty's Contracting & Stone, LLC

PC:	C. Goff
TECH:	J. Horsley
Plant: Beaver Dam	



Slack: 0.48"

Structure Total: 9086 lb

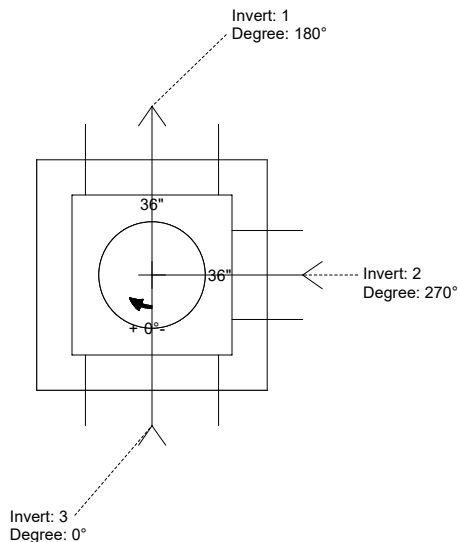


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	553.83'							
Reducer								
Invert 1	548.54'	180°	24" HDPE	27.8"	30"	Hole 30	-1.875"	P1
Invert 2	549.29'	270°	15" HDPE	17.6"	20"	Hole 20	7.75"	P1
Invert 3	548.54'	0°	24" HDPE	27.8"	30"	Hole 30	-1.875"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" - CASTING (cast in) - (P3)

36" x 36" - BX FLAT LID 8inW SPEC. (KY JB-B1) F/F - 8" - (P2)


36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 55" - (P1)

The drawing shows a top-down view of a rectangular assembly. At the top is a shaded rectangular area labeled '24" - CASTING (cast in) - (P3)'. Below this is a large rectangular area defined by a dashed line, labeled '36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 55" - (P1)'. To the right of the casting area, there is a label '36" x 36" - BX FLAT LID 8inW SPEC. (KY JB-B1) F/F - 8" - (P2)' which appears to be a dimension or specification for the lid, although it is not directly adjacent to a specific part in the drawing.

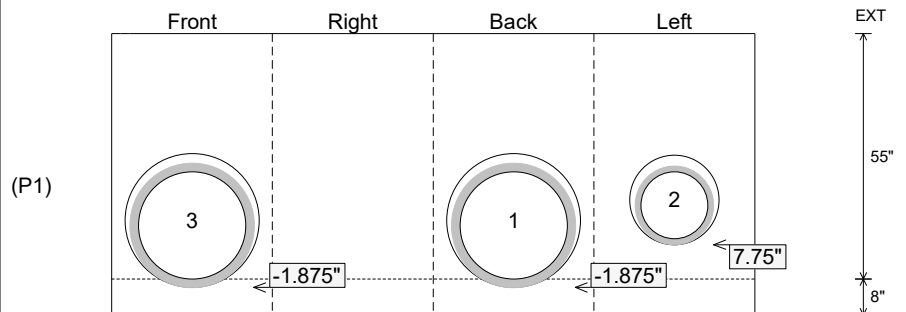
SUBMITTAL
APPROVED BY:

GENERAL NOTES:

1. MANUFACTURE TO ASTM C-913 (LATEST REVISION)
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60)
4. WEIGHT: 1,670 LBS
5. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO FLAT LID FLANGE SIDE UP

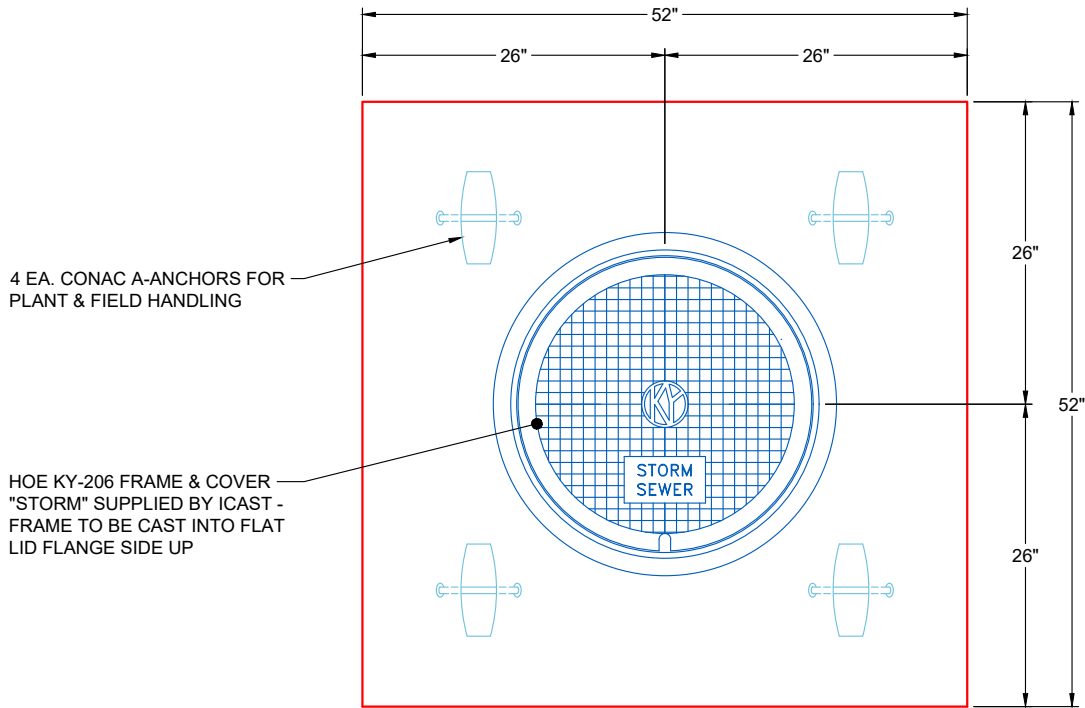

PLAN VIEW



FRONT VIEW

REVISIONS

REV. <u>0</u>	DATE:	NO REVISIONS TO DATE



SUBMITTAL DRAWING: 52" X 52" X 8" FLAT LID SPECIAL		
CUSTOMER: SCOTTY'S CONTRACTING & STONE, LLC		
PROJECT: KYTC CHRISTIAN CO. CALL 100 (241018)		
STRUCTURE: 220		
SALES ORDER NO: 24-4208		
CHECKED BY: B. SMITH	DRAWN BY: K. CARDWELL	
DATE: 06/26/26	SCALE: NTS	PG. 1 OF 1
