



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:35 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 252 (429+39 RT)											
P1		BX3648-08BA48		BOX BASE 8inW, 8inF F/n							
P5) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P4) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P3) 24" x 36" - FIELD ADJUSTMENT - 4.5" P2) 36" x 48" - CB FT REDUCER 24"x36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 48" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 48" - Conseal CS-102 1.00" 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 44 1) Hole - 6					3398 lb 5270 lb 0 lb 1654 lb 6689 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 17217 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 541.63'		Rim to Invert: 7.4'		Slack: 0.3"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	534.23'	270°	32"	36" HDPE	41.7"	Hole 44	44"	44"	-2.85"	0"	
Invert 2	534.23'	90°	32"	36" HDPE	41.7"	Hole 44	44"	44"	-2.85"	0"	
Invert 3	537.425'	270°	11"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	37.94"	-21"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

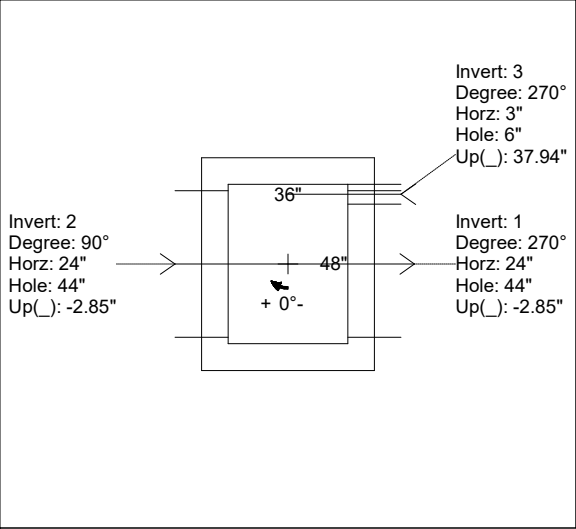

UPSIDE-DOWN VIEW (int. dimensions)

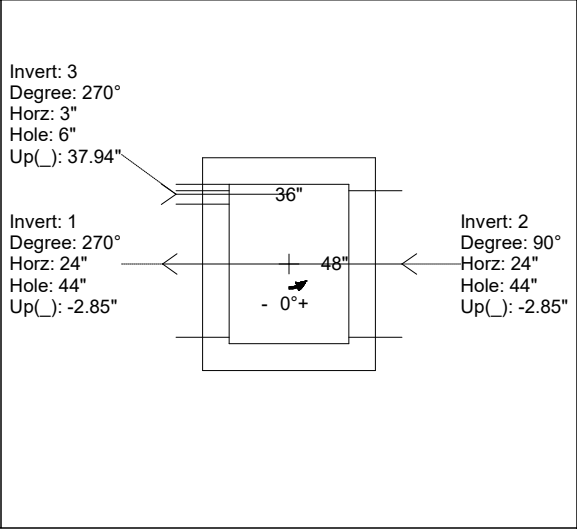

INSIDE WALL DIMENSIONS

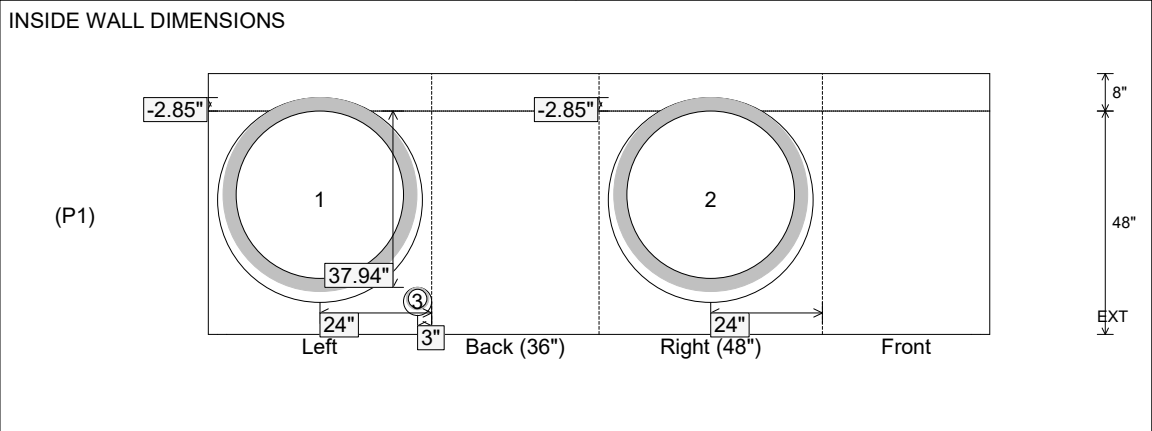

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 6689 lb Volume (Net): 1.71cu.yd
----------------------------------	-------------------------------	--	--	--
