



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 7/30/2026 8:59:17 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 262 (433+25 RT)										
P3 BX2436-08R36				BOX RISER 8inW F/G						
P6) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P5) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P4) 24" x 36" - FIELD ADJUSTMENT - 5" P3) 24" x 36" - BOX RISER 8inW F/G - 36" P2) 36" x 48" - CB FT REDUCER 24"x36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 48" - Conseal CS-102 1.00" 3) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 44 1) DOGHOUSE INVRTD - 26"x24.50" 1) Hole - 6					3400 lb 5270 lb 0 lb 3654 lb 1654 lb 7857 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 22041 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 544.53' Rim to Invert: 11.44' Slack: 0.28" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	540.16'	270°	26"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	14.44"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

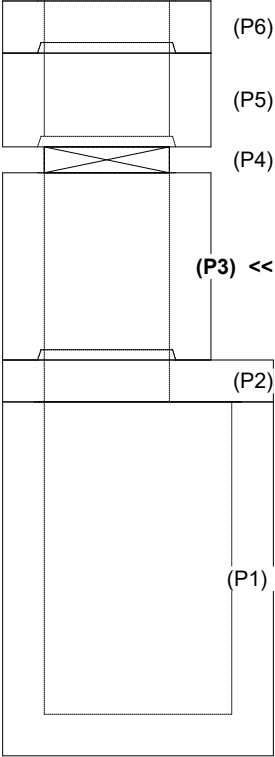


(P6)
(P5)
(P4)
(P3) <<
(P2)
(P1)



Invert: 4
Degree: 270°
Horz: 18"
Hole: 6"
Up(): 14.44"

INSIDE WALL DIMENSIONS



(P3)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 3654 lb Volume (Net): 0.93cu.yd
----------------------------------	----------------------------------	--	--	--
