

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 24" x 36"

Rim to Invert: 4.75'

Floor Height: 8"

Slack: 0"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"
P2) 24" x 36" - FIELD ADJUSTMENT - 4"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25"
1) CASTING - HOE KY-206 F/C (KY TY1)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 20
1) Hole - 6


3398 lb
5270 lb
0 lb
3717 lb
206 lb
0 lb
0 lb
0 lb

Structure Total: 12591 lb

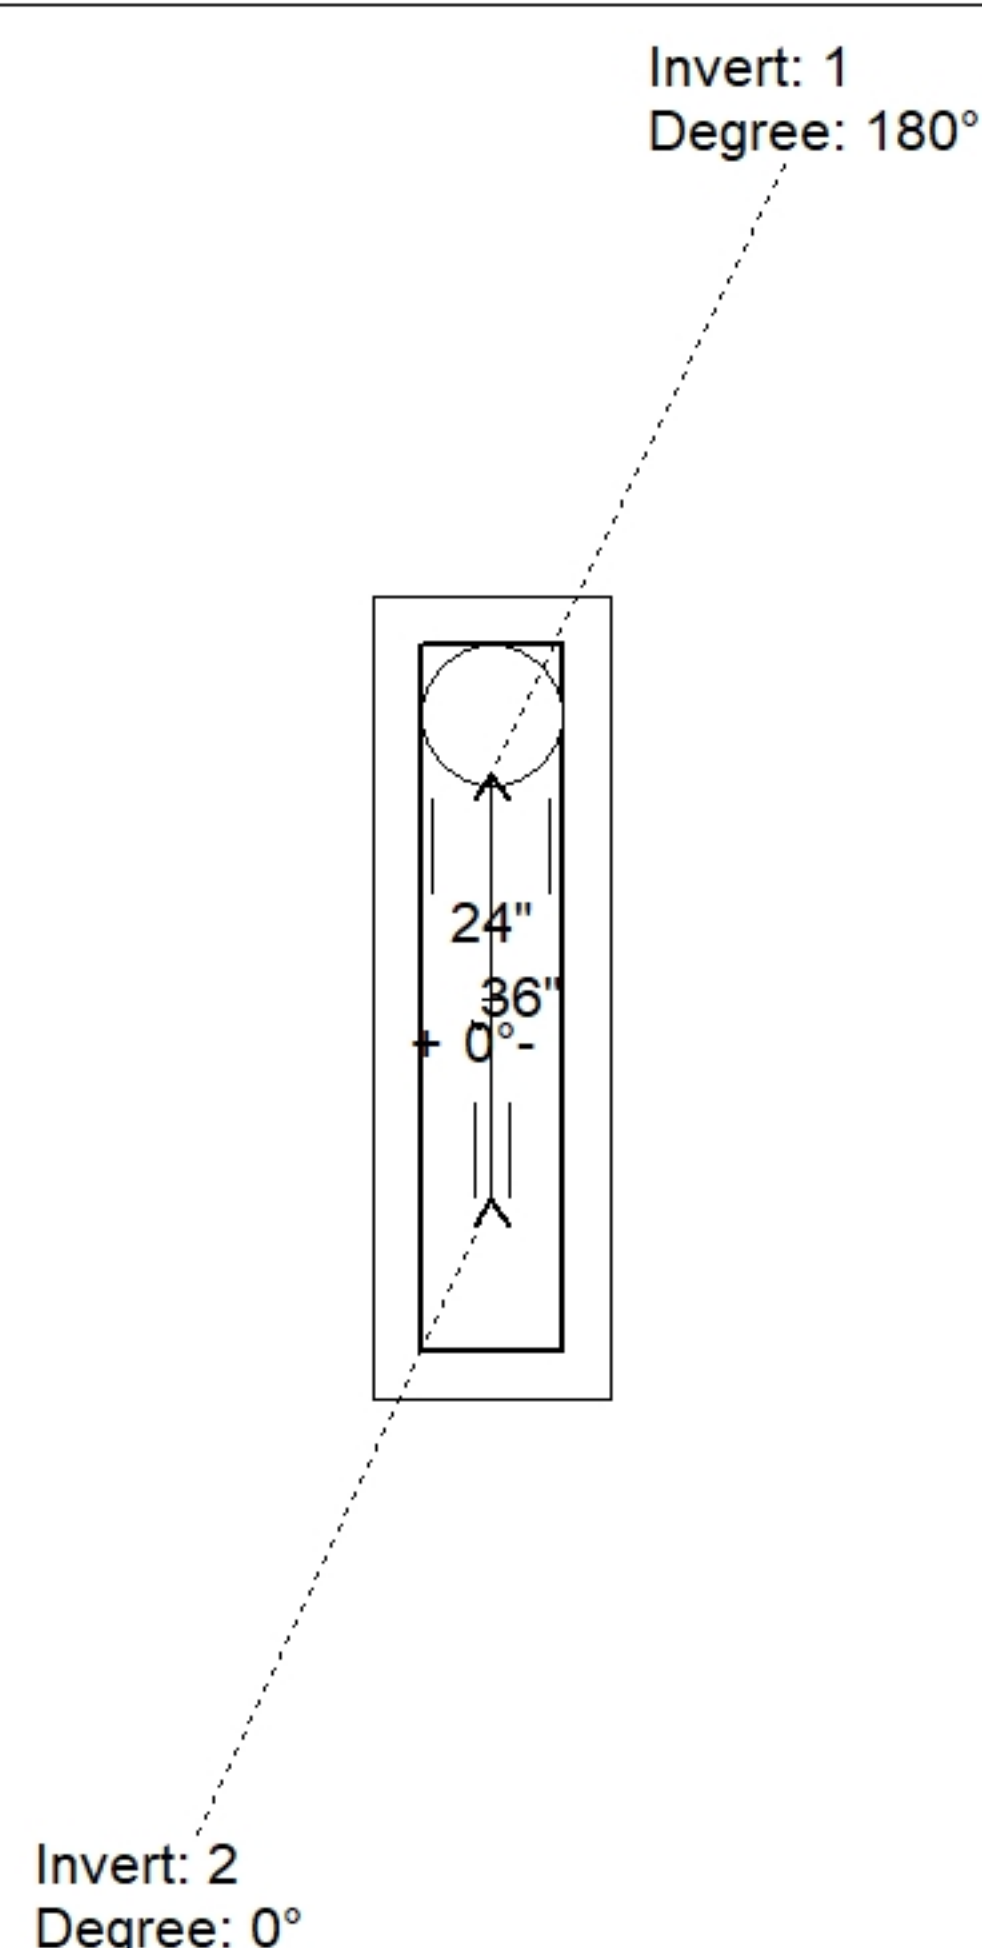

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	527.49'							
Reducer								
Invert 1	522.74'	180°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	524.02'	0°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	14.96"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

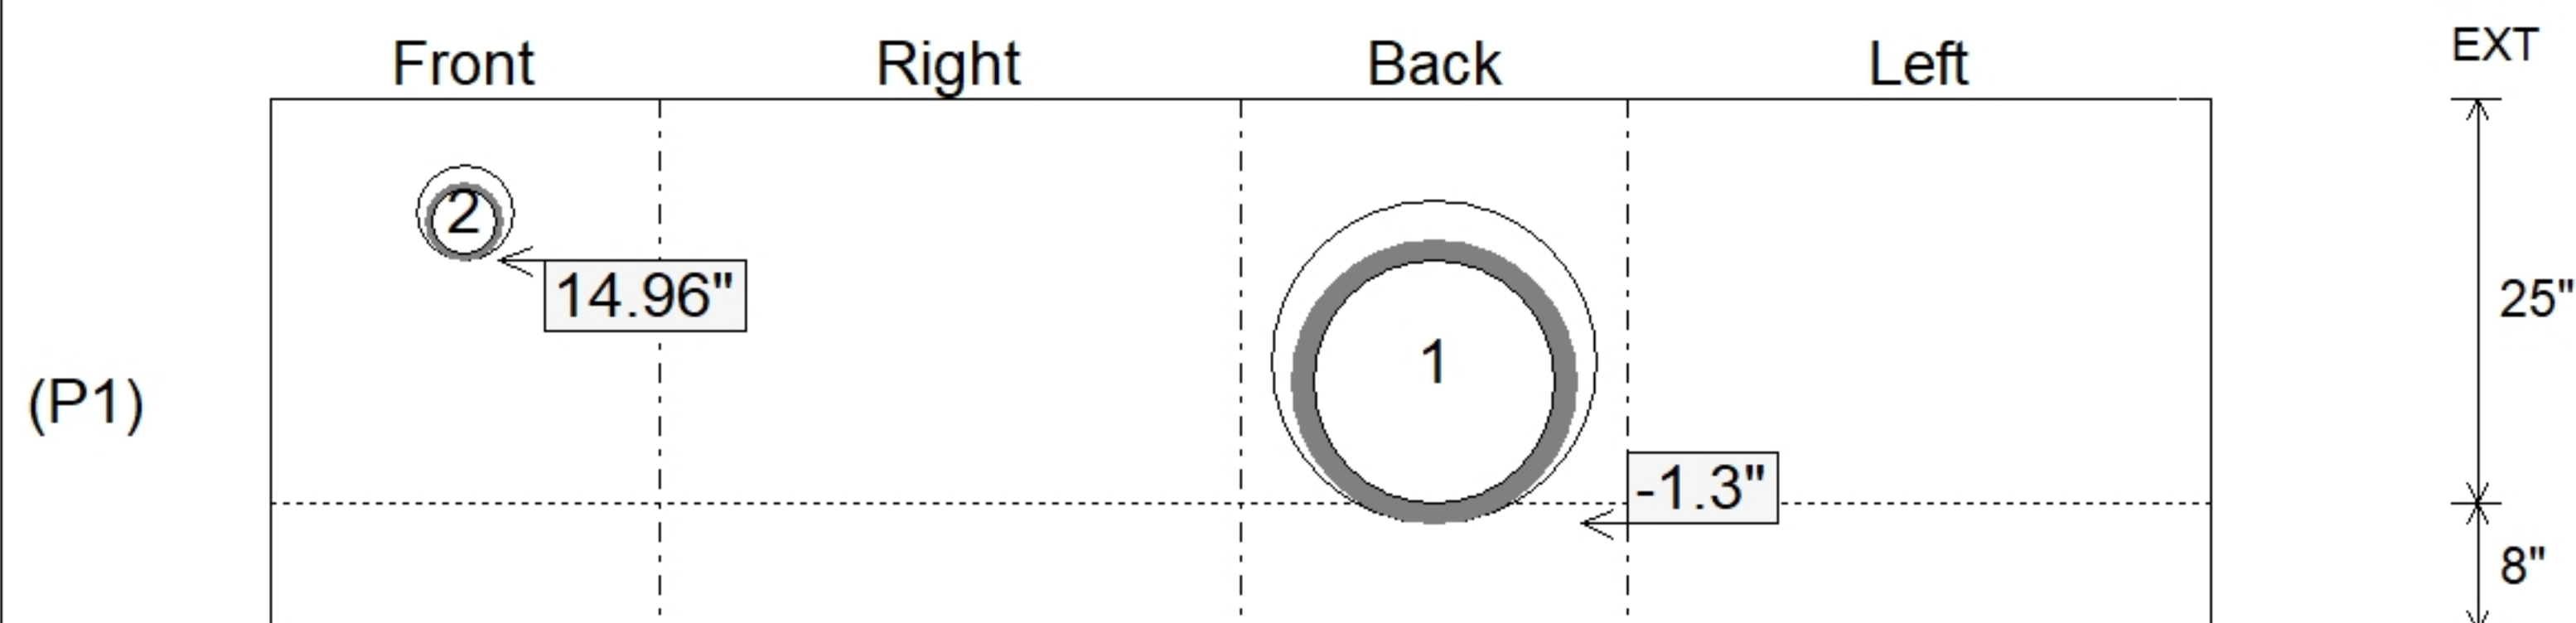

Submittal Drawing
8/3/2026 4:18:07 PM

SUBMITTAL
APPROVED BY:
