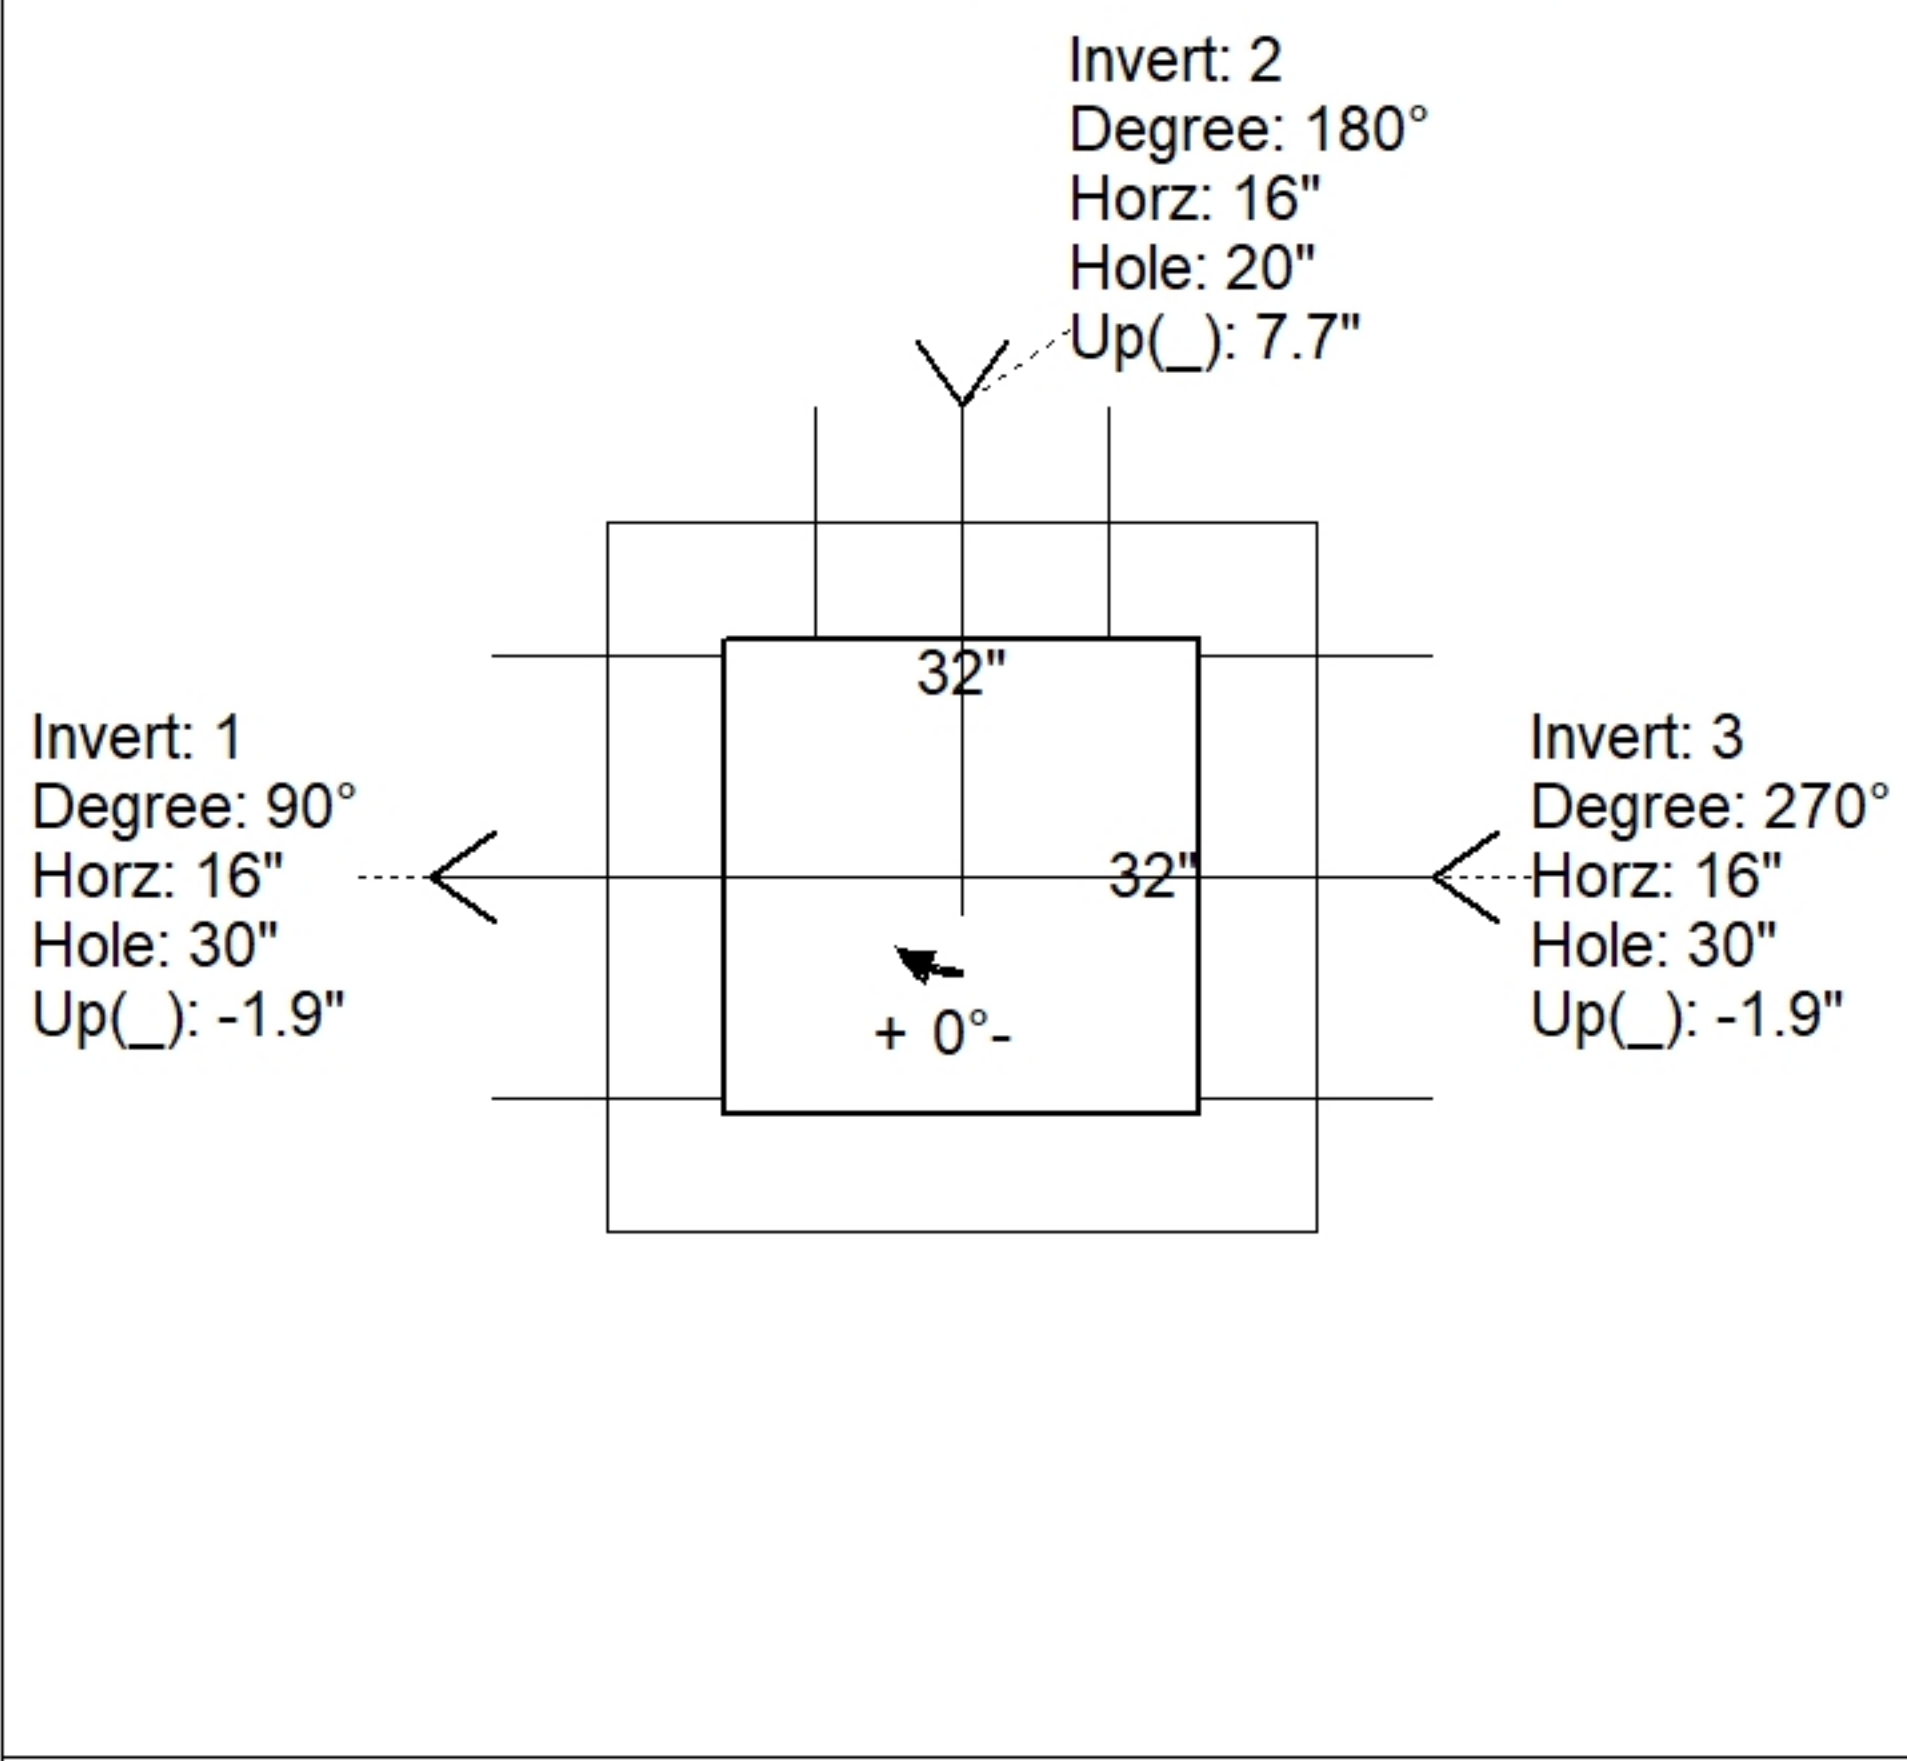
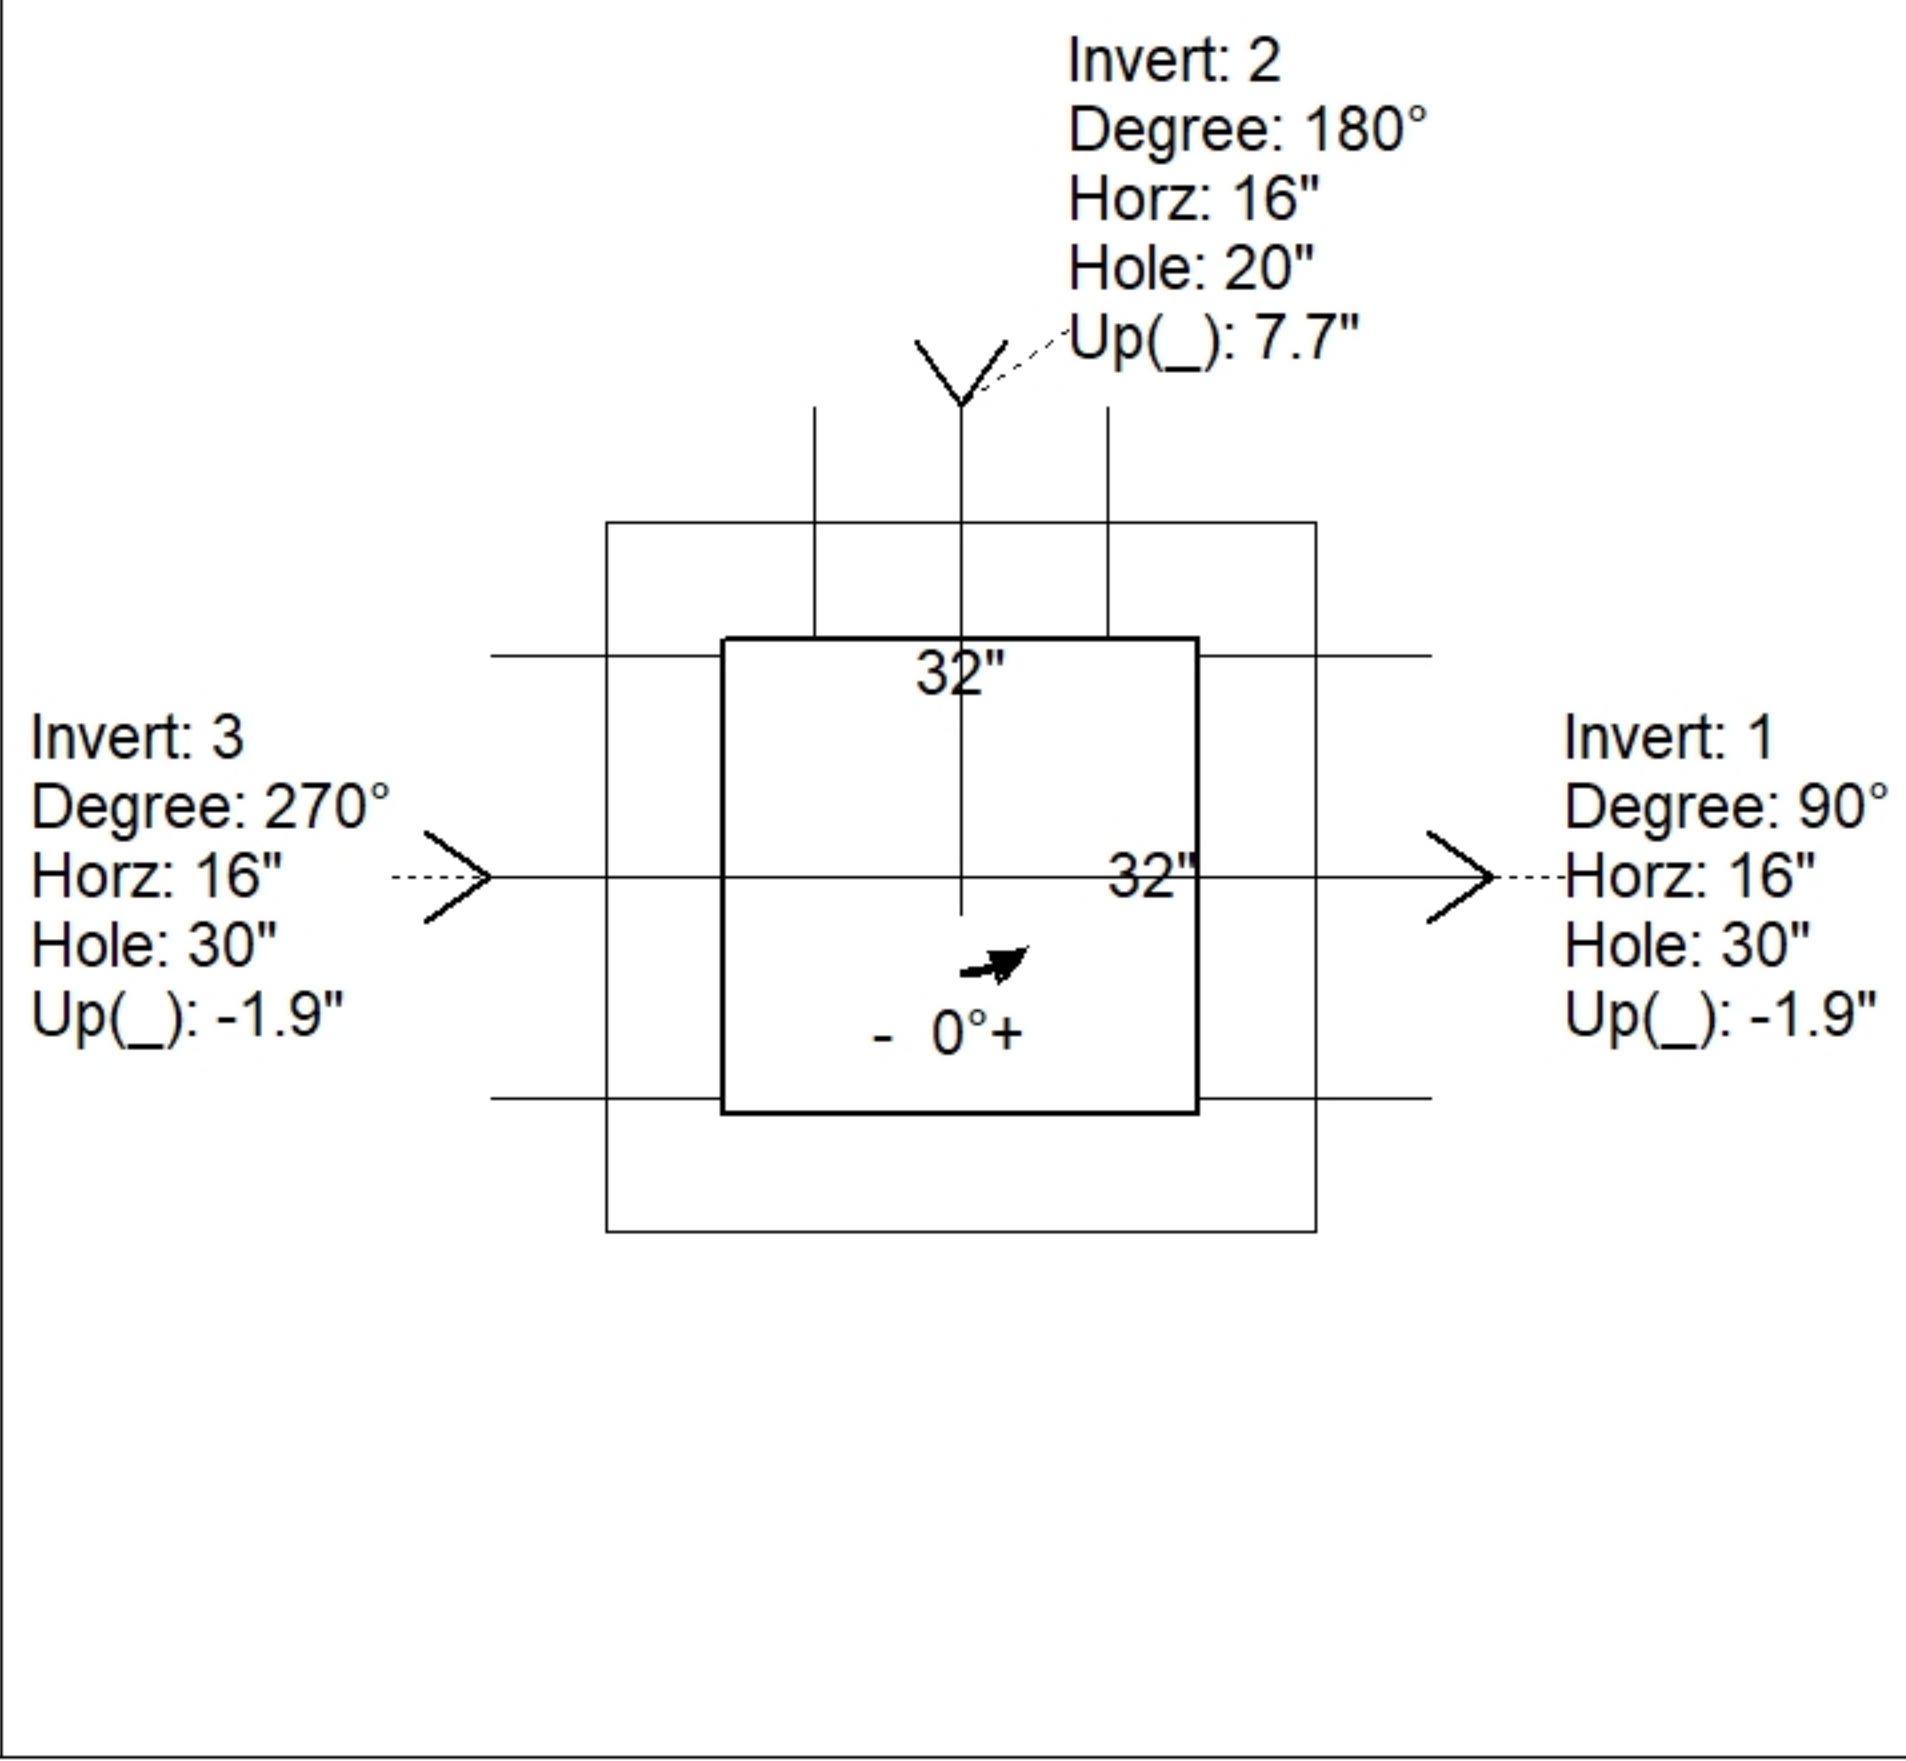
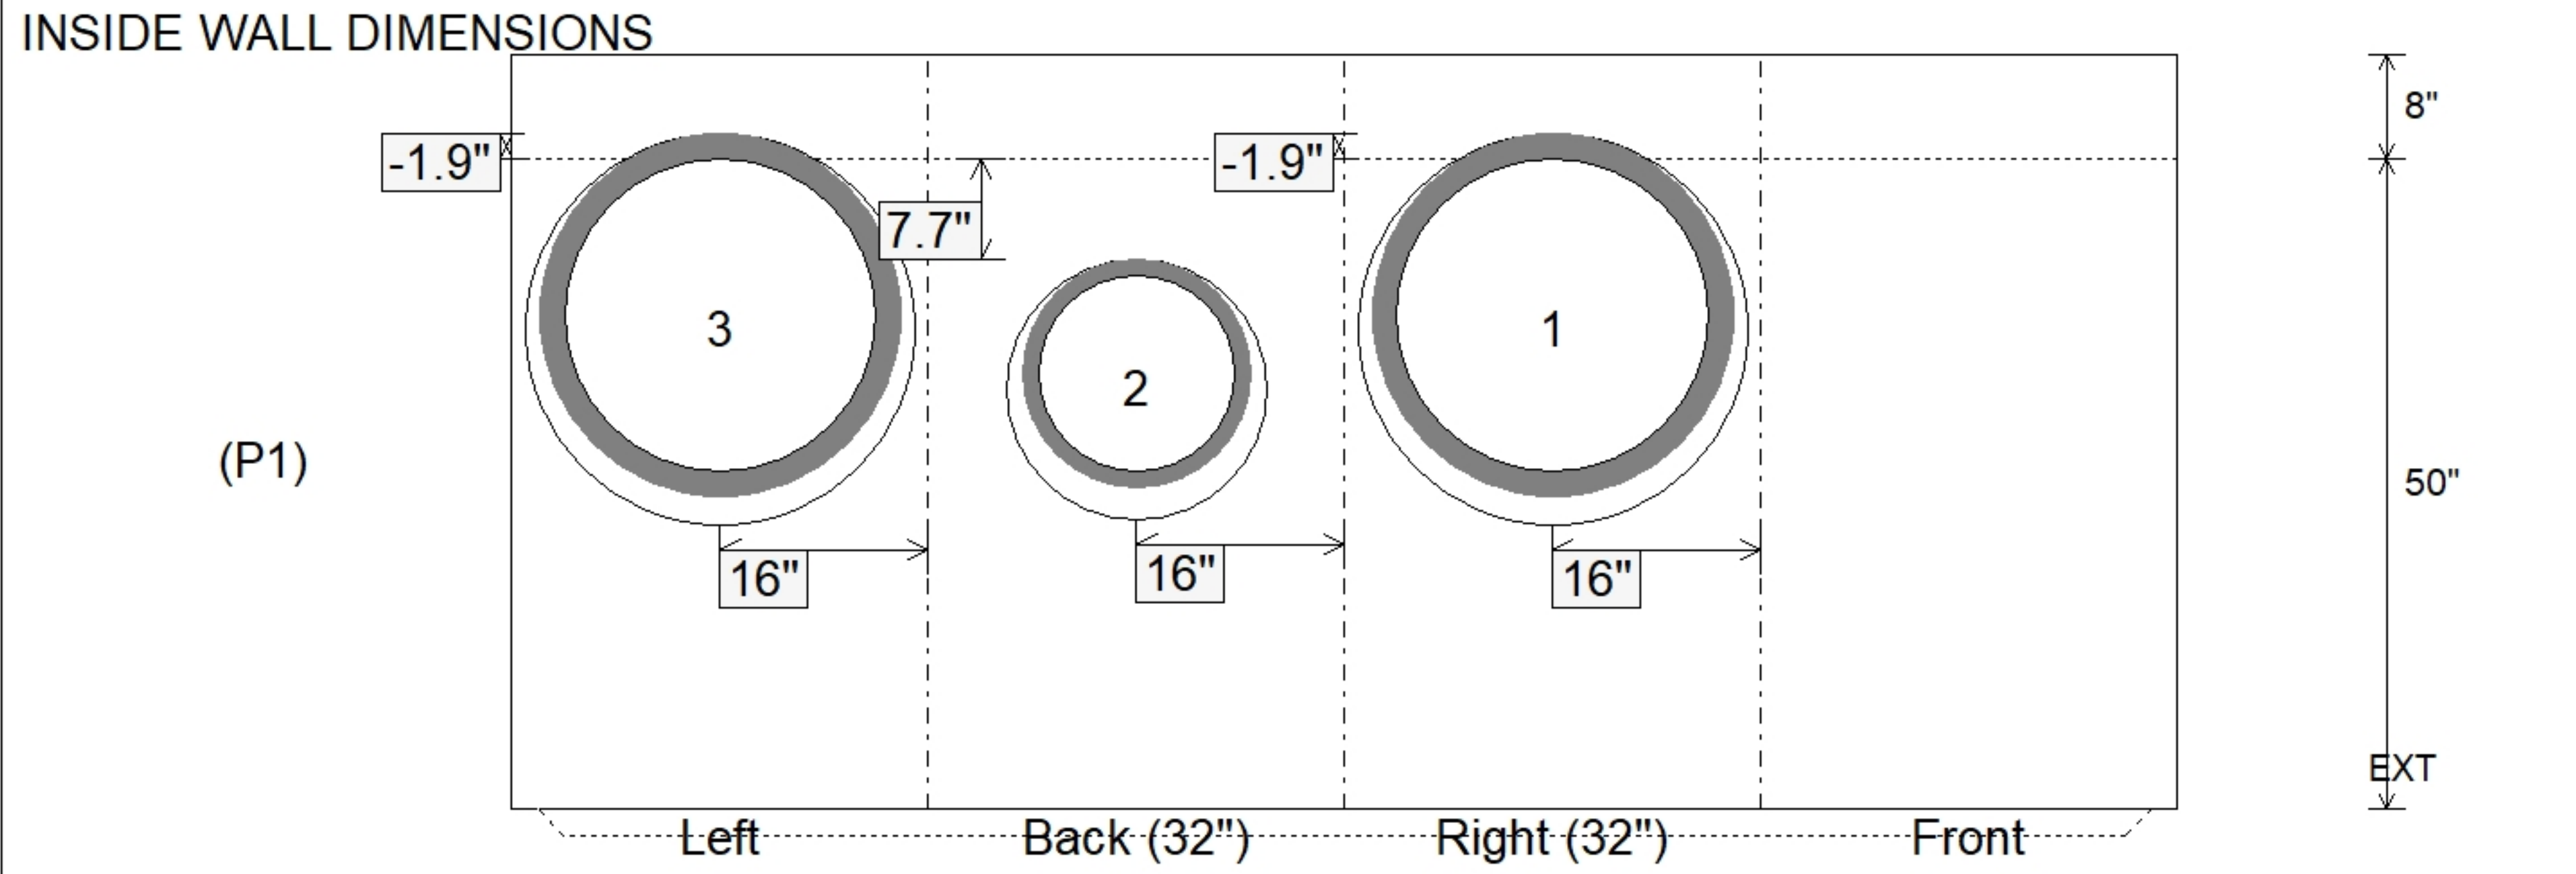


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)				Plant: Beaver Dam		Tech: J. Horsley				
Job Location: Hopkinsville, KY				8/3/2026 4:21:17 PM		PC: C. Goff				
Contractor: Scotty's Contracting & Stone, LLC										
Structure ID: 310 (452+55 RT)										
P1 BX3232-08BAVF				BOX BASE 8inW, 8inF, Variable Ht T/n						
P4) CASTING (cast in) - 0 P3) 32" x 32" - BX FLAT LID 8inW SPEC. (KY JB-B1) F/F - 8" P2) 32" x 32" - BOX RISER 8inW F/G - 24" P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht T/n - 50" 1) CASTING - HOE KY-206 F/C (KY TY1) 2) 32" x 32" - SGL 1"x14.5' Butyl 2) Hole - 30 1) Hole - 20						0 lb 1243 lb 2578 lb 5757 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 9784 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC JUNCTION BOX B1 / PER ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. TOP SLAB w KYTC TYPE 1 F/C CAST FLUSH. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12: C.C.E.W.		
Rim: 527.3' Rim to Invert: 6.86' Slack: 0.32" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	520.44'	90°	24"	24" HDPE	27.8"	Hole 30	30"	30"	-1.9"	0"
Invert 2	521.19'	180°	24"	15" HDPE	17.6"	Hole 20	20"	20"	7.7"	0"
Invert 3	520.44'	270°	24"	24" HDPE	27.8"	Hole 30	30"	30"	-1.9"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 										
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 50" Height (Ext): 58"		Weight (Net): 5757 lb Volume (Net): 1.47cu.yd	
