

Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.




Slack: 0"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- FRAME & GRATES BY OTHERS.
- KYTC CERTIFICATIONS REQUIRED.
- #5 BAR EXTENDED OUT OF TOP OF BOX 20" AT 12" C/C.

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 28"
1) 36" x 36" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 30"x28"

0 lb
4580 lb
0 lb
0 lb



Structure Total: 4580 lb

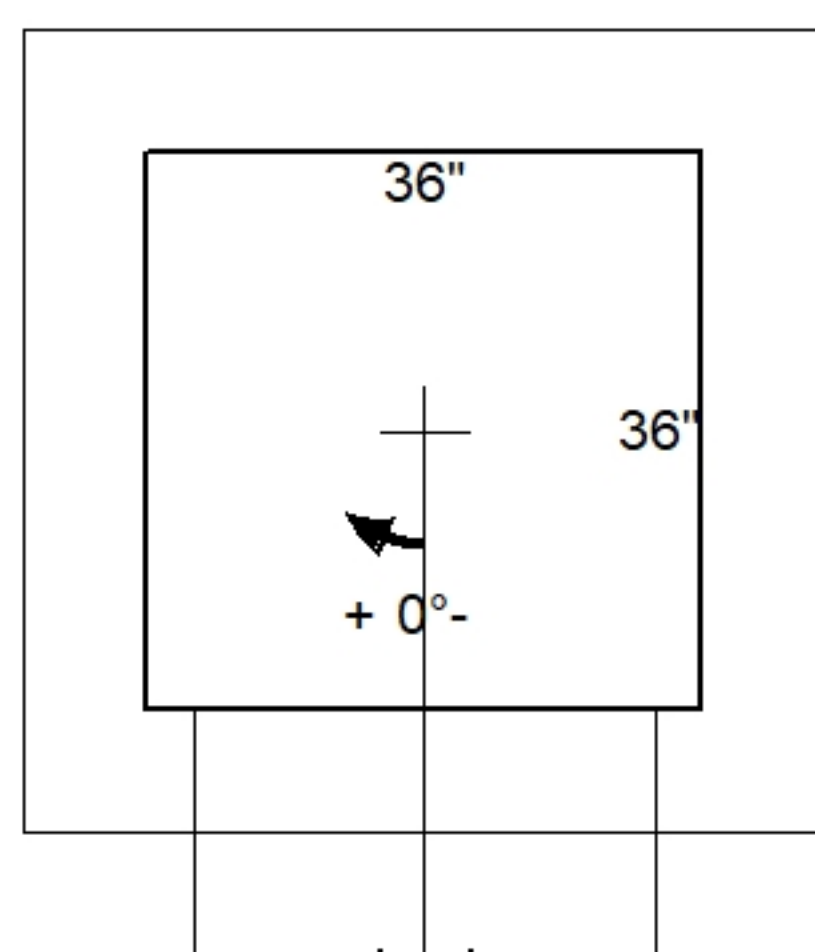

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	561.87'							
Reducer								
Invert 1	558.87'	0°	24" CMP	25"	30" x 28"	DOGHOUSE INVRTD 30"x28"	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

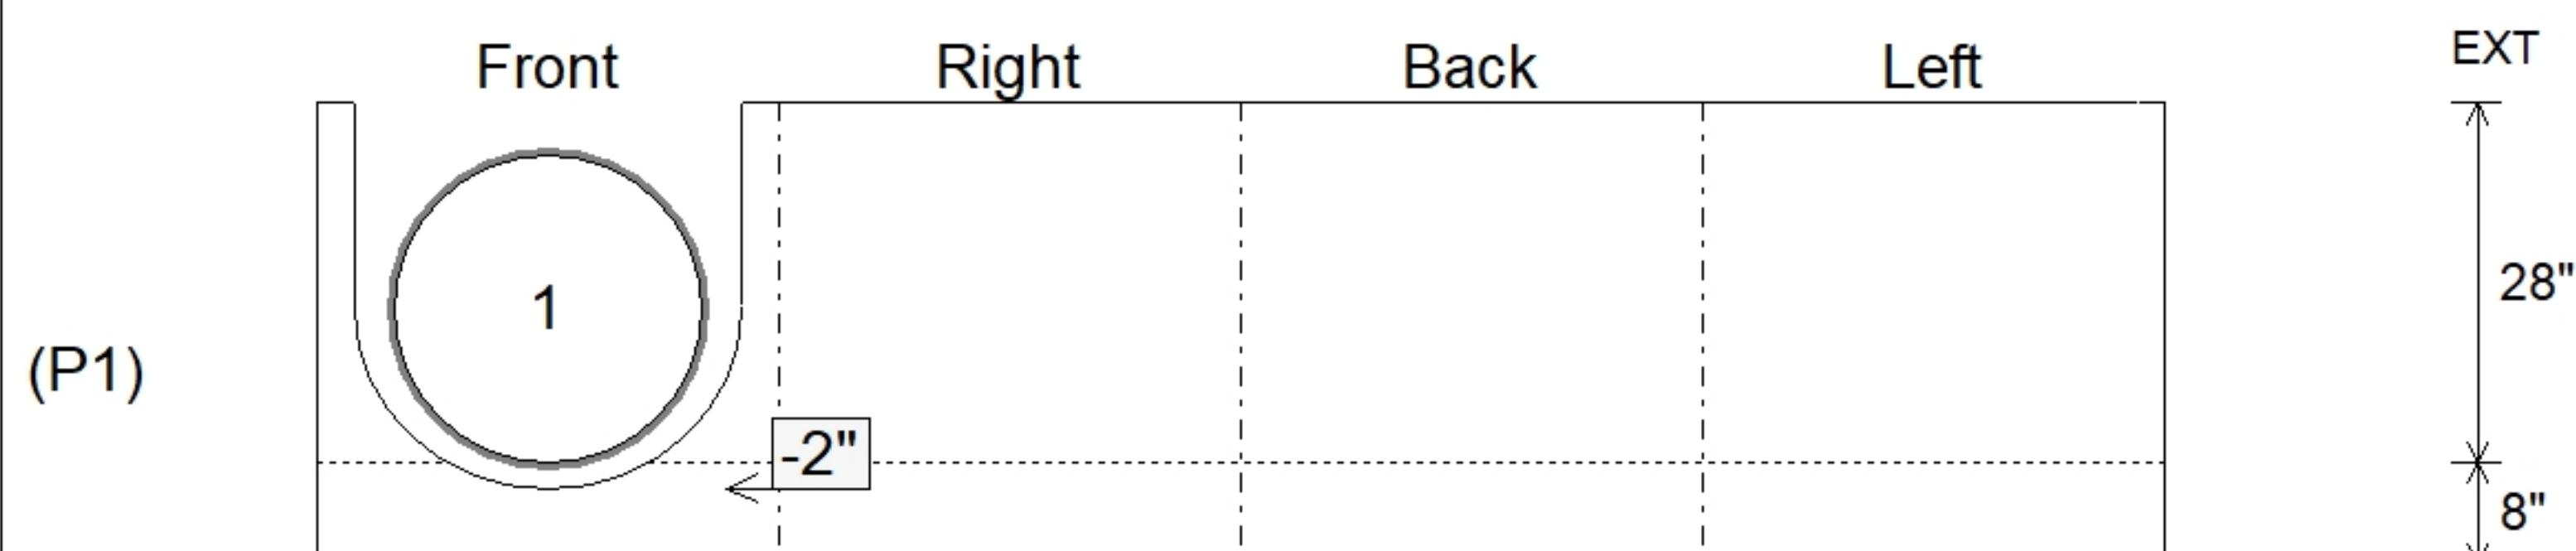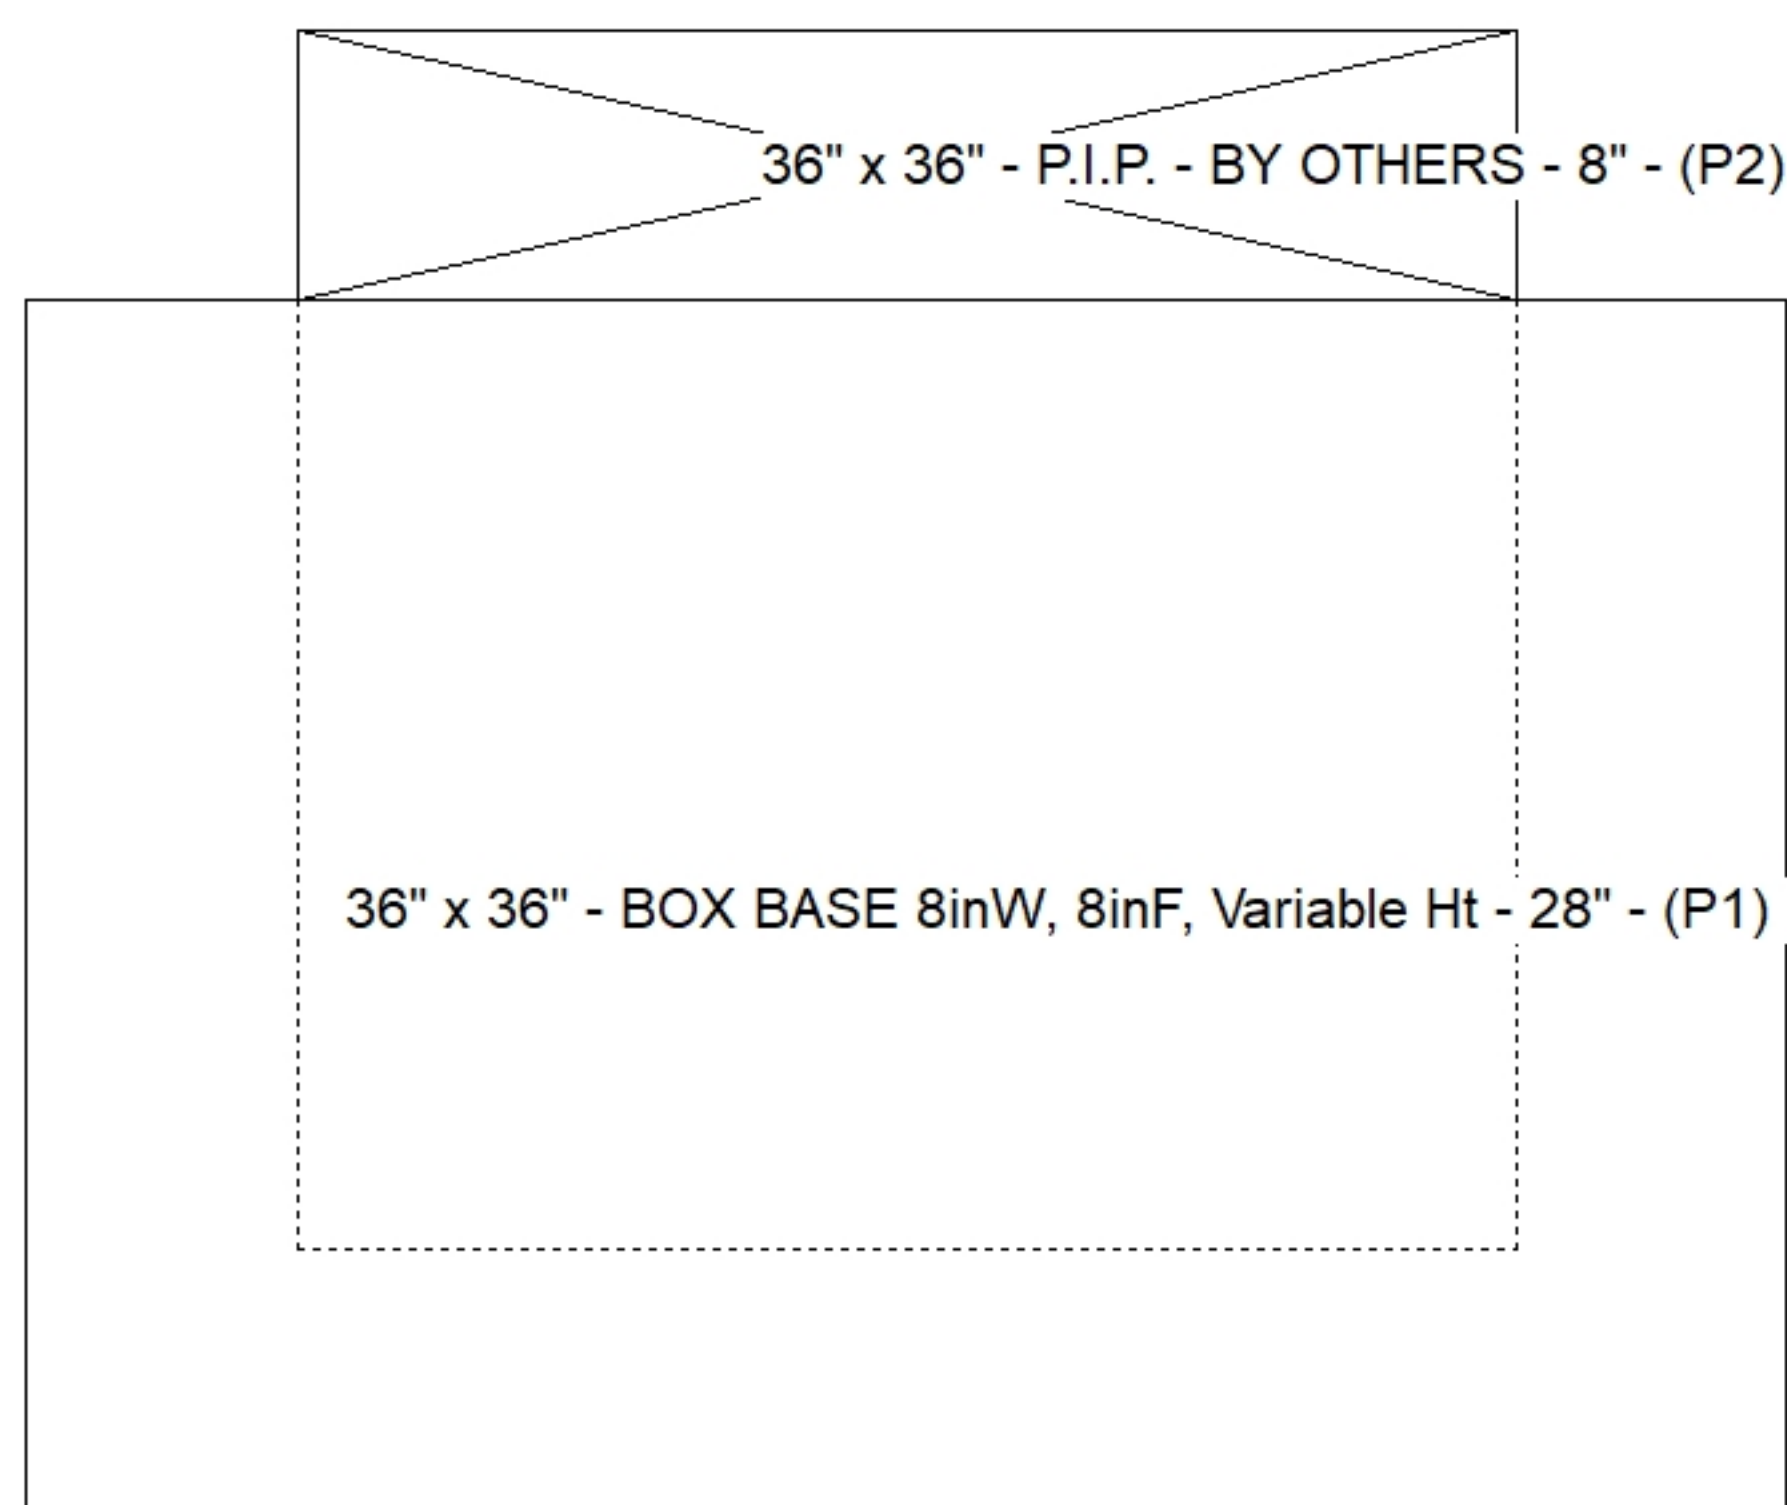

Submittal Drawing
7/22/2026 9:17:59 AM

SUBMITTAL
APPROVED BY:
