

Contractor: Cleary Construction, Inc.


Plant: Beaver Dam, Ky.



Slack: 1.12"



- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

Structure Total: 3529 lb

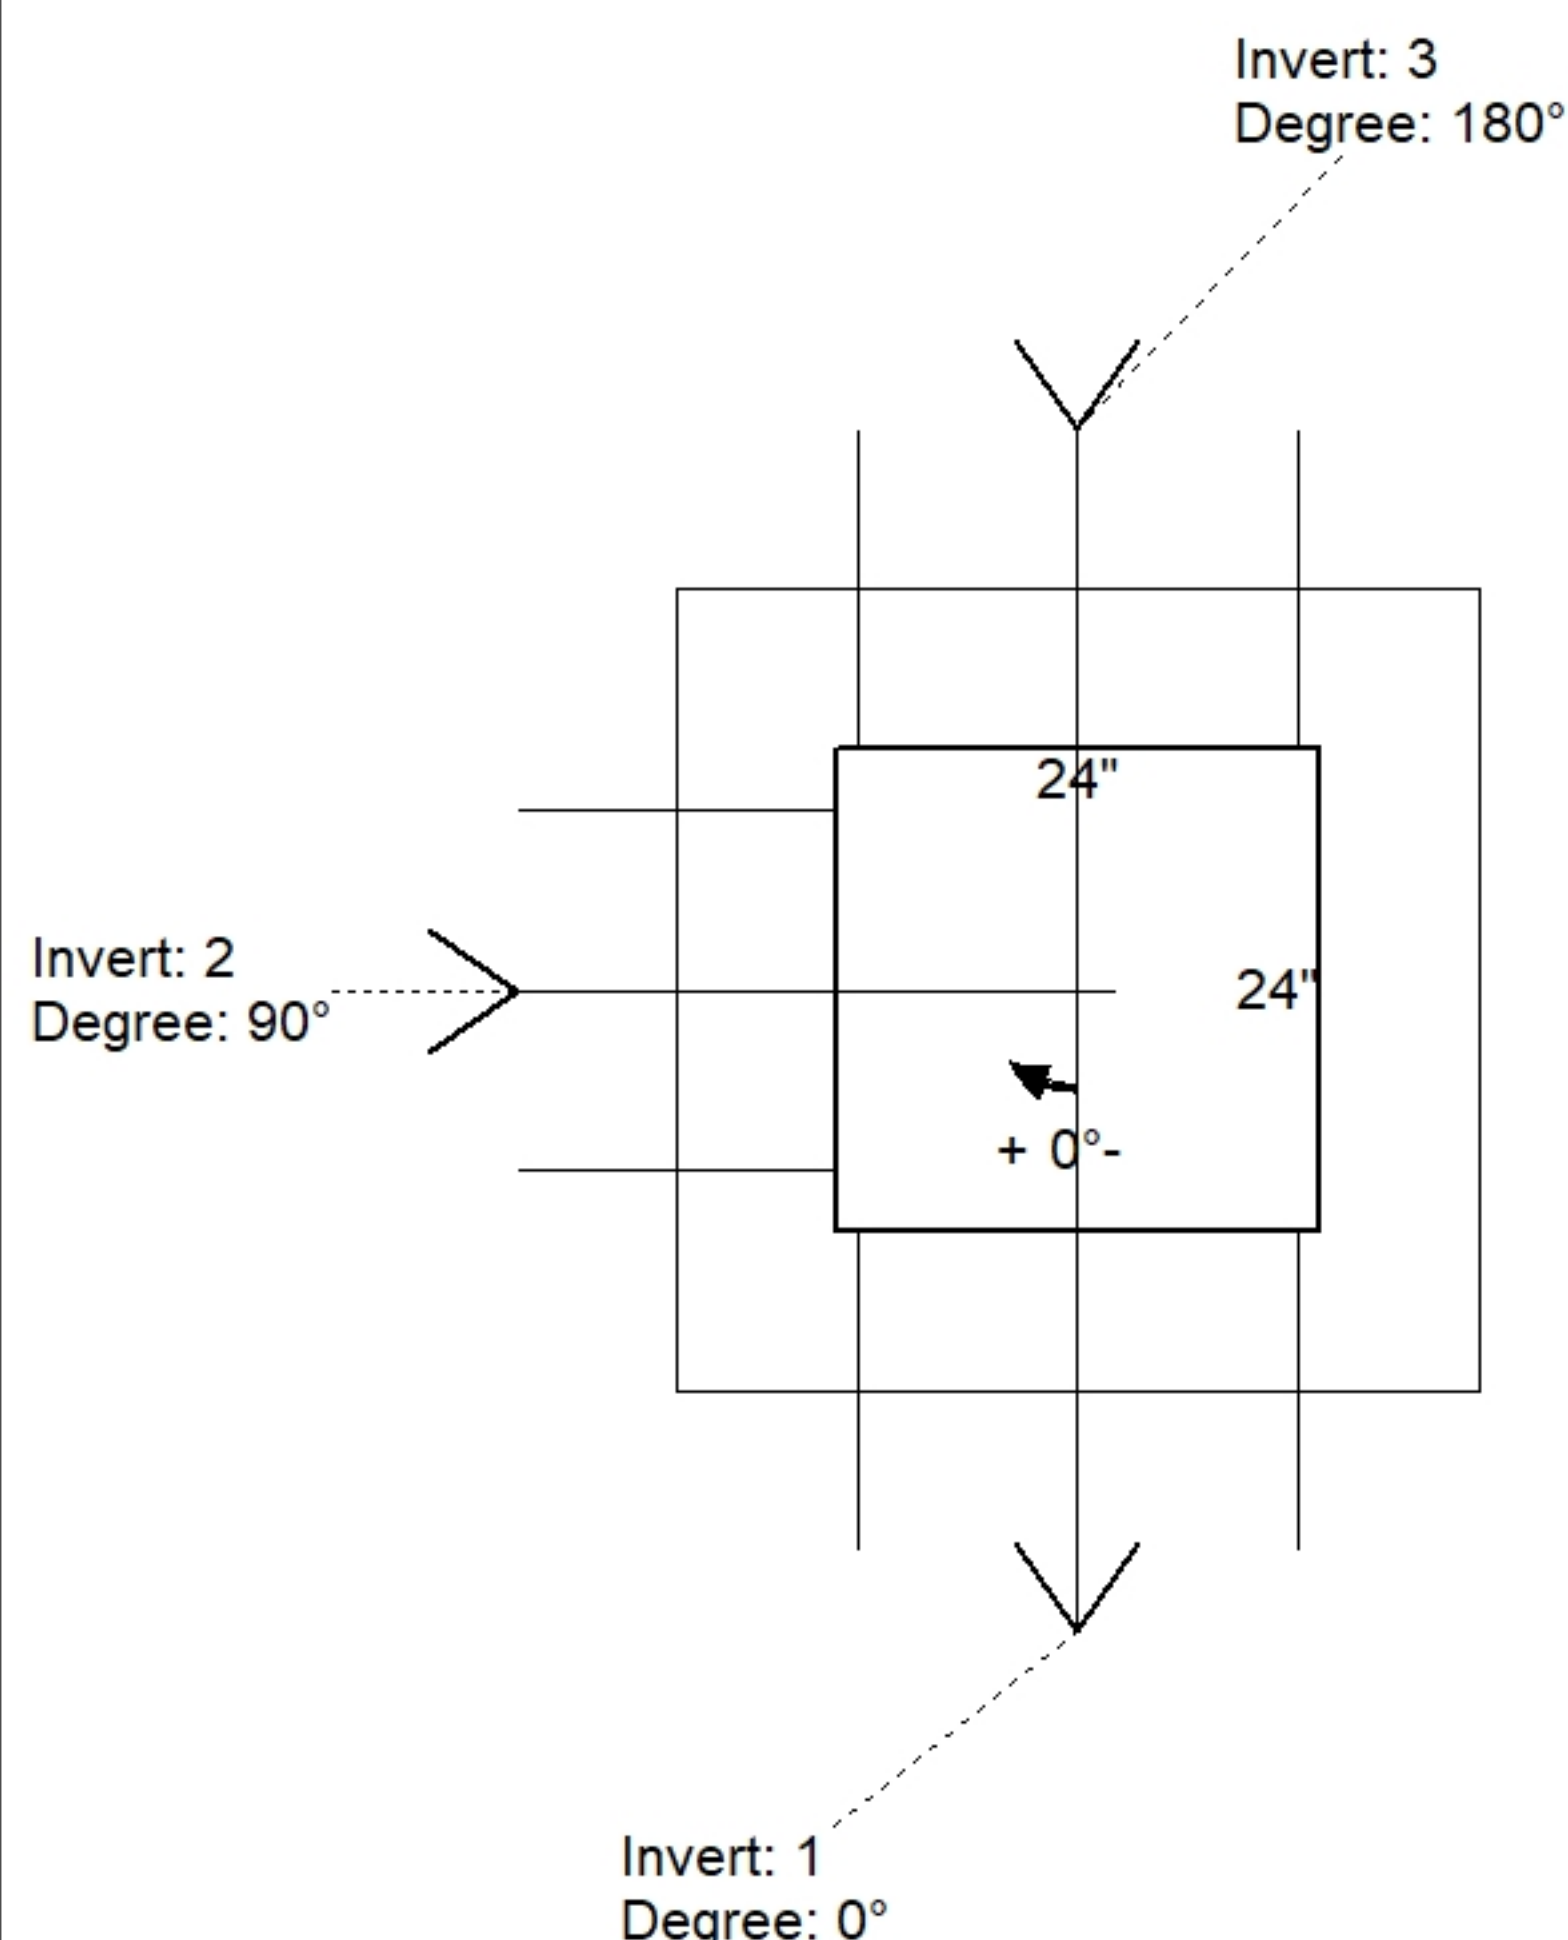

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	556'							
Reducer								
Invert 1	553.24'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	553.24'	90°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3	553.24'	180°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

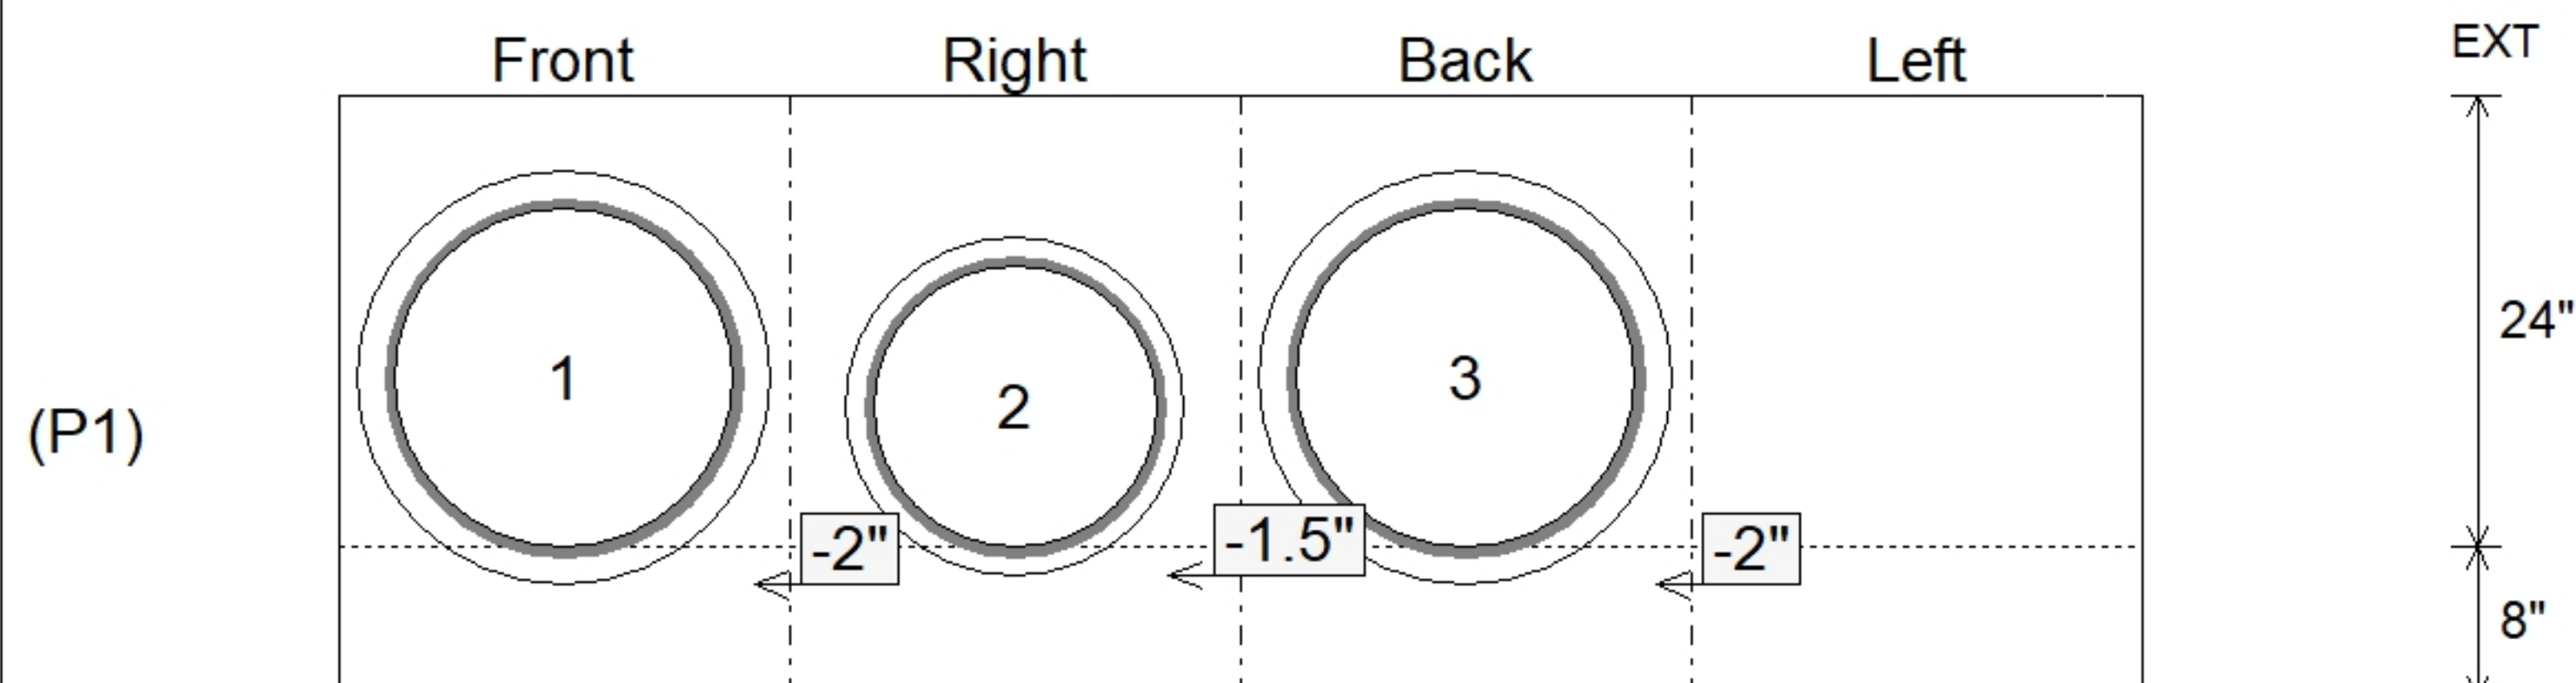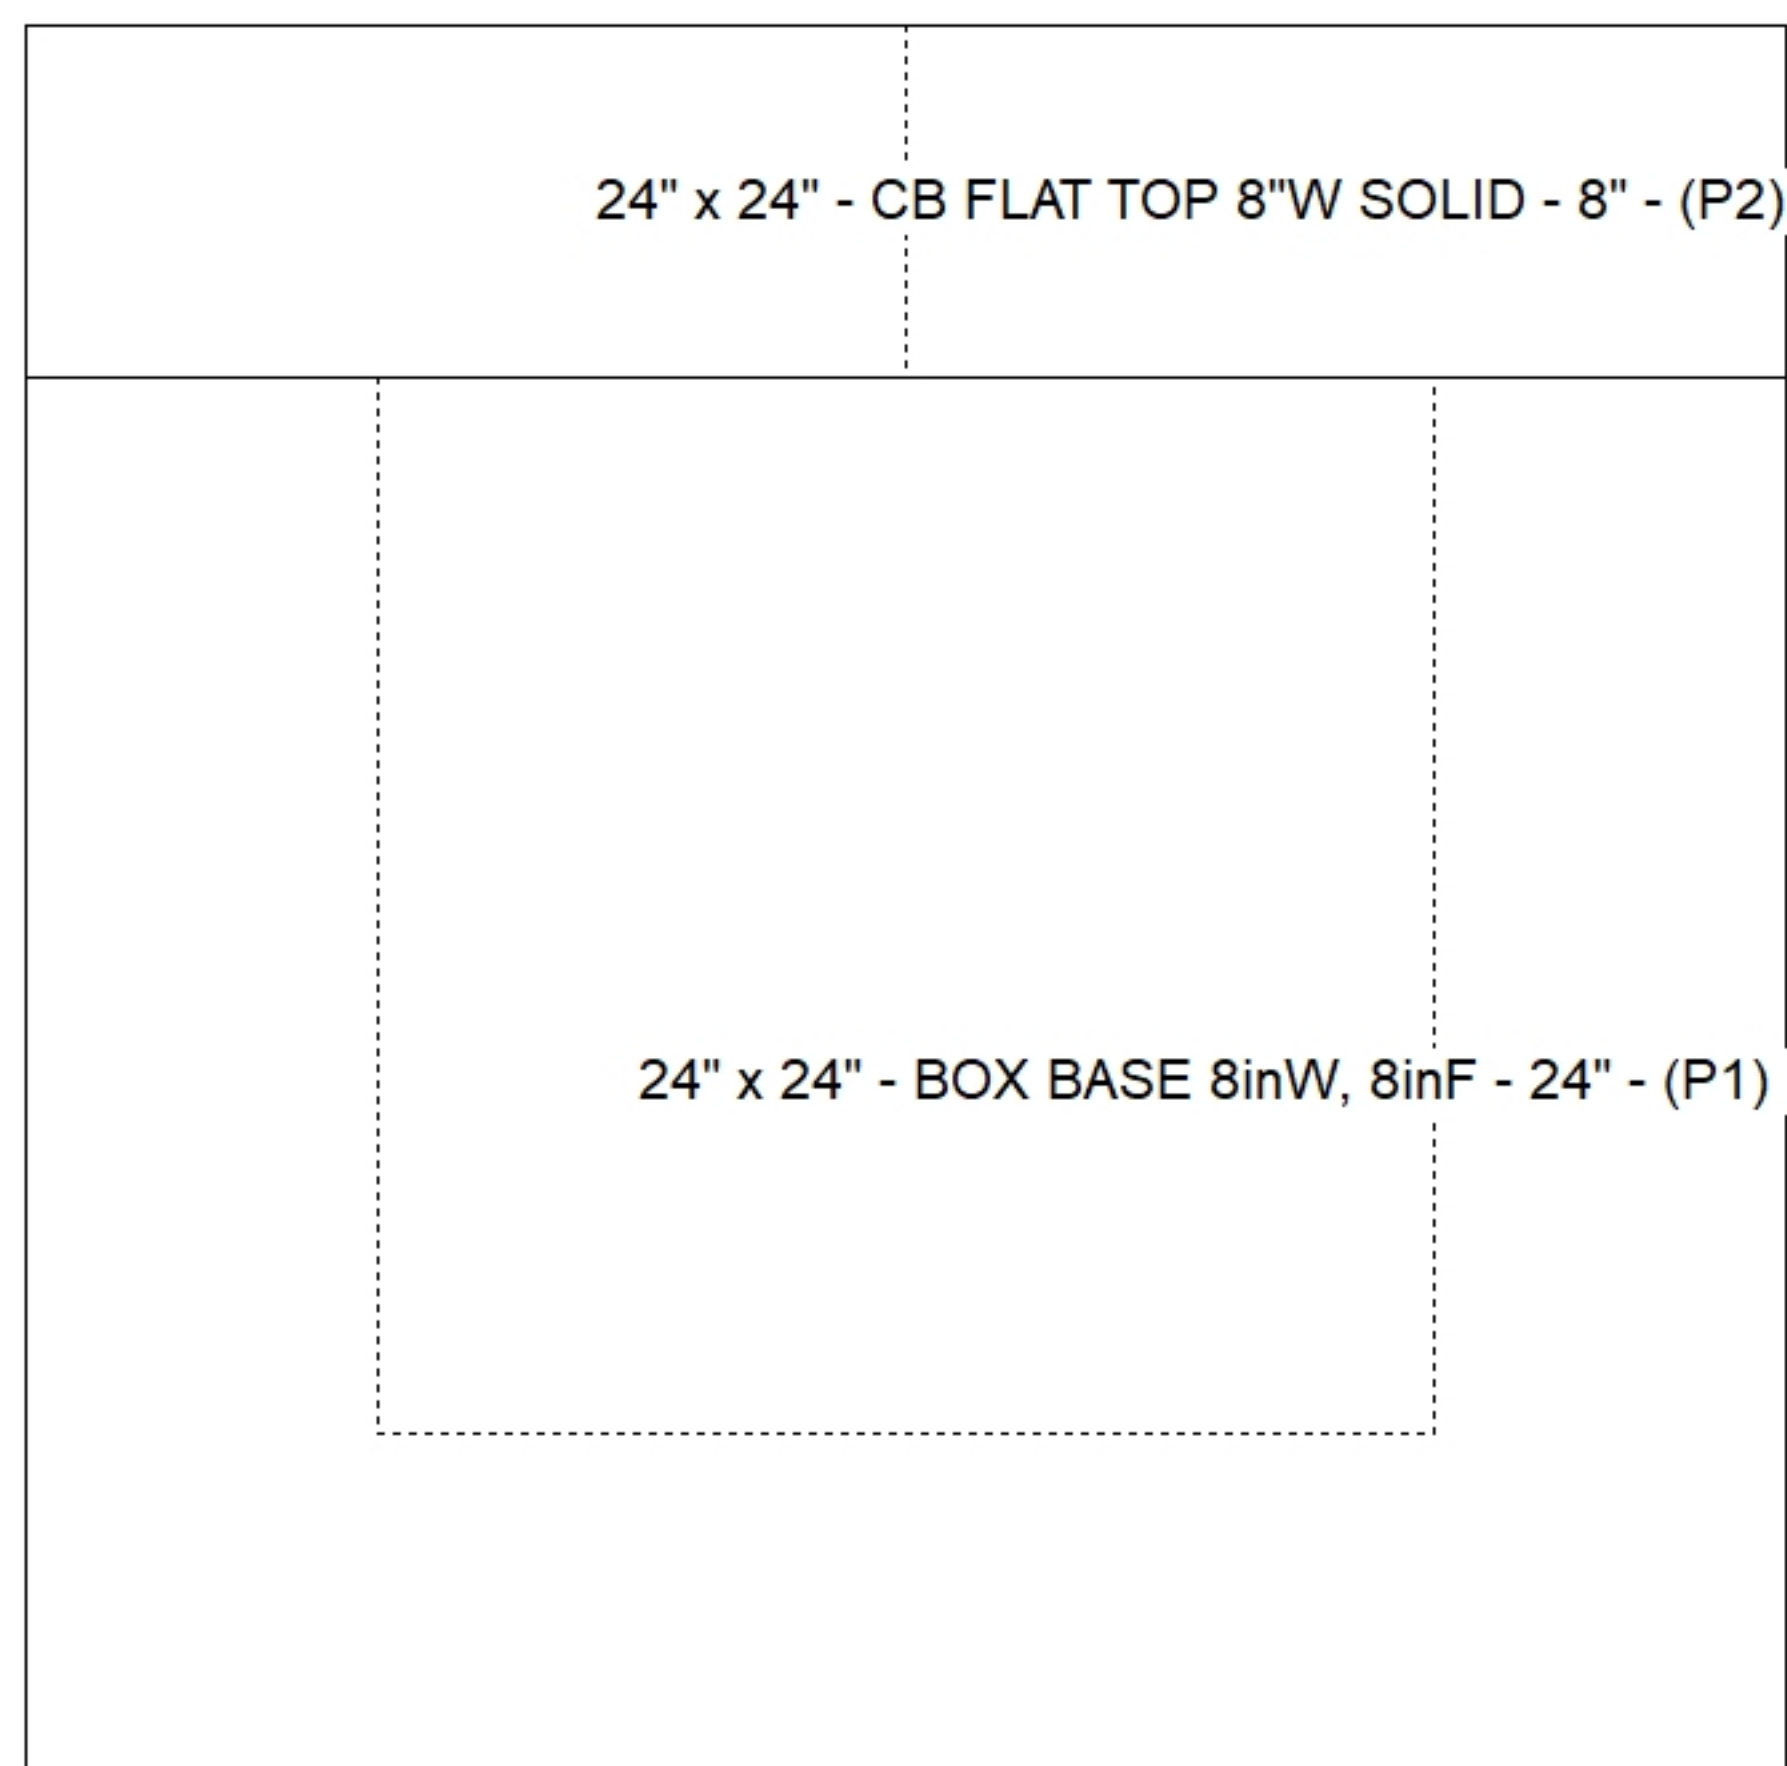

SUBMITTAL
APPROVED BY:
