

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, KY	




Slack: 0"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.
- #5 BAR EXTENDED OUT OF TOP OF BOX 20" AT 12" C/C.


P2) 36" x 48" - P.I.P. - BY OTHERS - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 46"
1) 36" x 48" - Conseal CS-102 1.00"
2) Hole - 40

0 lb
6934 lb
0 lb
0 lb


Structure Total: 6934 lb

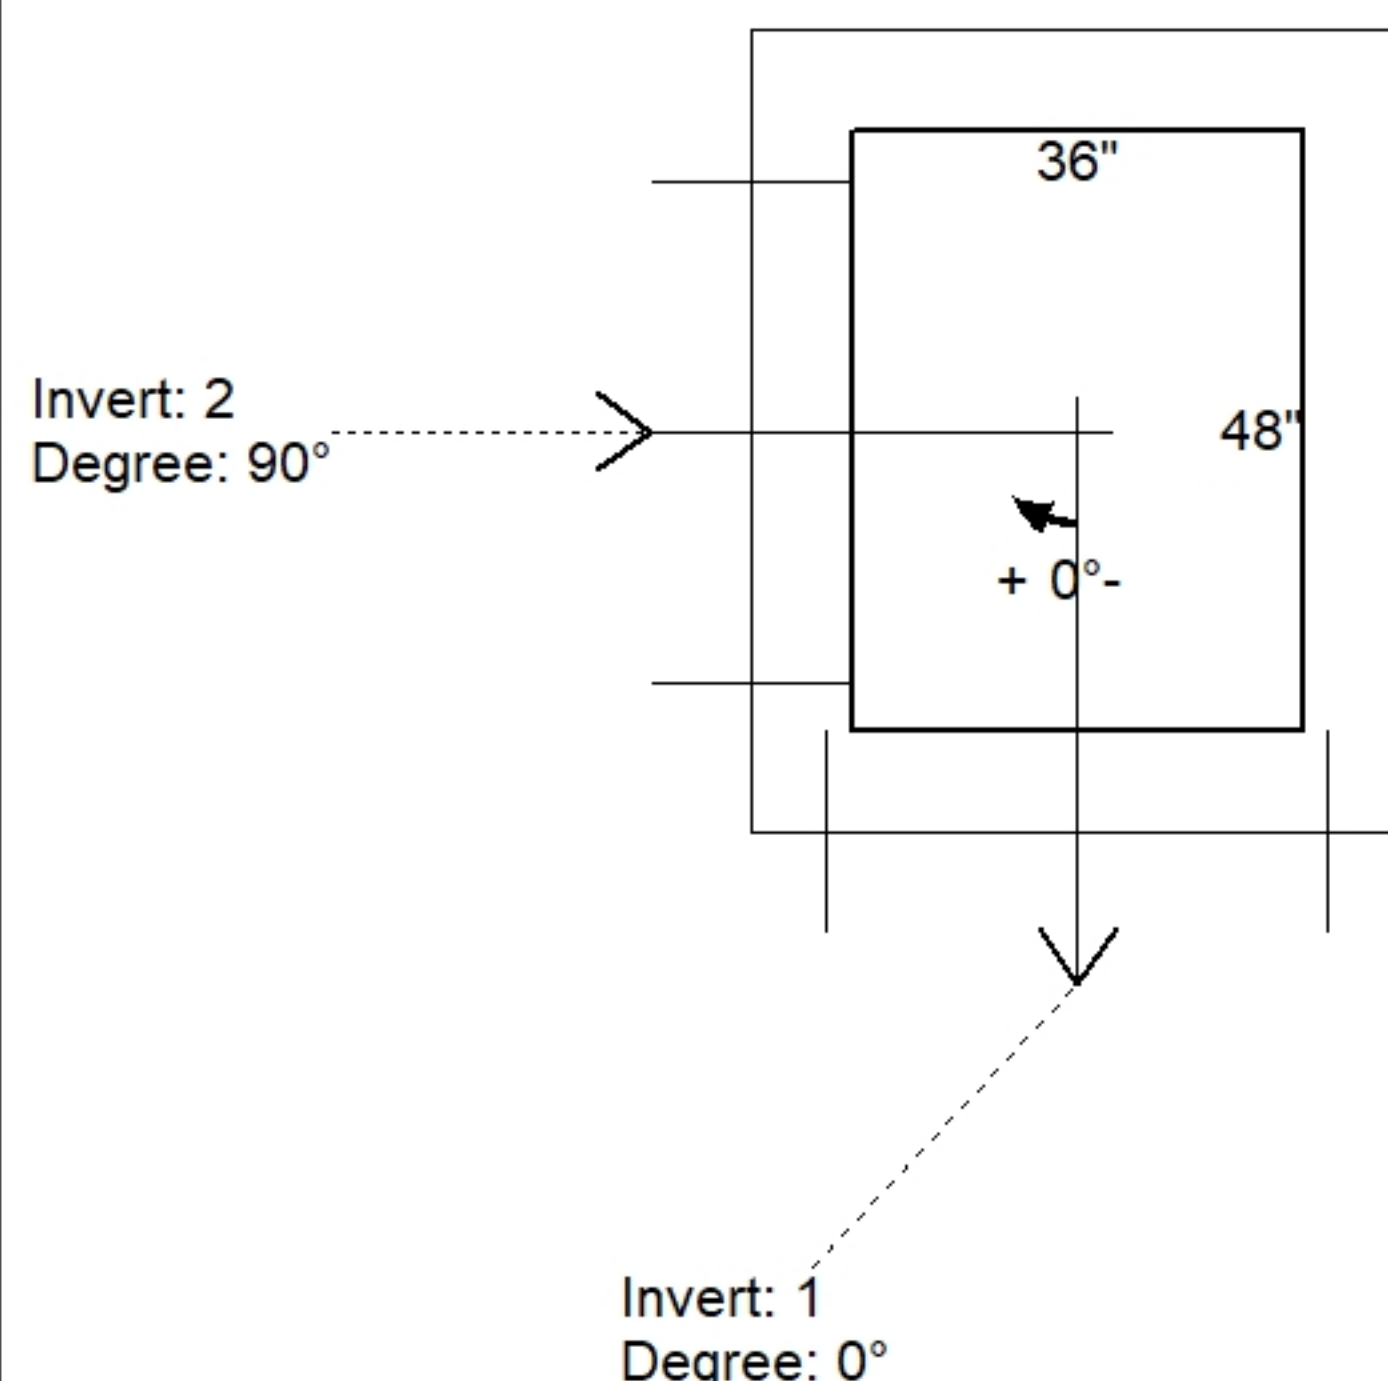

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	556.86'							
Reducer								
Invert 1	552.36'	0°	36" CMP	37"	40"	Hole 40	-2"	P1
Invert 2	552.36'	90°	36" CMP	37"	40"	Hole 40	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

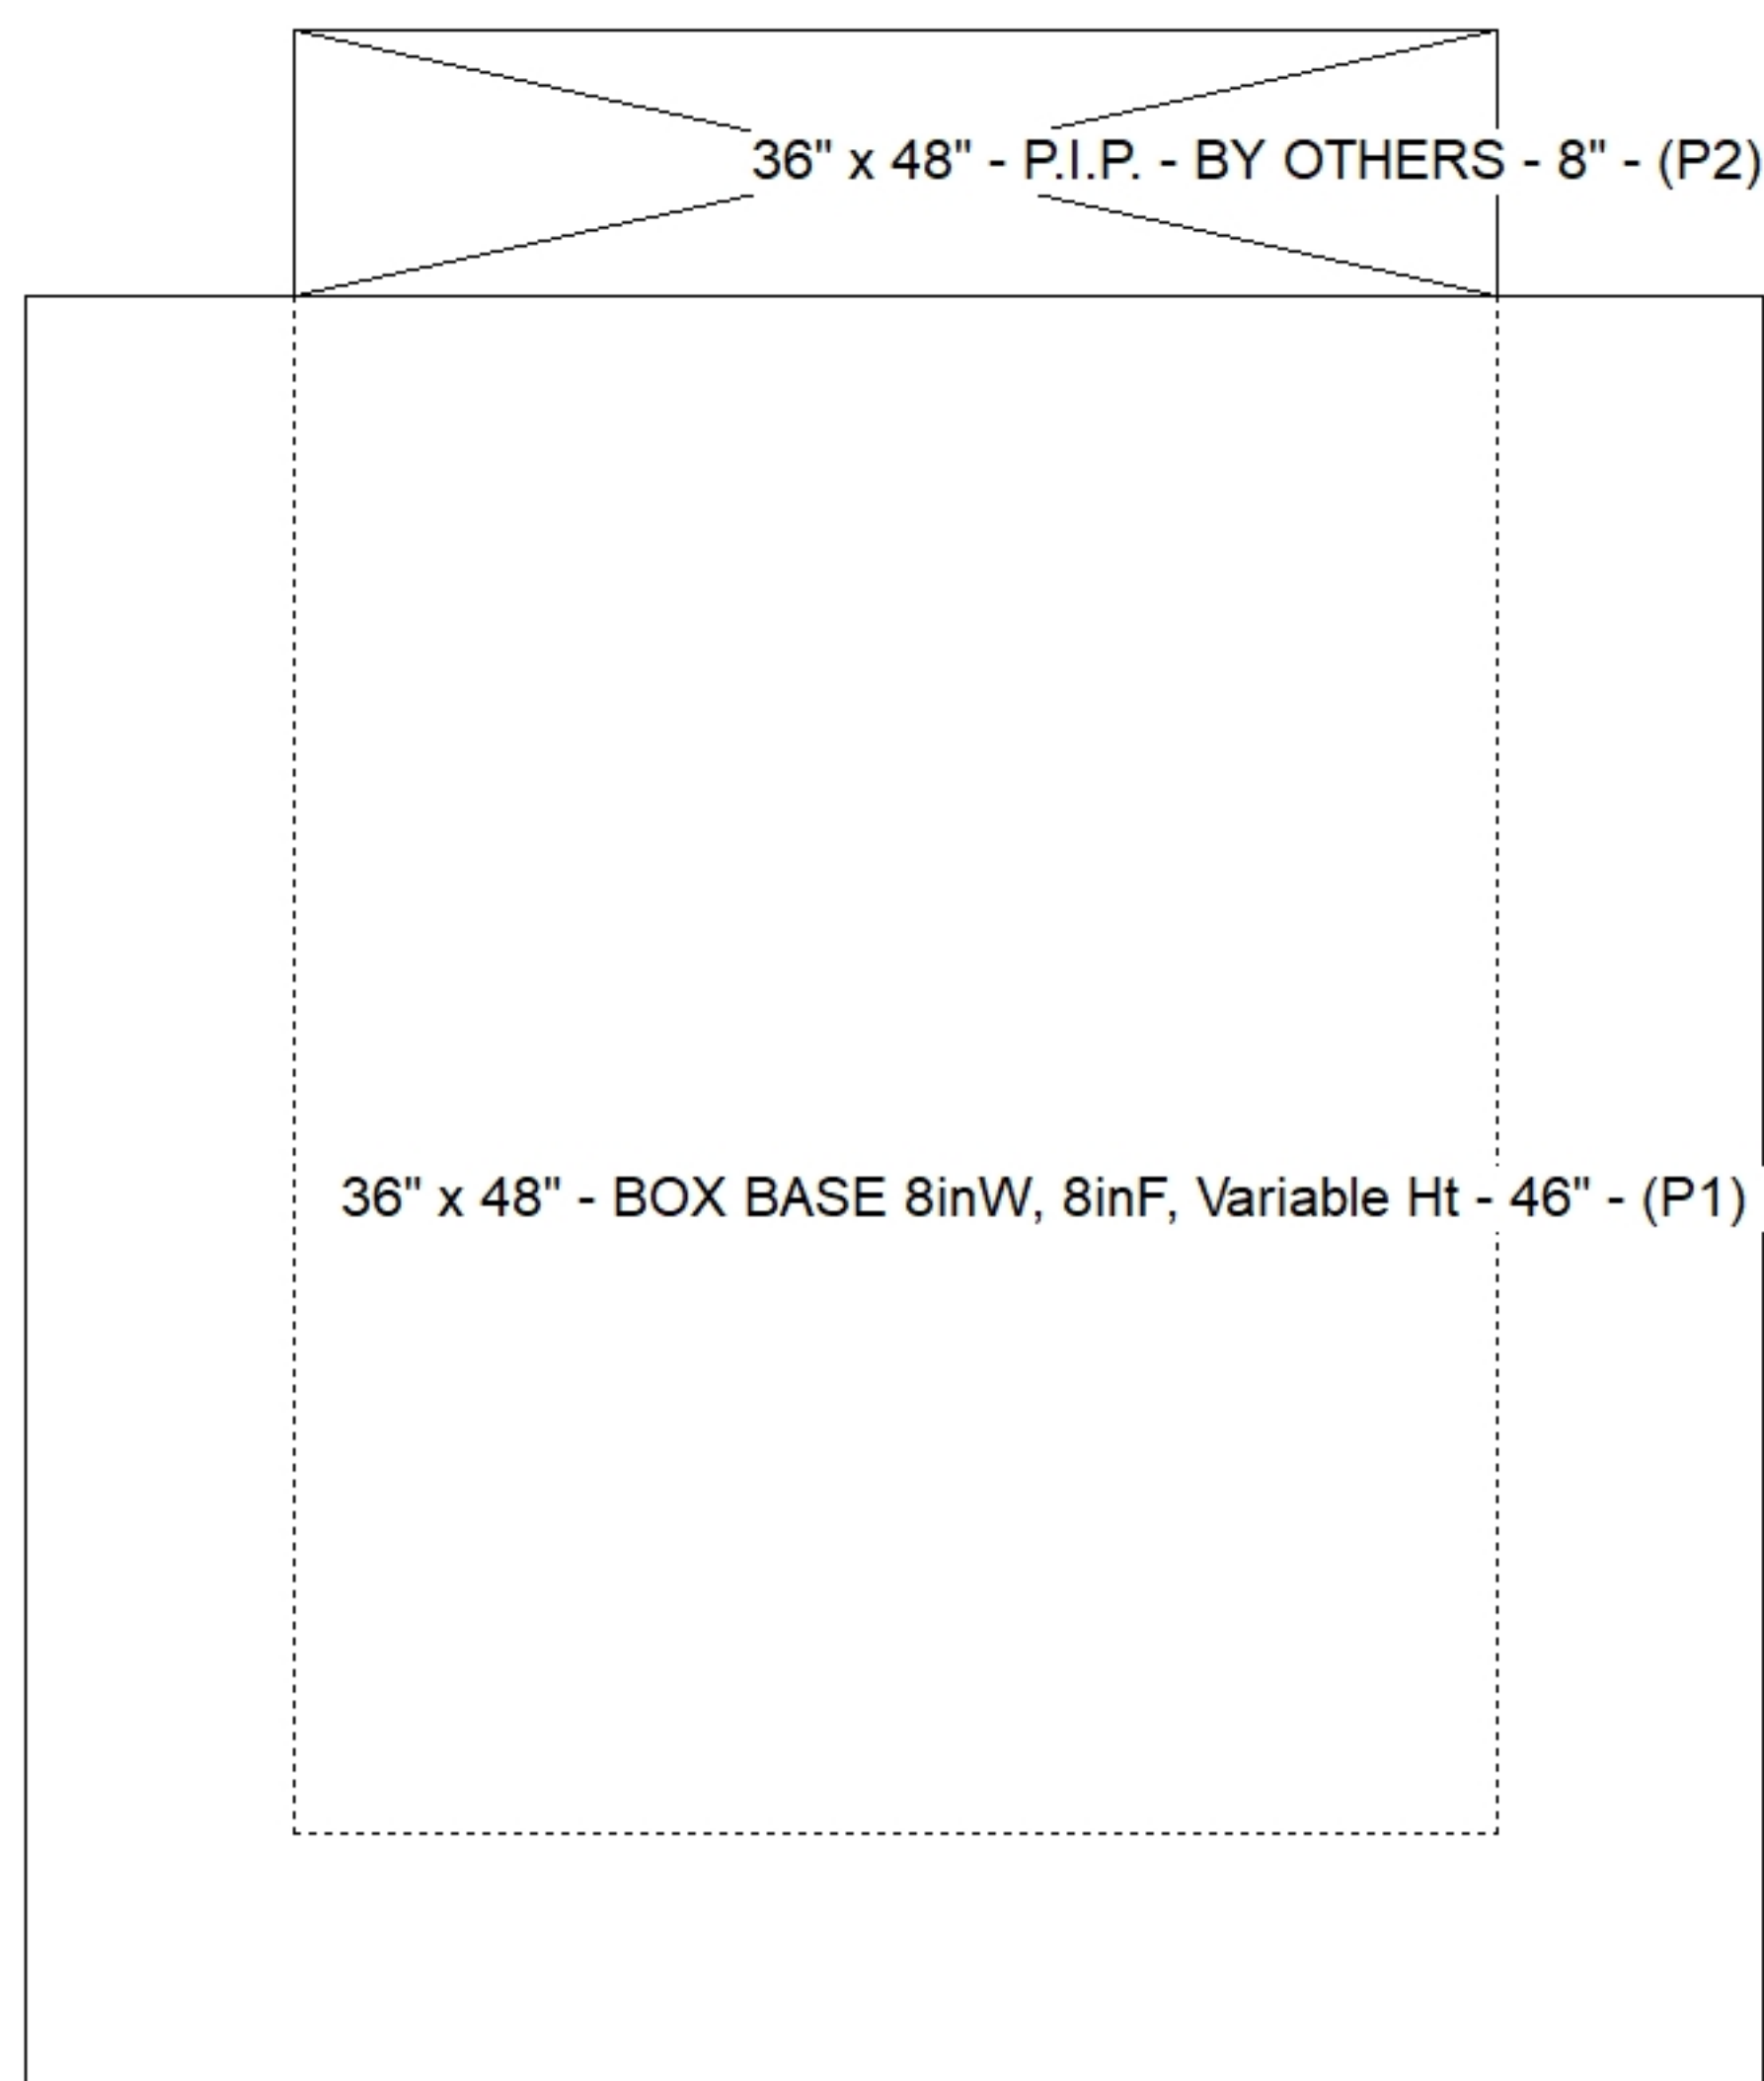

Default - Interior Dimensions

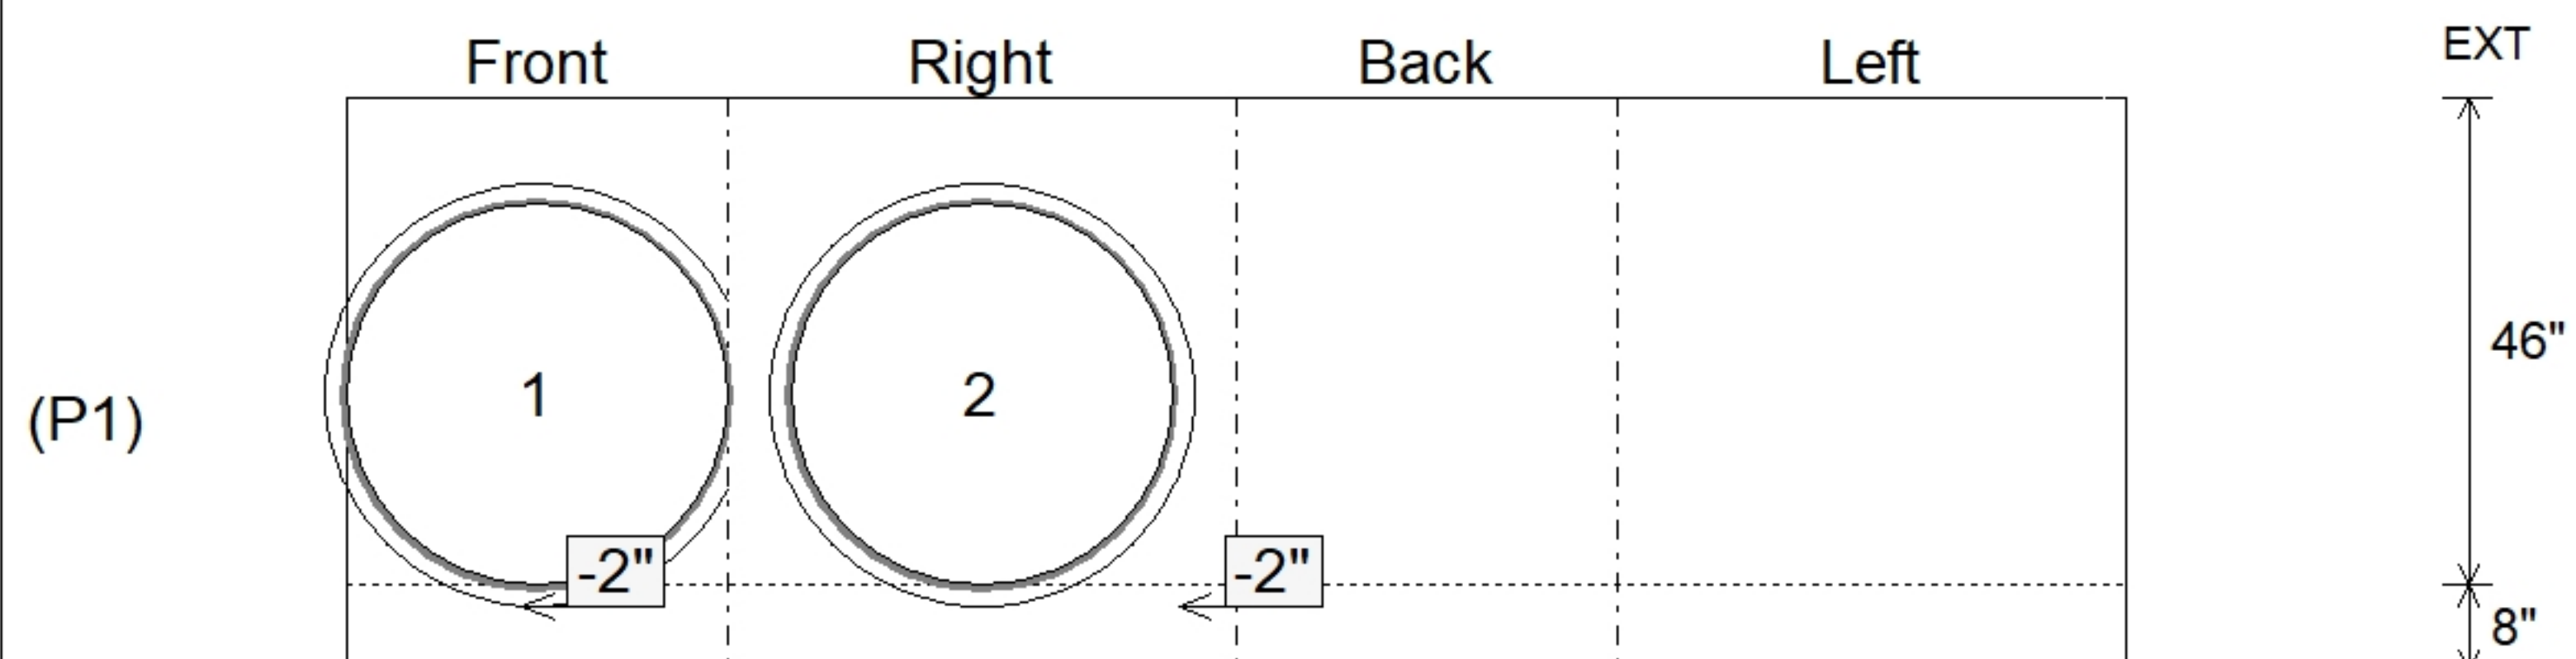

Submittal Drawing
8/10/2026 11:02:38 AM

SUBMITTAL
APPROVED BY:
