

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, KY	




Slack: 4"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICST).
- KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22
1) Hole - 26


0 lb
4000 lb
4241 lb
0 lb
0 lb
0 lb

Structure Total: 8241 lb

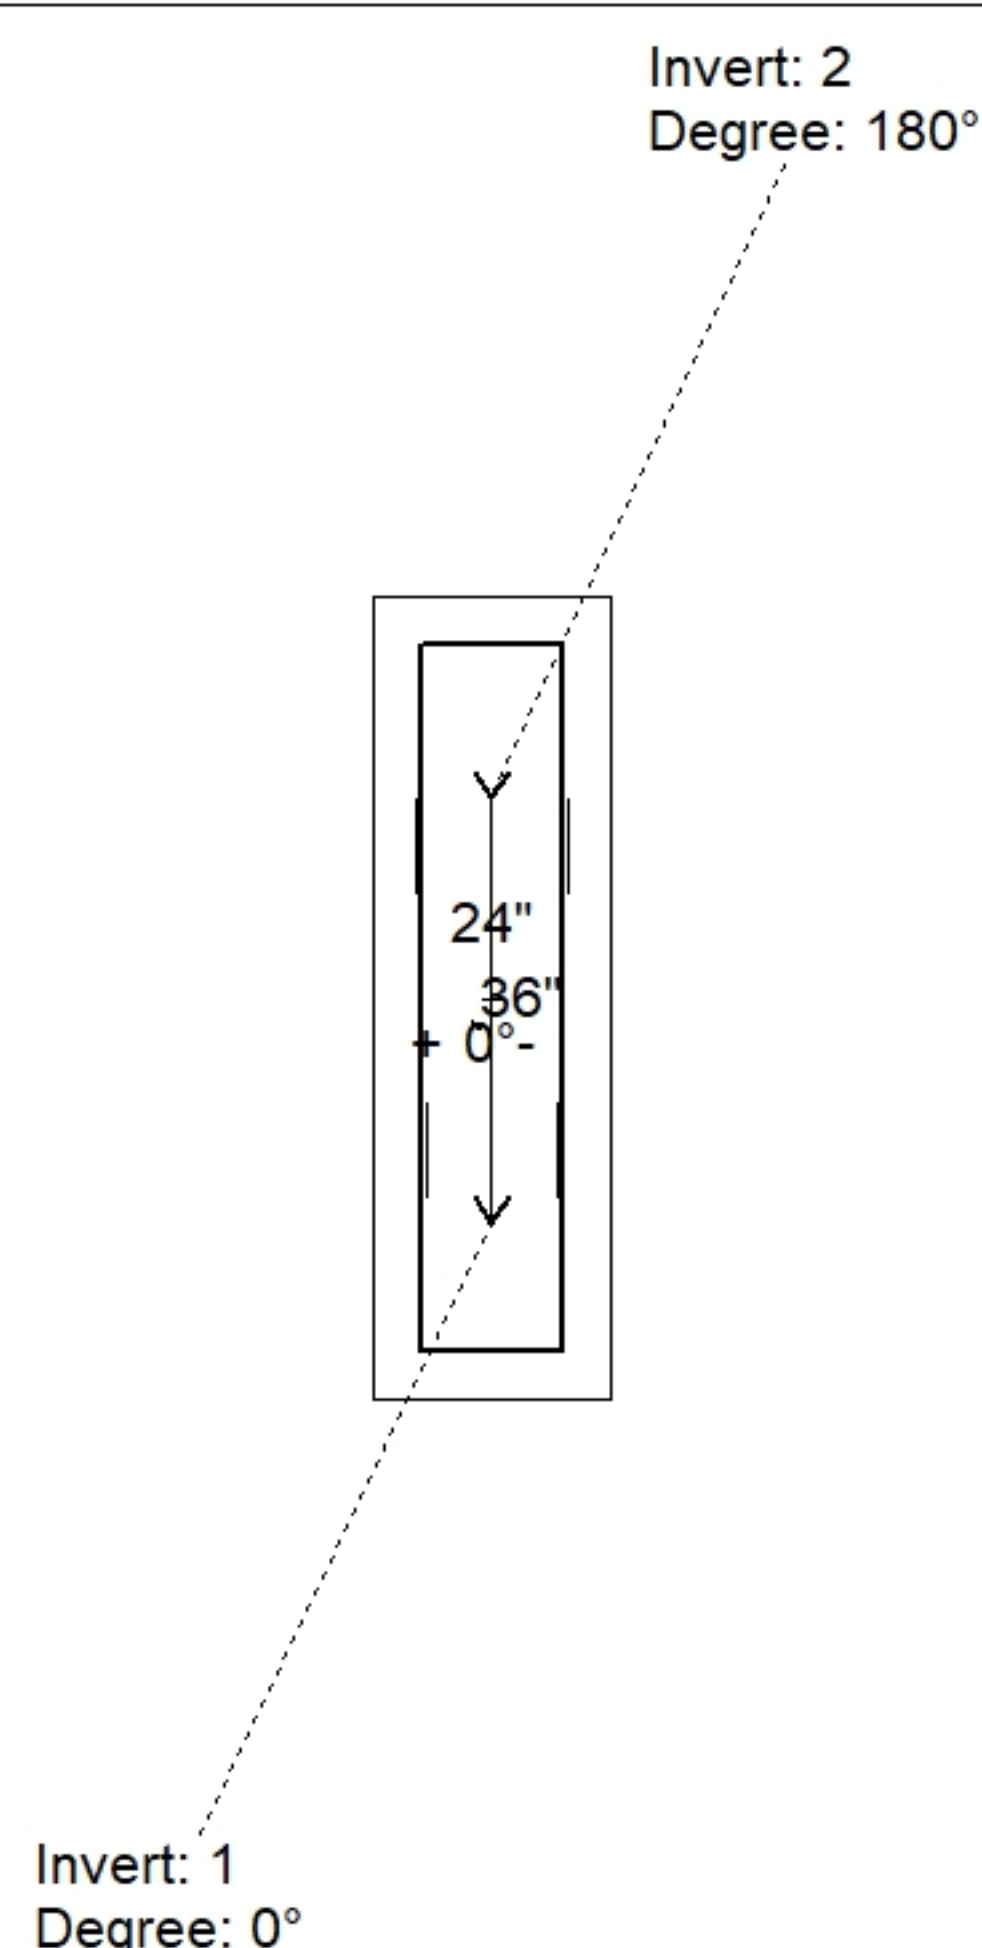

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	572.36'							
Reducer								
Invert 1	567.86'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	567.86'	180°	18" RCP B WALL	23"	26"	Hole 26	-4"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

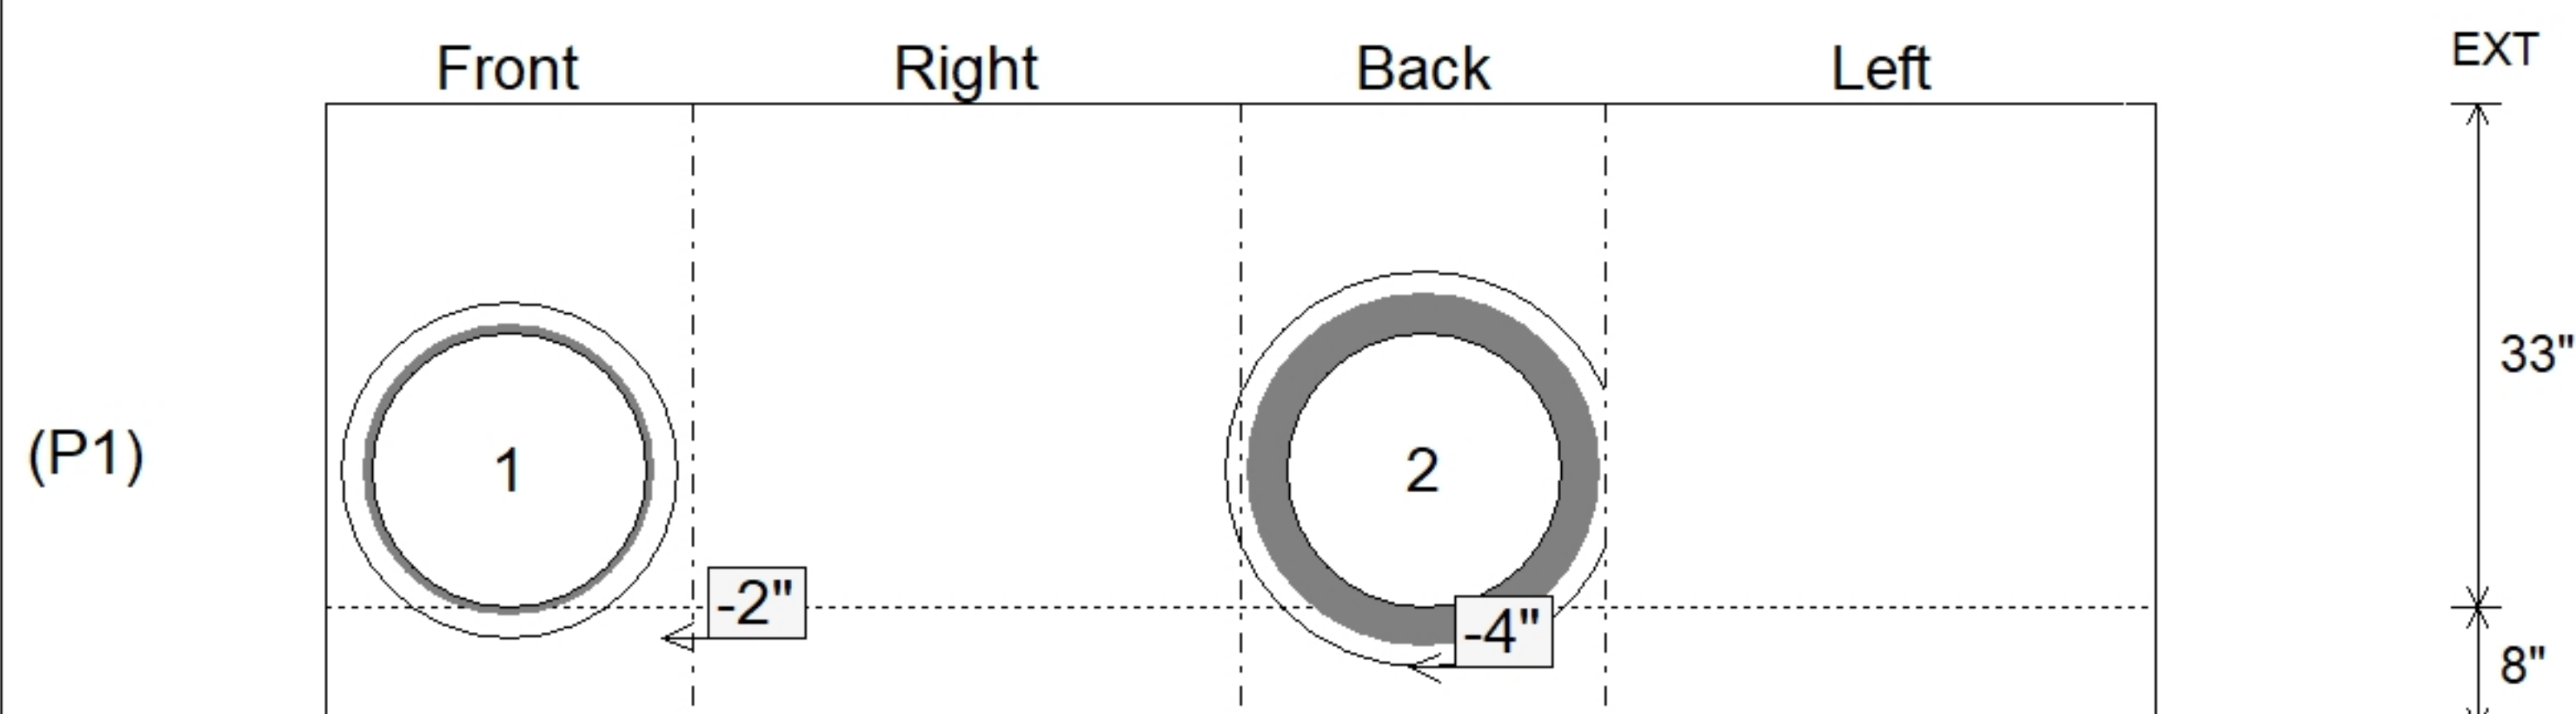

Submittal Drawing
8/10/2026 11:02:40 AM

SUBMITTAL
APPROVED BY:
