

**Contractor: Cleary Construction, Inc.**

|                        |            |
|------------------------|------------|
| PC:                    | T. Ryan    |
| TECH:                  | J. Coppage |
| Plant: Beaver Dam, Ky. |            |




Slack: 1.72"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.).
- TYPE 2 FRAME & COVER BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.


P3) 24" - CASTING HEIGHT - 8"  
P2) 24" x 24" - BX FLAT LID 8inW w/CC 24" HOLE - 8"  
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 28"  
1) 24" x 24" - Conseal CS-102 1.00"  
1) 24" - Conseal CS-102 1.00"  
1) Hole - 22  
2) Hole - 18

0 lb  
770 lb  
2883 lb  
0 lb  
0 lb  
0 lb  
0 lb


Structure Total: 3654 lb

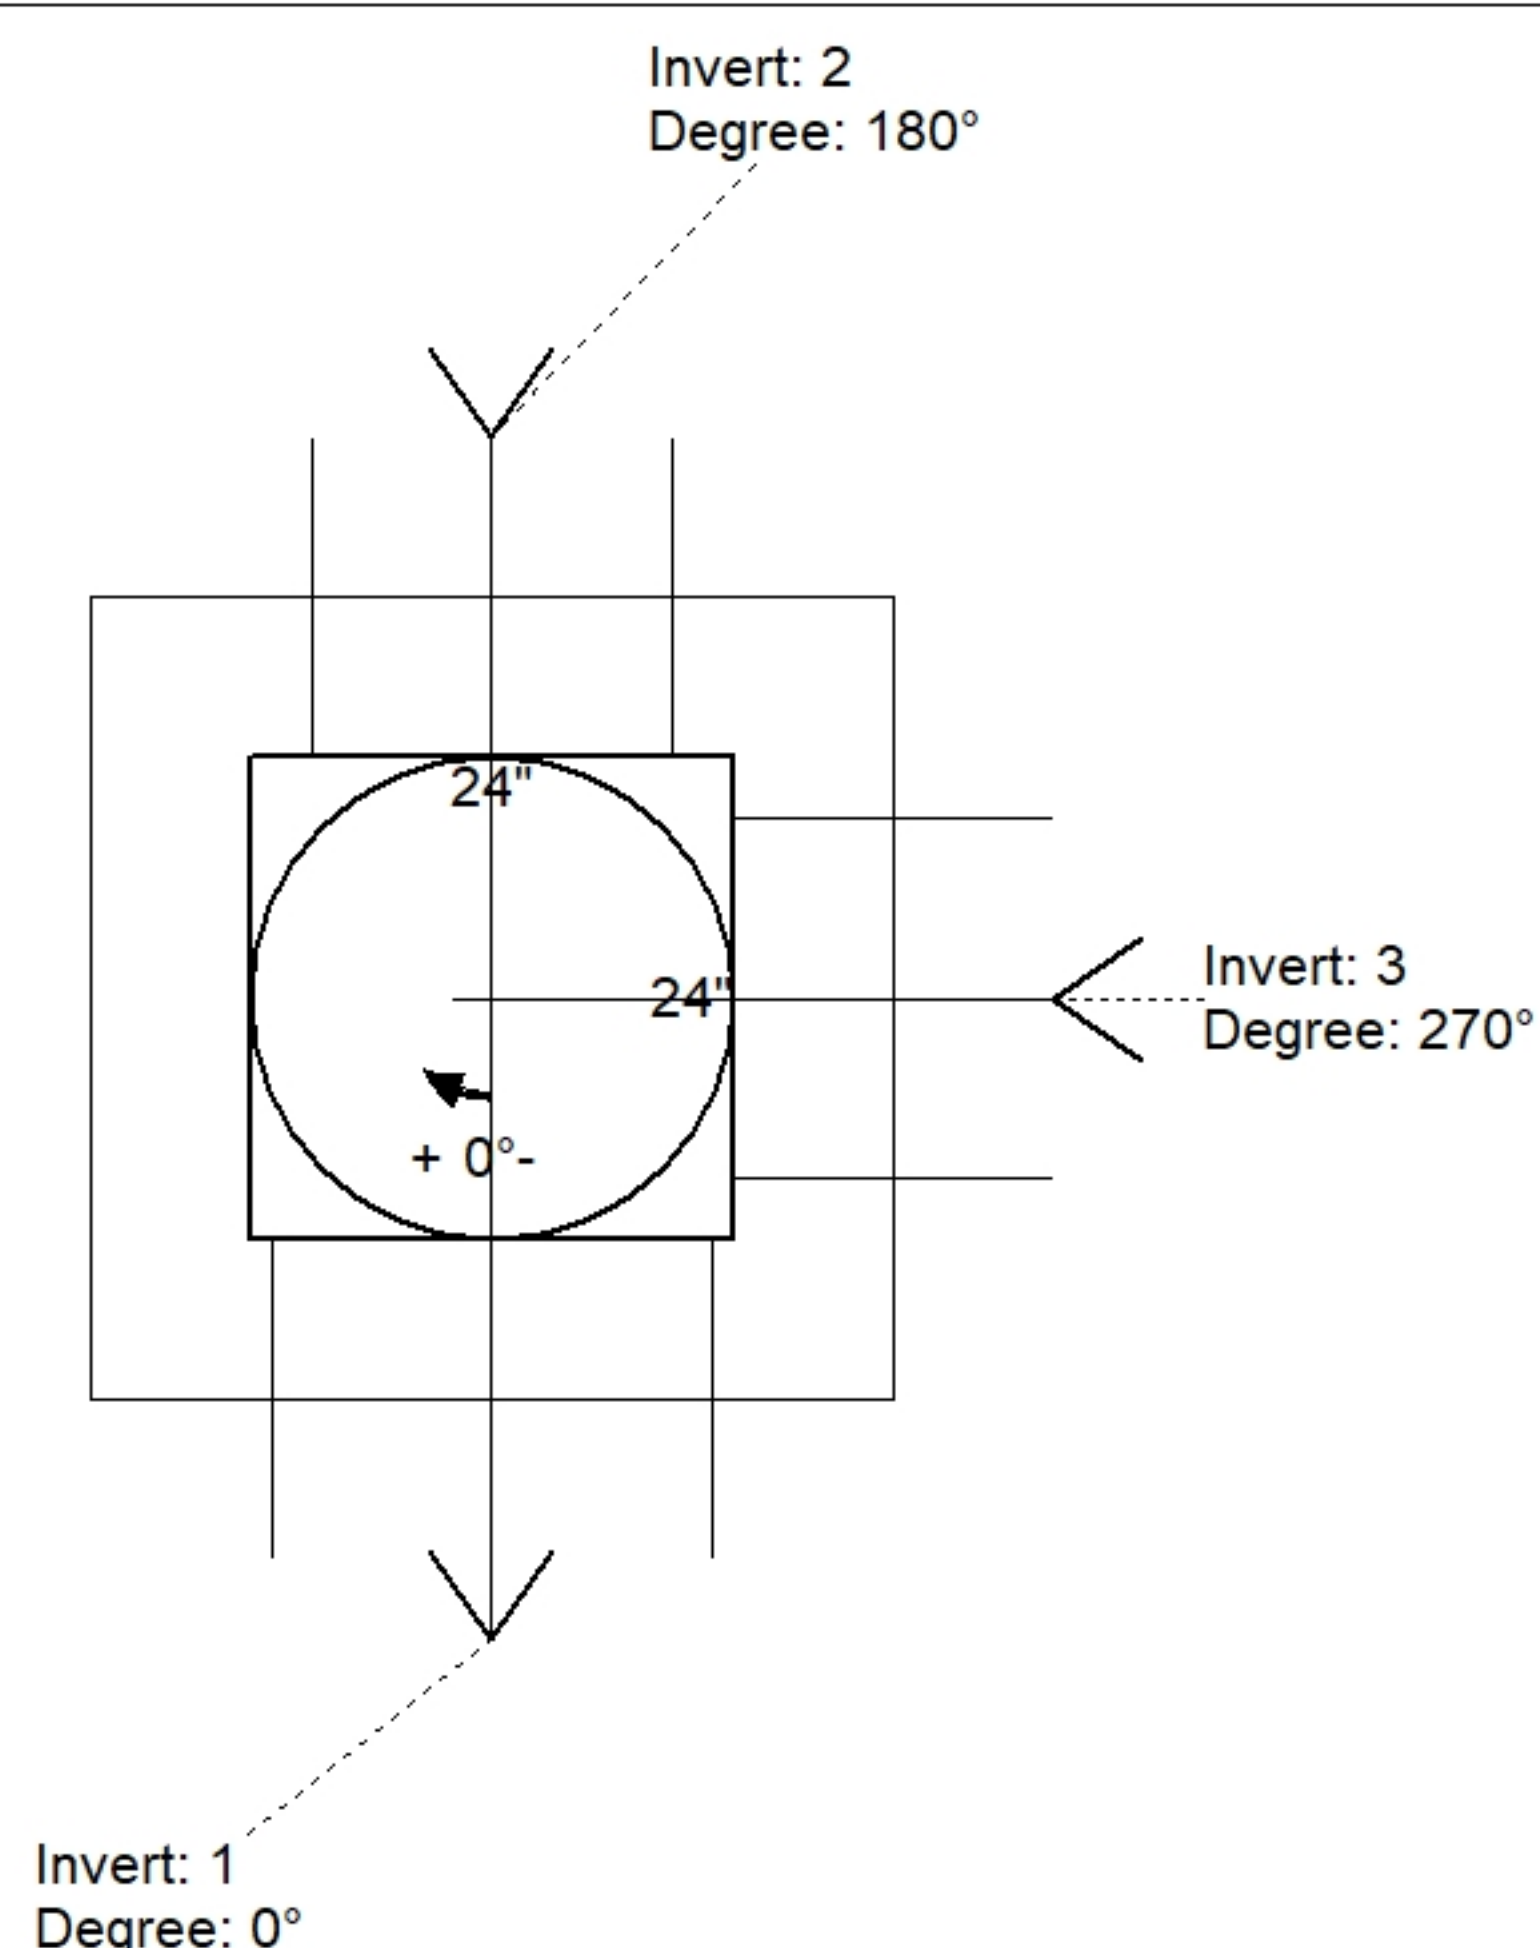

| Position | Elev    | Angle | Pipe           | Pipe OD | Hole | Connector | Up (⌵) | Ref |
|----------|---------|-------|----------------|---------|------|-----------|--------|-----|
| Rim      | 590.92' |       |                |         |      |           |        |     |
| Reducer  |         |       |                |         |      |           |        |     |
| Invert 1 | 587.11' | 0°    | 15" RCP B WALL | 19.5"   | 22"  | Hole 22   | -3.5"  | P1  |
| Invert 2 | 587.11' | 180°  | 15" CMP        | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 3 | 587.11' | 270°  | 15" CMP        | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 4 |         |       |                |         |      |           |        |     |
| Invert 5 |         |       |                |         |      |           |        |     |
| Invert 6 |         |       |                |         |      |           |        |     |
| Invert 7 |         |       |                |         |      |           |        |     |
| Invert 8 |         |       |                |         |      |           |        |     |

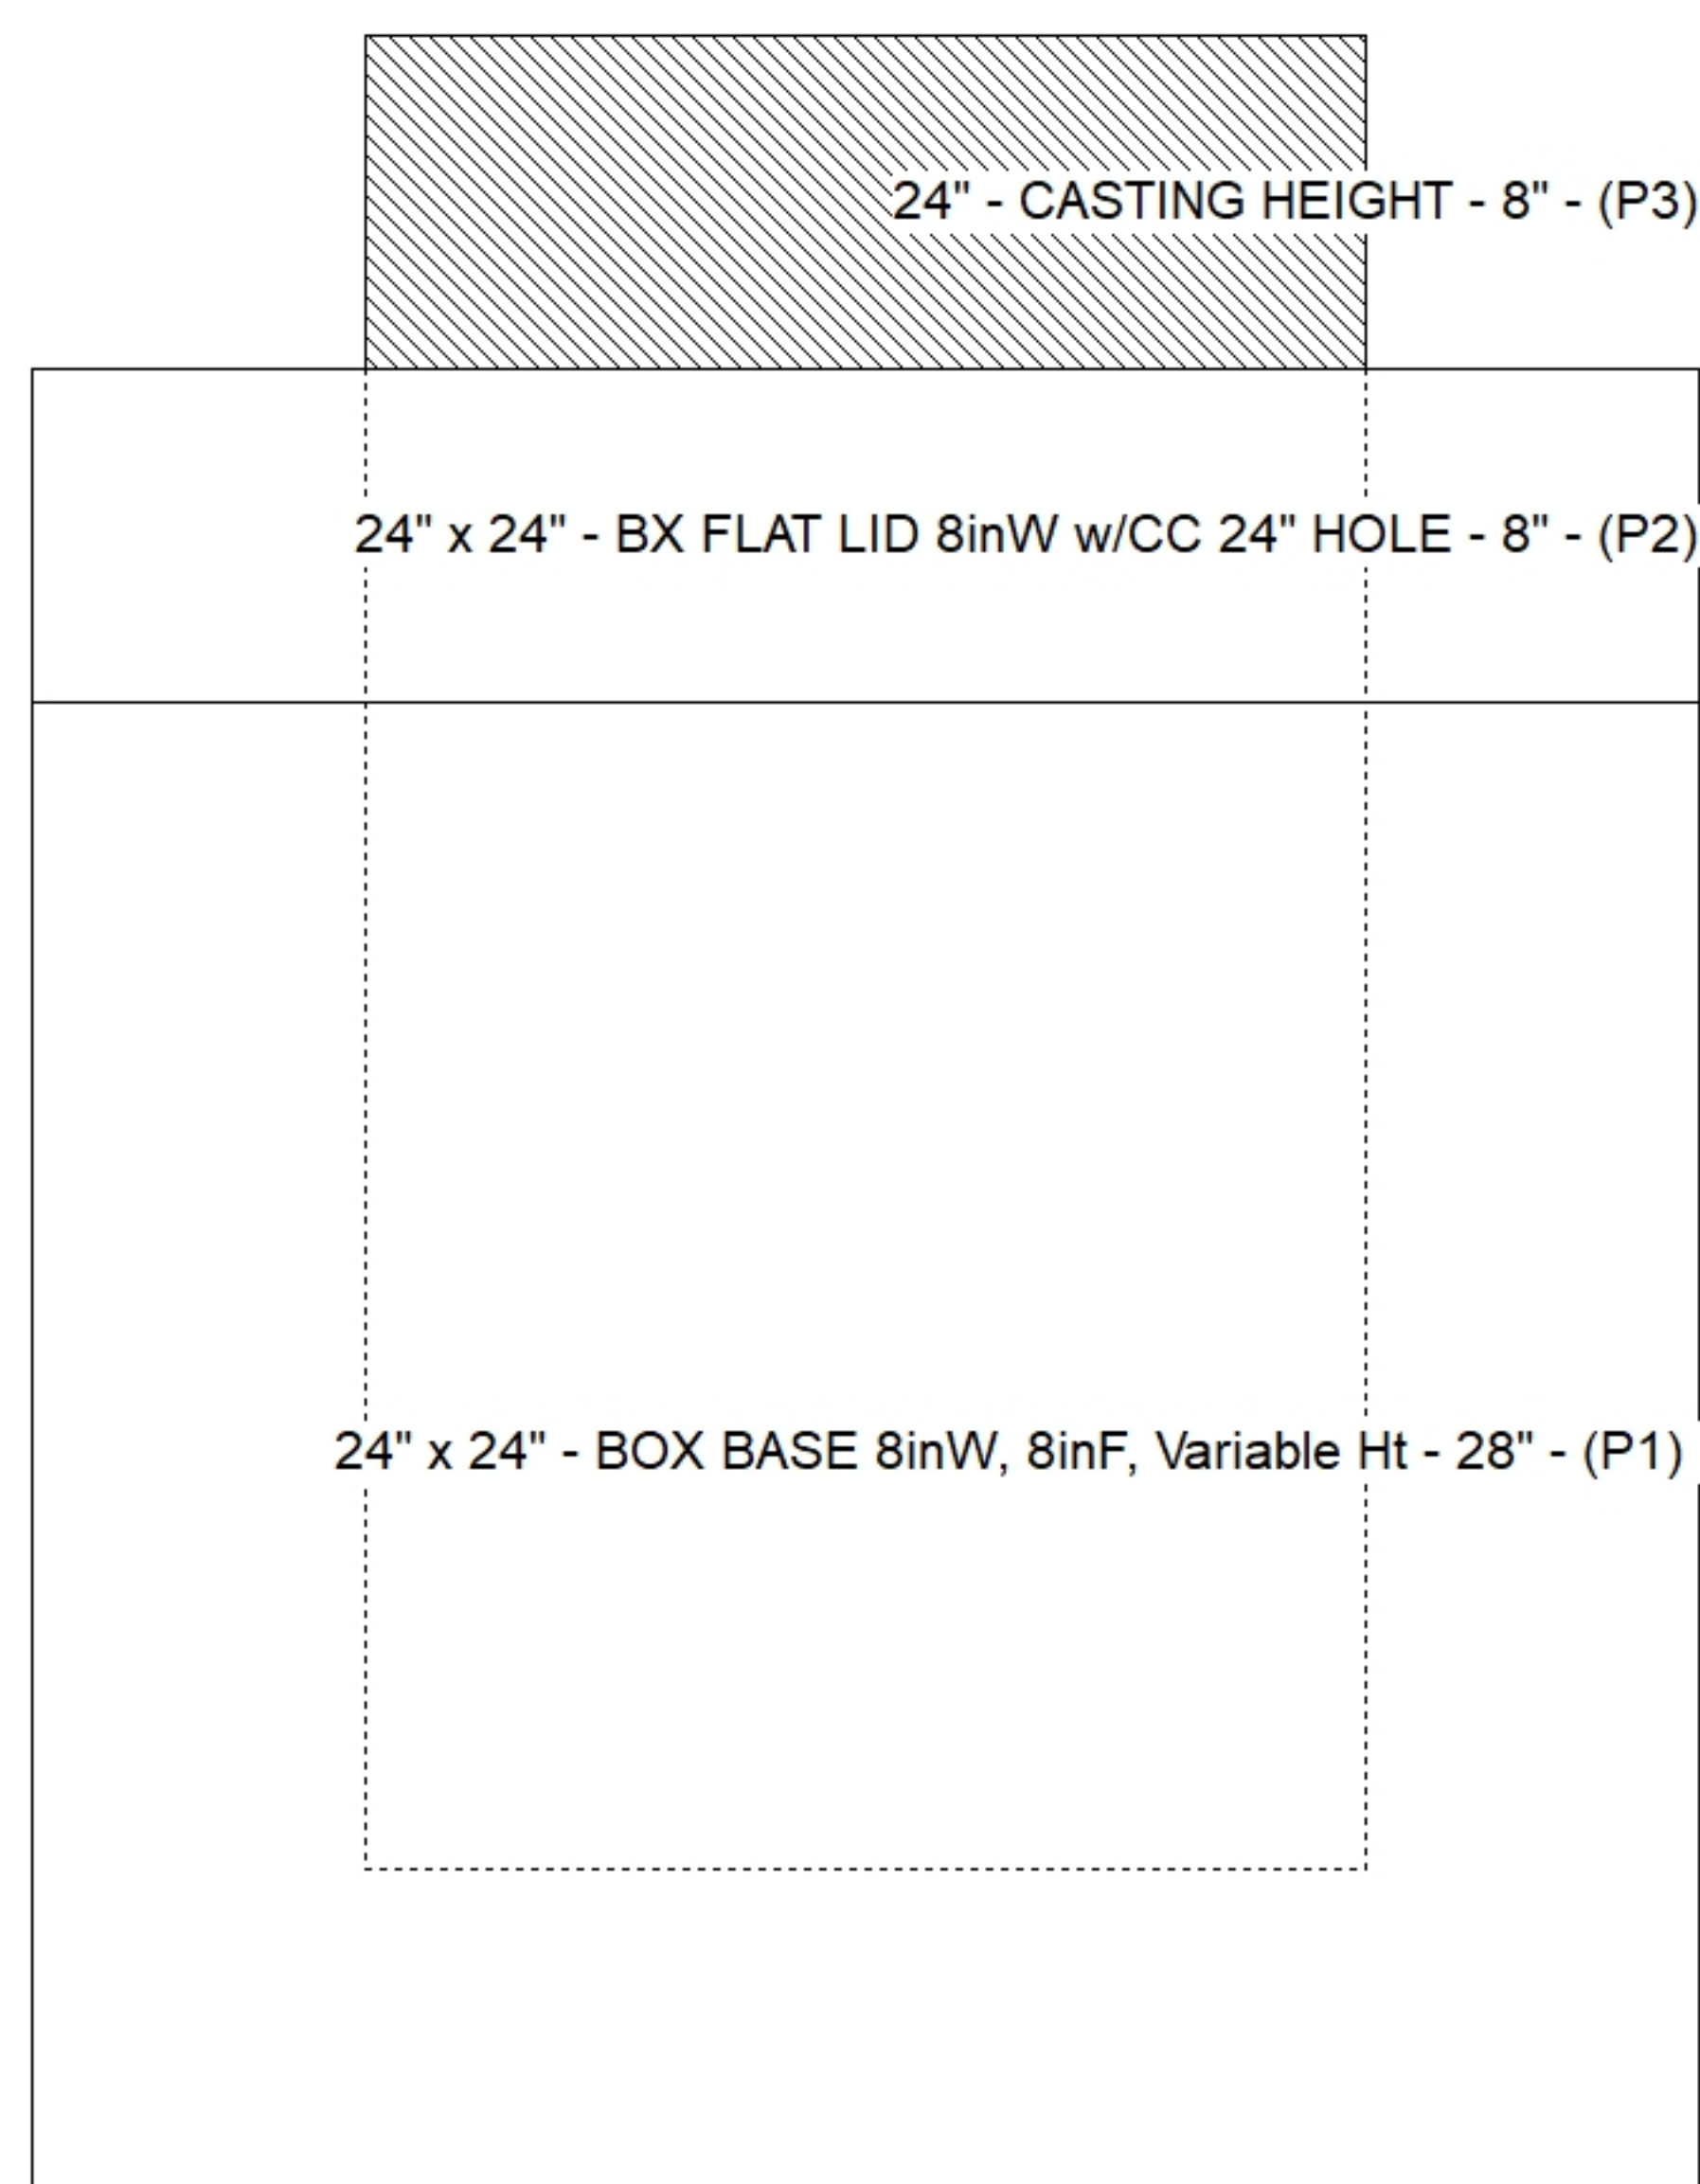

### Default - Interior Dimensions

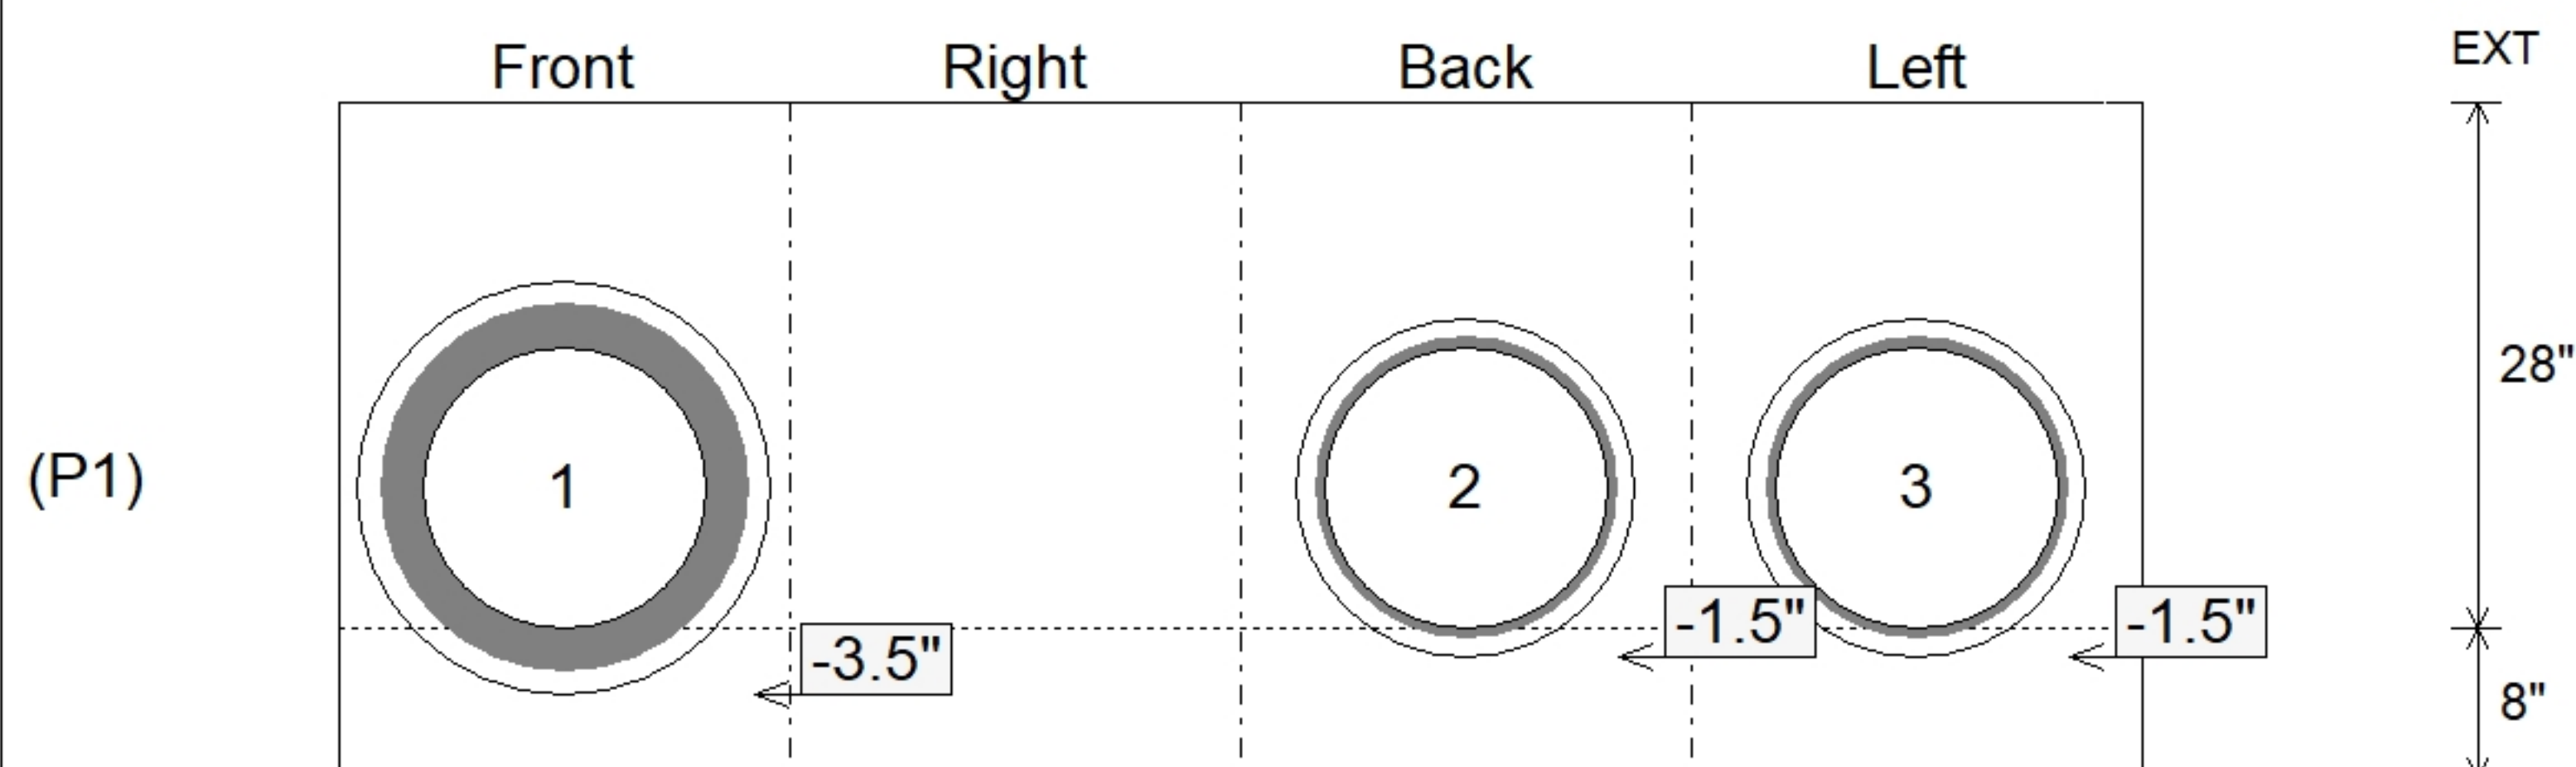

Submittal Drawing  
8/18/2026 9:55:18 AM

SUBMITTAL  
APPROVED BY:
