



Job Name: 25-2073 - Alcoa Outfall Job Location: Newburgh, IN Contractor: Bowen Engineering Corporation				Plant: 100 6/16/2026 2:37:55 PM		Tech: J. Horsley PC: A. Chambers						
Structure ID: MH 1												
P2 BX084084-08RVF				BOX RISER 8inW, Variable Ht F/G								
P5) 30" x 30" - CASTING HEIGHT - 4" P4) 30" x 30" - GRADE RING F/F - 3" P3) 84" x 84" - CB FLAT TOP 8"W w/30"x30" ECC HOLE F/F - 8" P2) 84" x 84" - BOX RISER 8inW, Variable Ht F/G - 66" P1) 84" x 84" - BOX RISER 8inW, Variable Ht FB T/F - 58" 1) CASTING - HOE 468 F/G 2) 84" x 84" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 2) DOGHOUSE - 48"x48" 1) SQ. Hole n/n - 72"x42" 11) MH Step ML-10-TDS-NCR - 10"						0 lb 218 lb 6109 lb 14274 lb 11548 lb 489 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 32637 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 8" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) - ADDITIONAL REBAR REQUIRED AROUND OPENING FOR INVERT 2 4. STEPS AT 270 DEGREES 5. HOE 468 FRAME & GRATE SUPPLIED BY ICAST 6. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED IN 0° & 180° WALLS, 18" FROM TOP OF WALLS				
Rim: 394.26' Rim to Invert: 11.28' Slack: 0.36" Sump: 4" Step Position: 270°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2	389'	90°	50"	48" x 24" BOX CULV. (8W8F8T)	64" x 40"	SQ. Hole 72"x42"	72" x 42"	72"	8.25"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

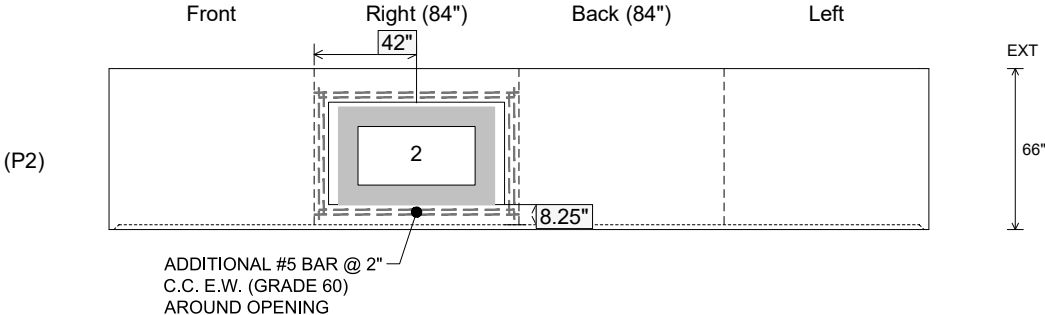

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 66" Height (Ext): 66"	Weight (Net): 14274 lb Volume (Net): 3.65cu.yd
----------------------------------	----------------------------------	--	--	---
