

Contractor: Byard Construction, LLC

Plant: 100




Slack: 0"

1. (2)JBS 3080-V SETS (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 28" x 64" - CASTING HEIGHT - 6.50"
P1) 28" x 64" - BOX BASE 6inW, 6inF - 36"
2) CASTING - JBS 3080-V SET (F/G/H)
1) 28" x 64" - Conseal CS-102 1.00"
1) Hole - 22

0 lb
5109 lb
1000 lb
0 lb
0 lb


Structure Total: 6109 lb

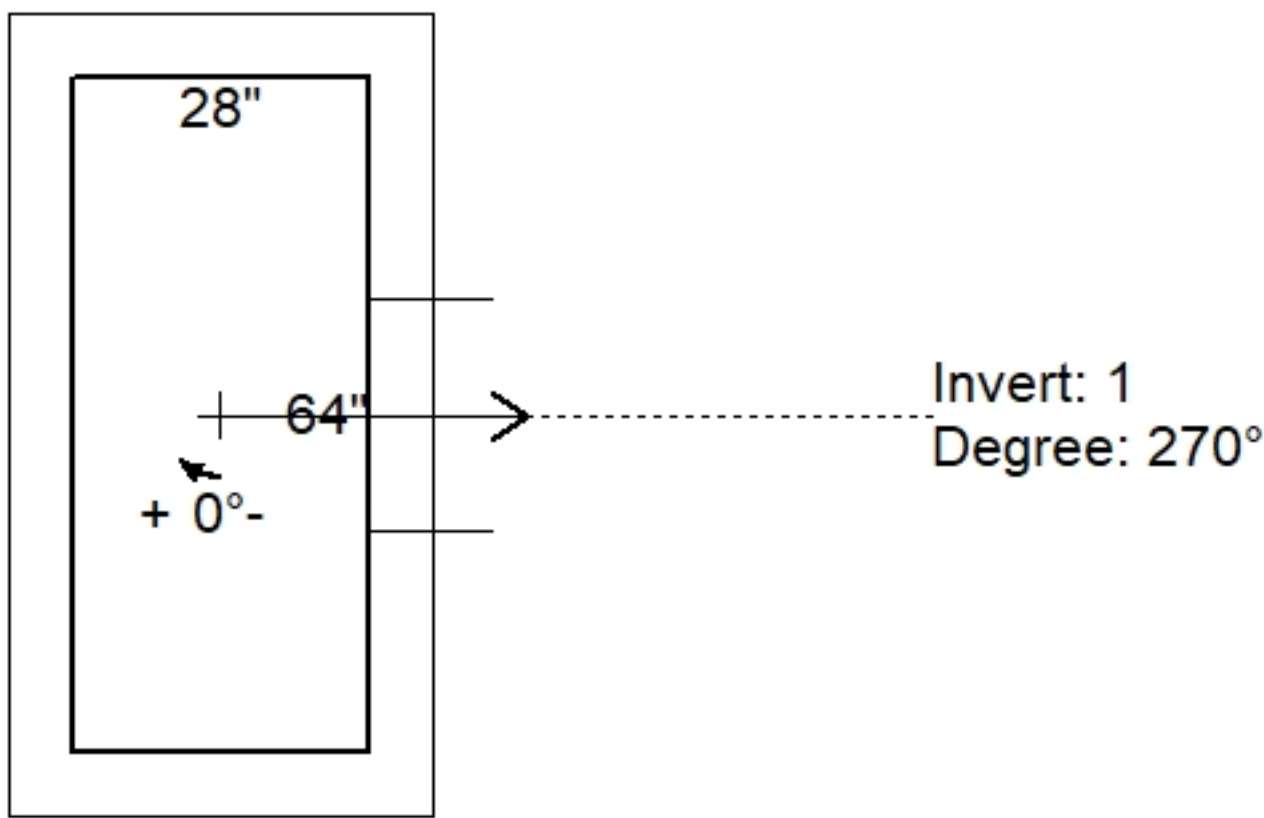

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	435.02'							
Reducer								
Invert 1	431.52'	270°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

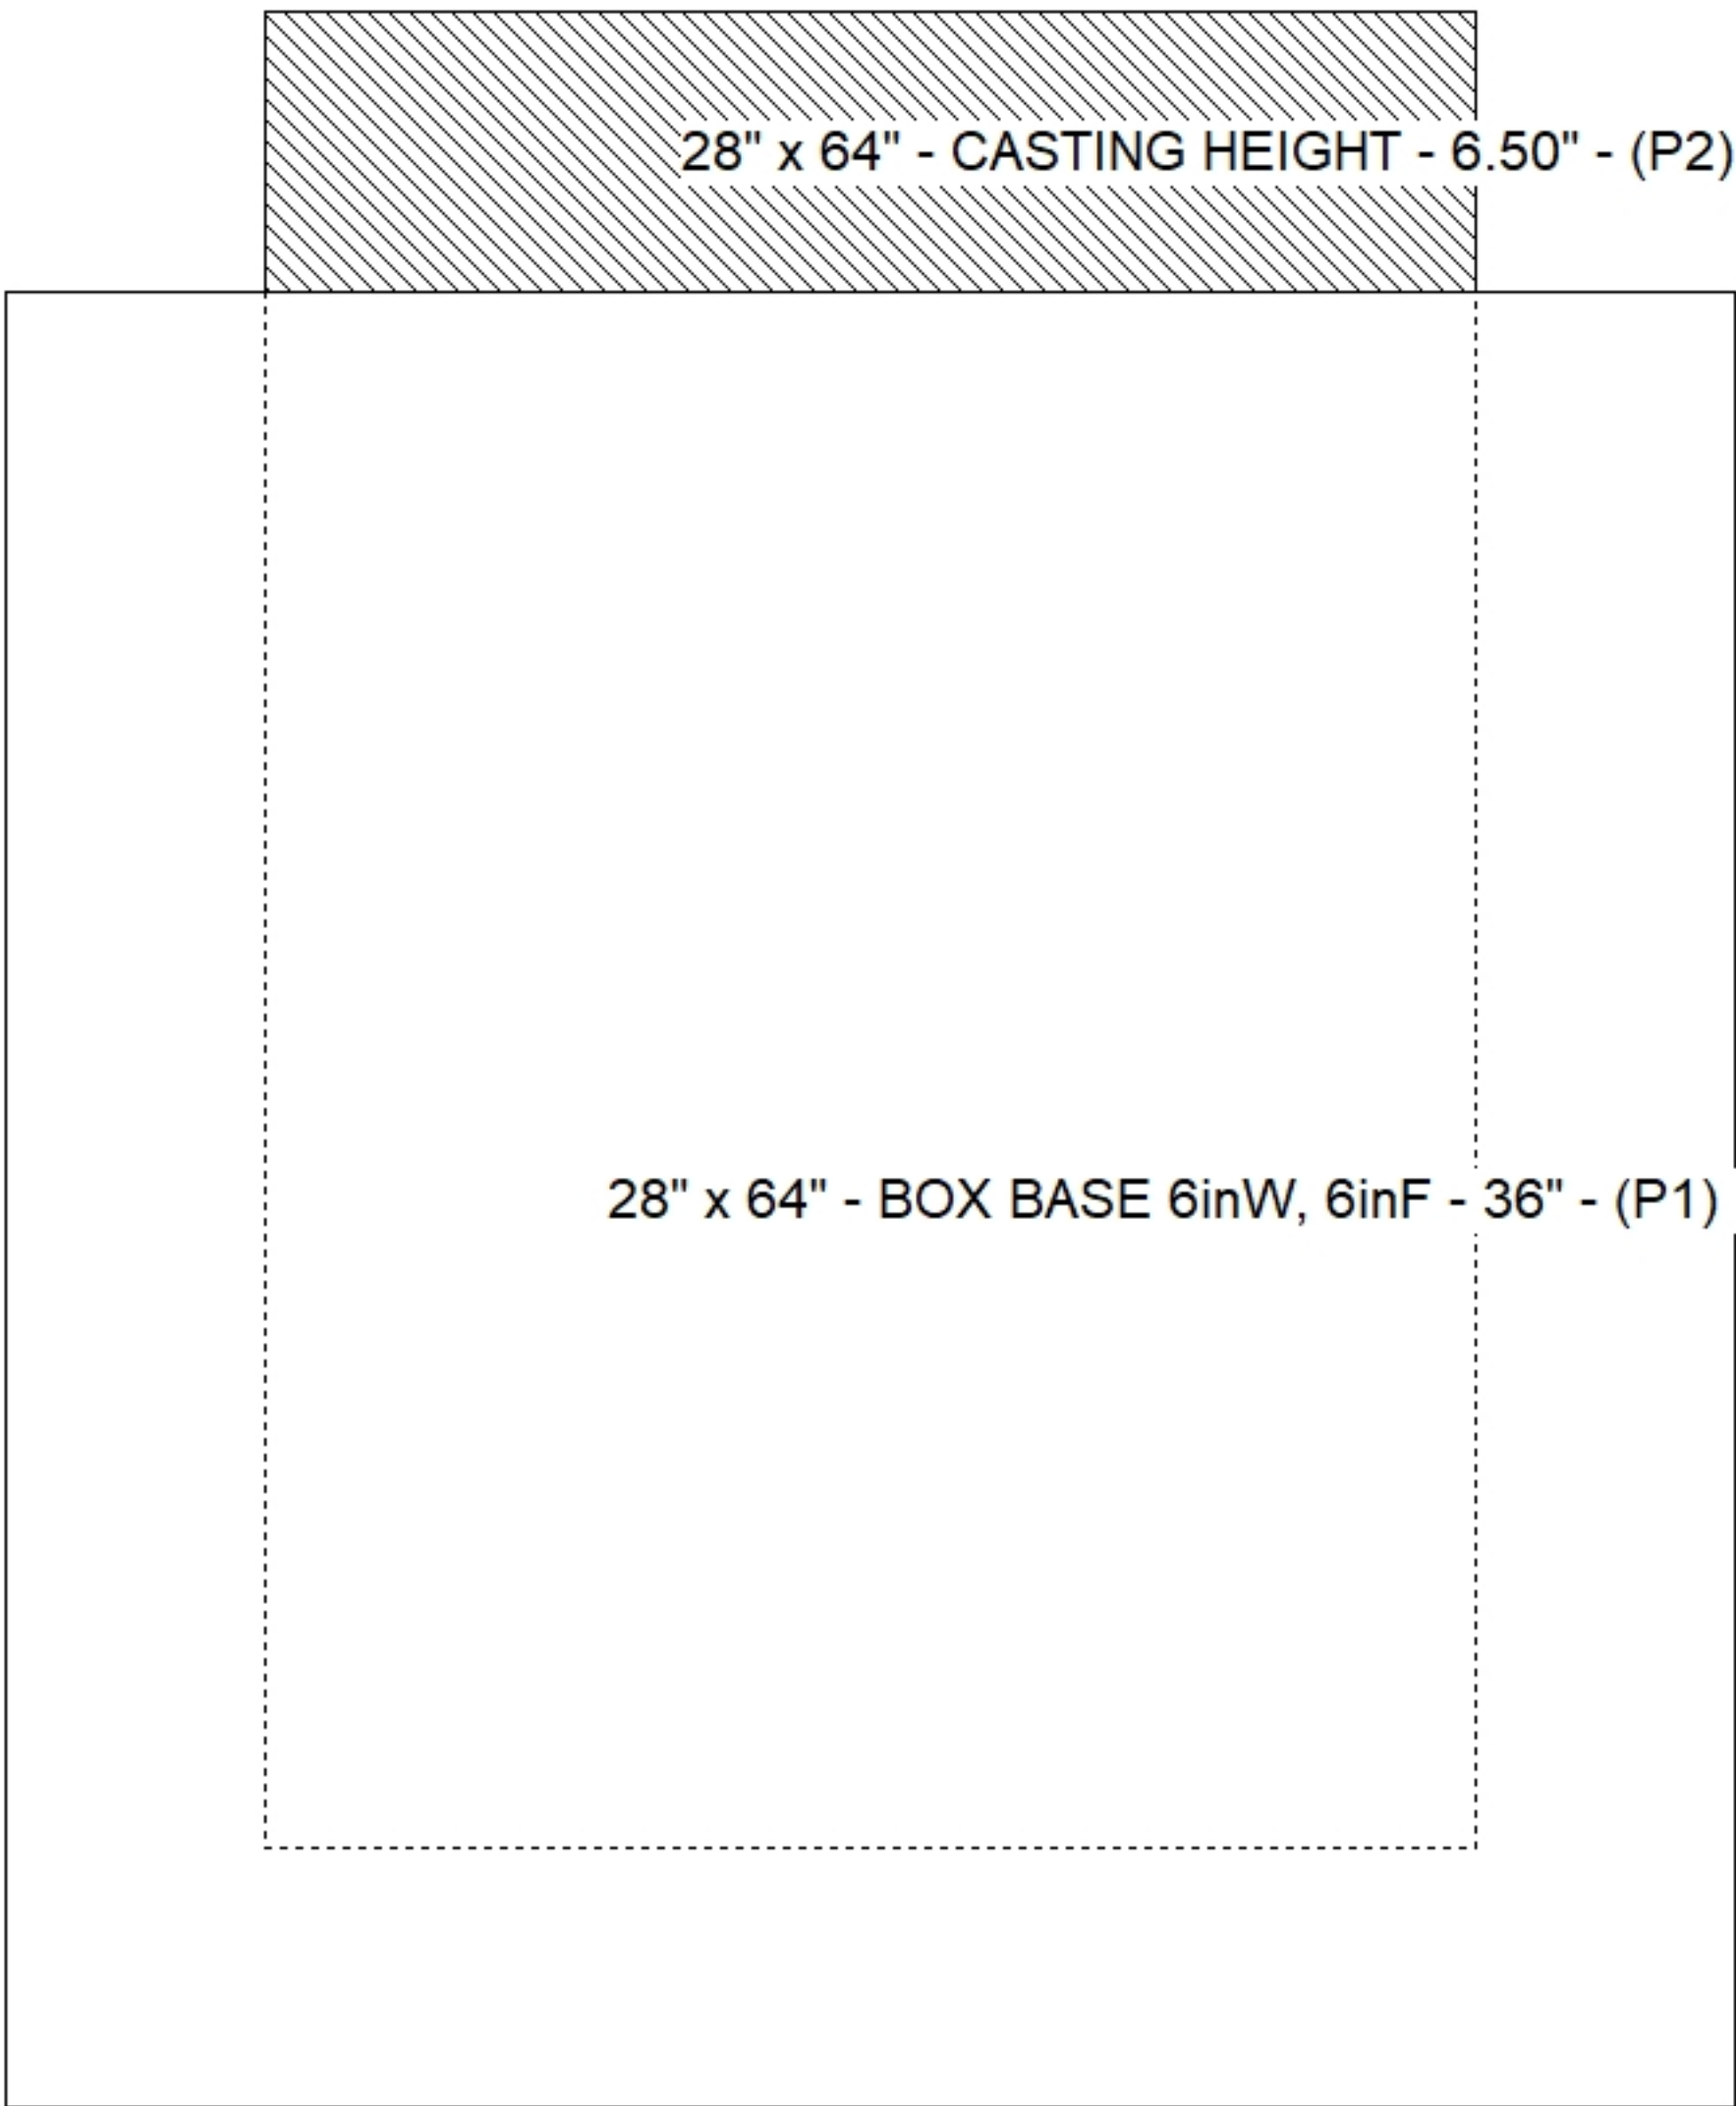

Default - Interior Dimensions

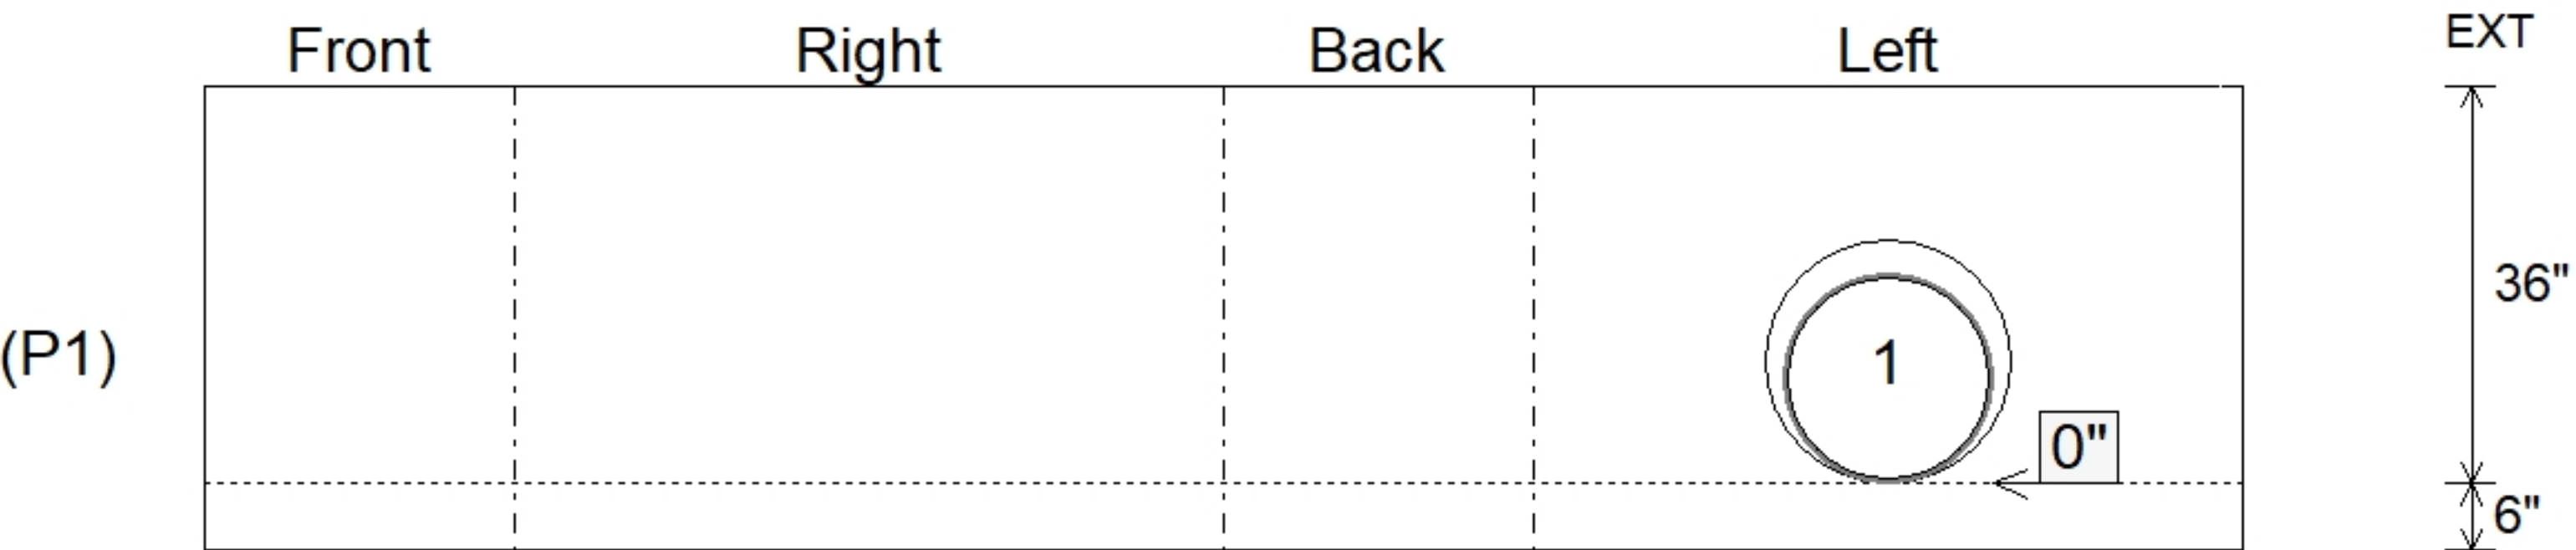

Submittal Drawing
9/9/2026 3:27:52 PM

SUBMITTAL
APPROVED BY:
