

Contractor: Byard Construction, LLC

TECH: Jared - A

Plant: 100




Slack: 0.56"

1. (2)JBS 3080 SETS (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 28" x 64" - CASTING HEIGHT - 6.50"
P1) 28" x 64" - BOX BASE 6inW, 6inF, Variable Ht - 40"
2) CASTING - JBS 3080 SET (F/G/H)
1) 28" x 64" - Conseal CS-102 1.00"
2) Hole - 22

0 lb
5337 lb
1000 lb
0 lb
0 lb


Structure Total: 6337 lb

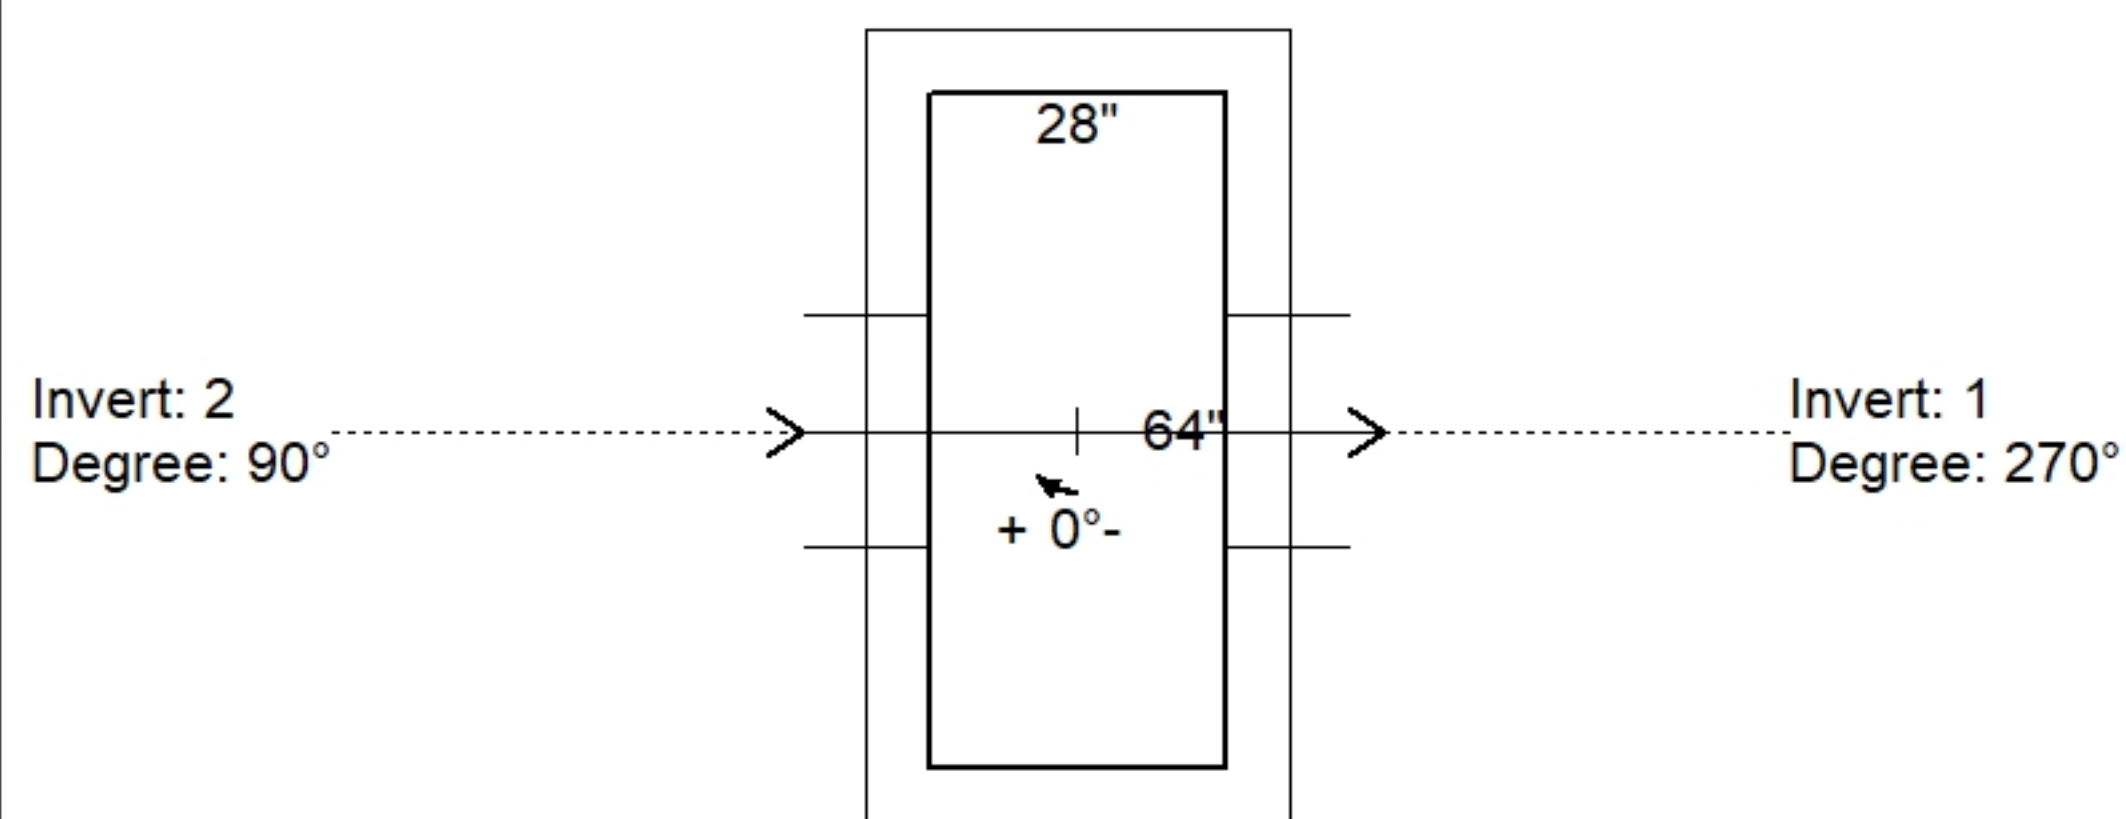

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (␣)	Ref
Rim	427.02'							
Reducer								
Invert 1	423.14'	270°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 2	423.24'	90°	18" CMP	19"	22"	Hole 22	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

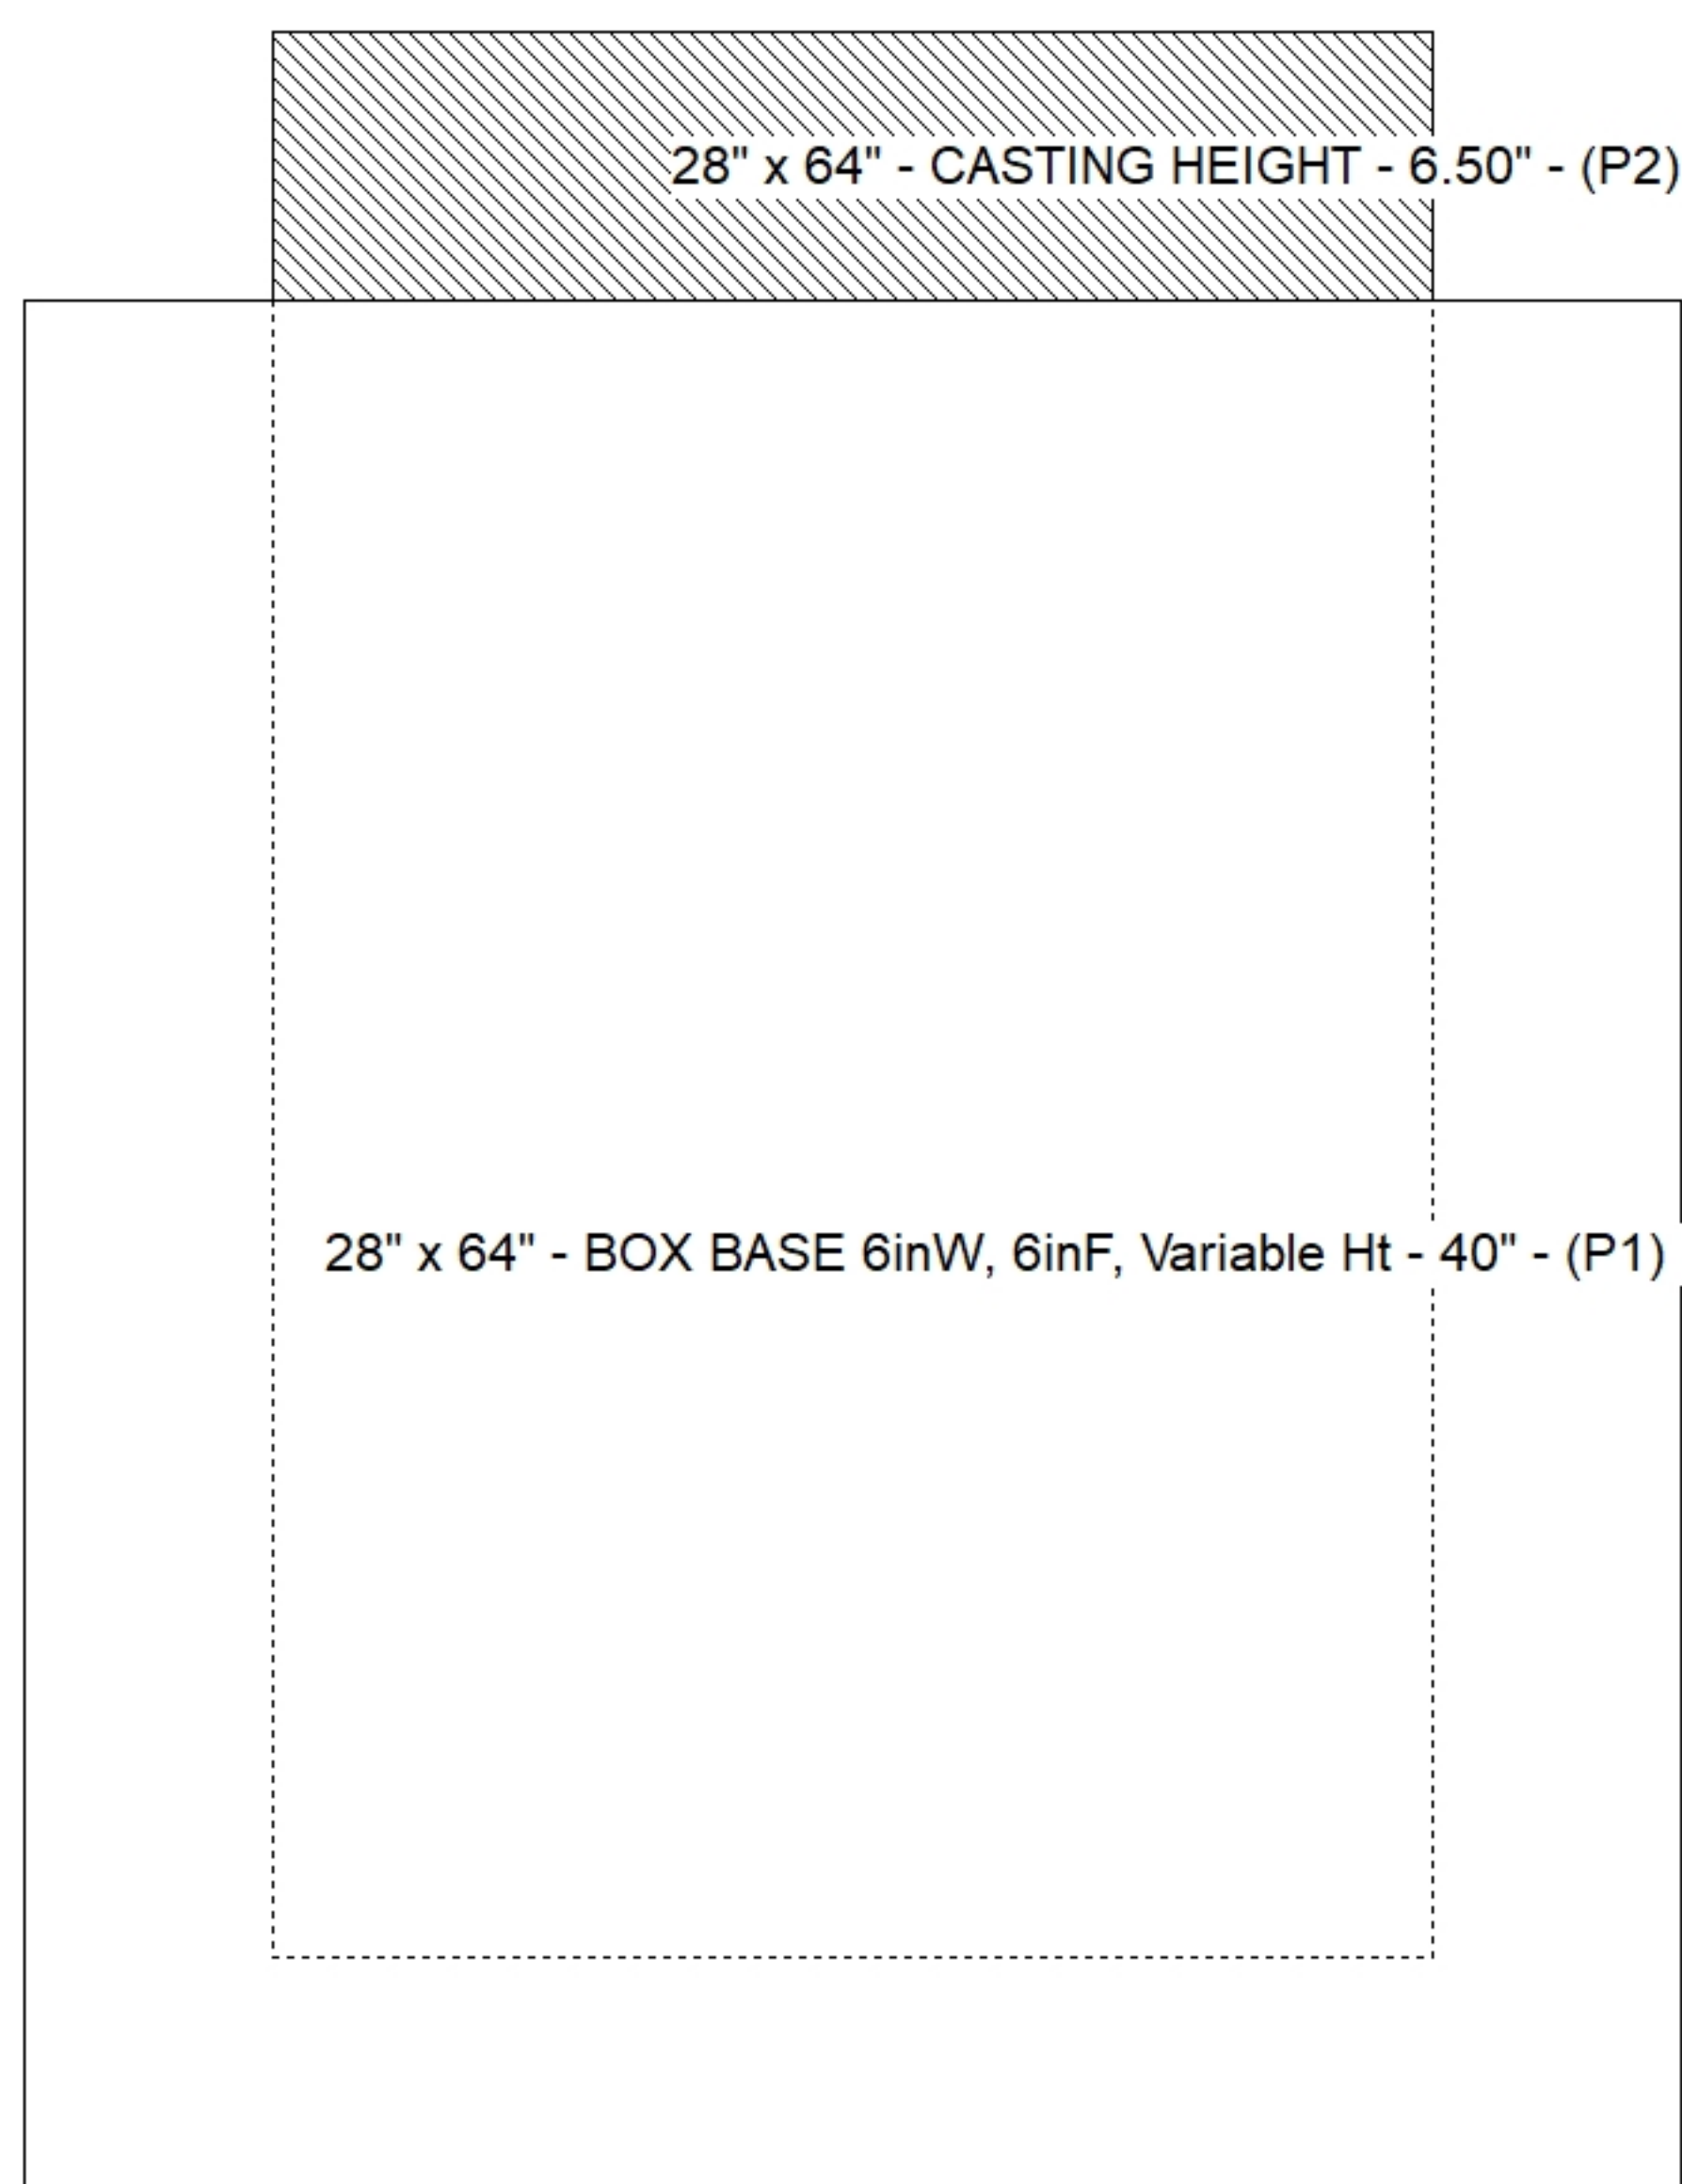

Default - Interior Dimensions

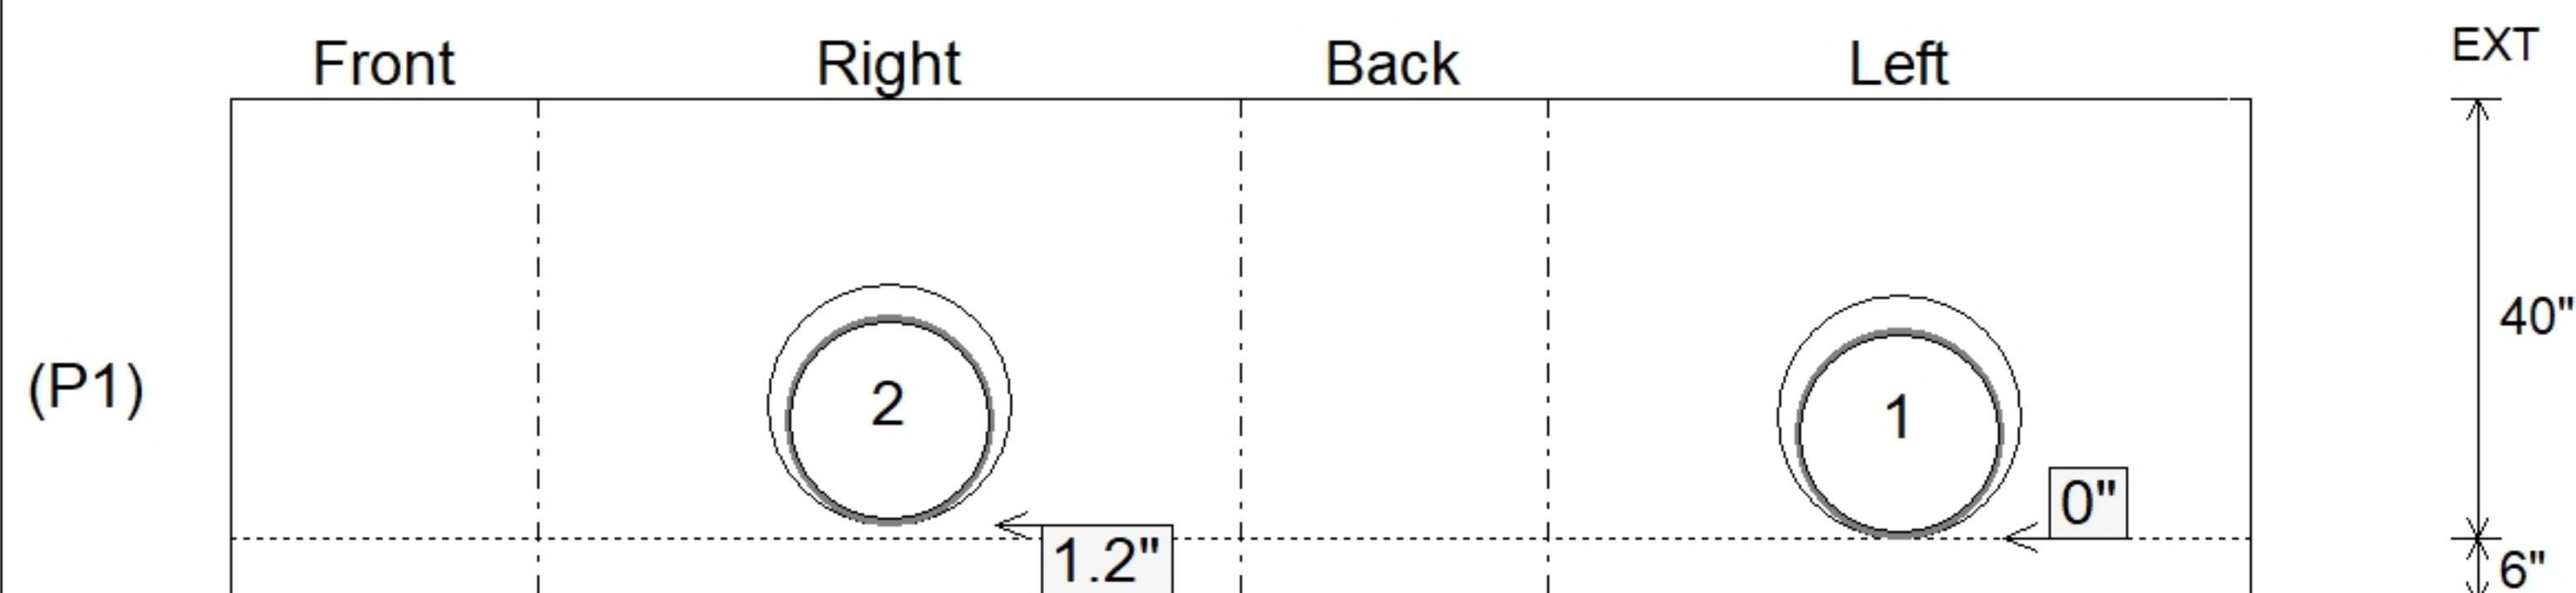

Submittal Drawing
9/9/2026 3:27:55 PM

SUBMITTAL
APPROVED BY:
