




Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:10:07 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 50											
P1		MH048BAVF									
MH BASE Custom Ht T/n											
P3) 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 38" 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 20 1) Hole - 18 3) MH Step ML-10-TDS-NCR - 10" Structure Total: 5166 lb						Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STORM INVERT 5. STEPS AT 270 DEGREES 6. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY OTHERS					
Rim: 551.73' Rim to Invert: 4.25' Slack: 0" Sump: 3" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	547.48'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	0.5"	0"	
Invert 2	547.48'	70°	35.375"	12" HDPE	14.5"	Hole 18	18"	18.451"	0"	0"	
Invert 3	547.48'	160°	81"	15" HDPE	17.6"	Hole 20	20"	20.629"	0.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

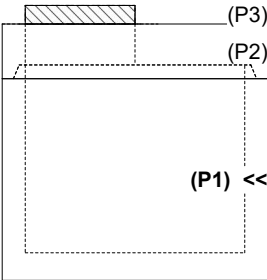


RIGHT-SIDE UP VIEW (int. dimensions)

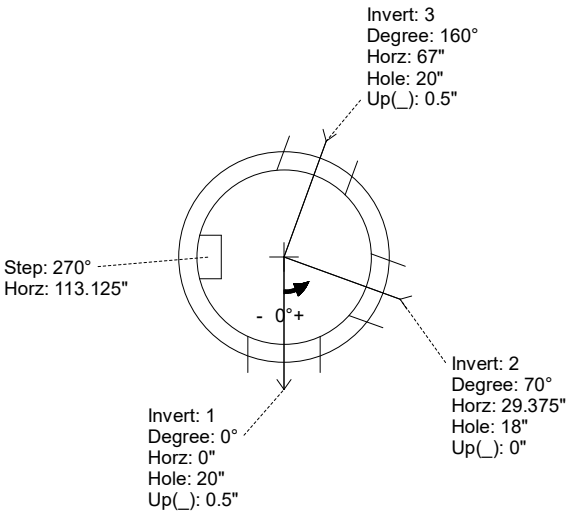

UPSIDE-DOWN VIEW (int. dimensions)

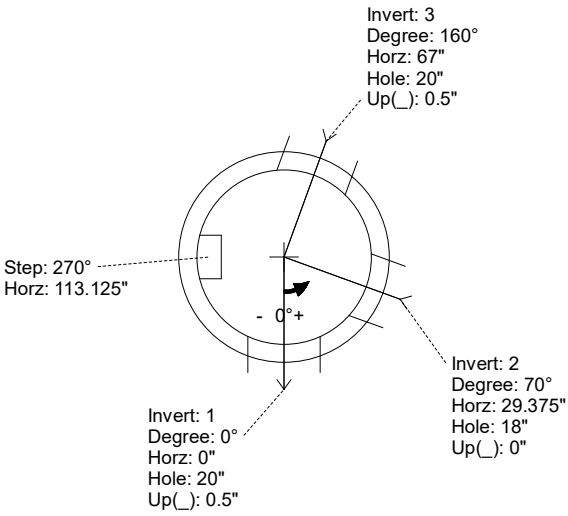

INSIDE WALL DIMENSIONS

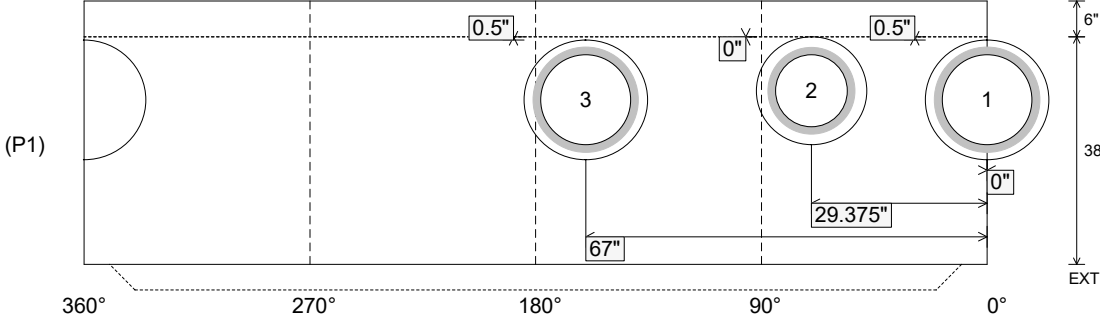

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 38"
Height (Ext): 44"

Weight (Net): 3605 lb
Volume (Net): 0.92cu.yd
