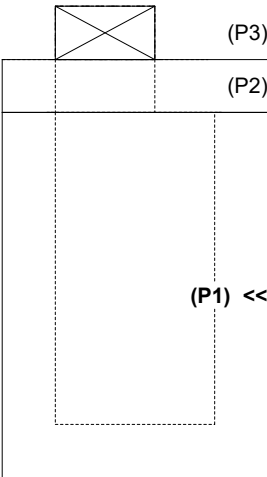
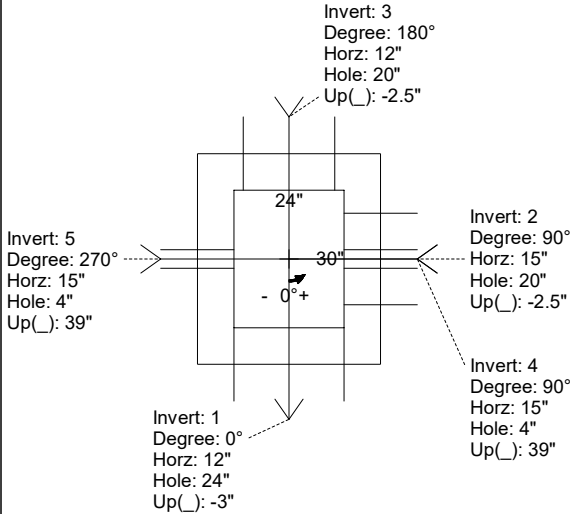
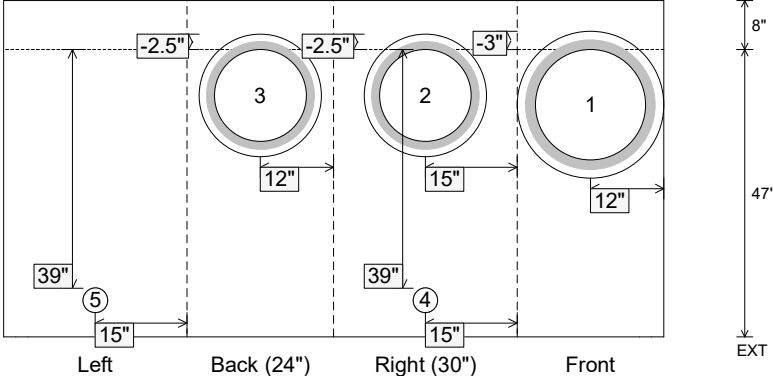


Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:09:28 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 54											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 47" 1) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 24 2) Hole - 20 2) Hole - 4 Structure Total: 5949 lb						Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS					
Rim: 552.01' Rim to Invert: 5.25' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	546.76'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-3"	0"	
Invert 2	546.76'	90°	23"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"	
Invert 3	546.76'	180°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"	
Invert 4	550.01'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	39"	0"	
Invert 5	550.01'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	39"	0"	
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 47" Height (Ext): 55"		Weight (Net): 4986 lb Volume (Net): 1.27cu.yd		
