



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction				Plant: 100 6/12/2026 3:11:12 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 60										
P2 BX2430-08R18				BOX RISER 8inW F/G						
P4) 15" x 27" - P.I.P. - BY OTHERS - 8" P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P2) 24" x 30" - BOX RISER 8inW F/G - 18" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38" 2) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 20 2) Hole - 4						0 lb 963 lb 1675 lb 4140 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS		
Rim: 551.92' Rim to Invert: 6.08' Slack: 0.96" Sump: 0" Step Position:						Structure Total: 6778 lb				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	549.84'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	8"	0"
Invert 5	549.84'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	8"	0"
Invert 6										
Invert 7										
Invert 8										

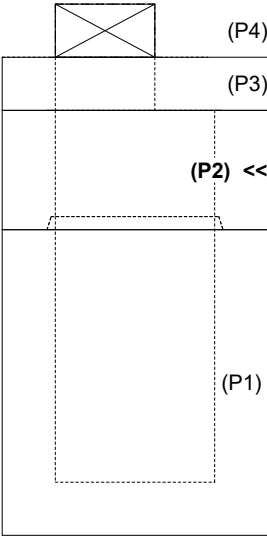

(P4)
(P3)
(P2) <<
(P1)


RIGHT-SIDE UP VIEW (int. dimensions)



Invert: 4
Degree: 90°
Horz: 15"
Hole: 4"
Up(): 8"

Invert: 5
Degree: 270°
Horz: 15"
Hole: 4"
Up(): 8"

INSIDE WALL DIMENSIONS



Front Right (30") Back (24") Left

(P2)

EXT 18"

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 18" Height (Ext): 18"	Weight (Net): 1675 lb Volume (Net): 0.43cu.yd
----------------------------------	----------------------------------	--	--	--
