



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:10:01 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 64											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht T/n											
P4) 15" x 27" - P.I.P. - BY OTHERS - 8" P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P2) 24" x 30" - BOX RISER 8inW F/G - 36" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 35" 2) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 18 2) Hole - 4					0 lb 963 lb 3366 lb 3898 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS				
Rim: 552.28' Rim to Invert: 7.25' Slack: 0" Sump: 0" Step Position:					Structure Total: 8228 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	545.03'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-3"	0"	
Invert 2	545.03'	90°	23"	12" HDPE	14.5"	Hole 18	18"	18"	-3"	0"	
Invert 3	545.03'	180°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

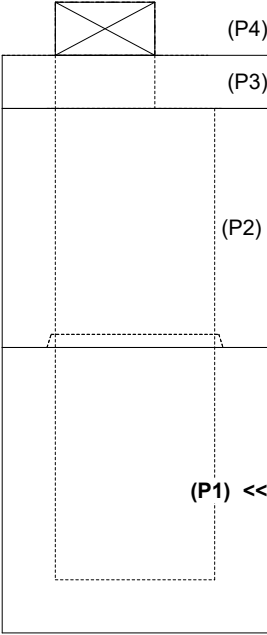

UPSIDE-DOWN VIEW (int. dimensions)

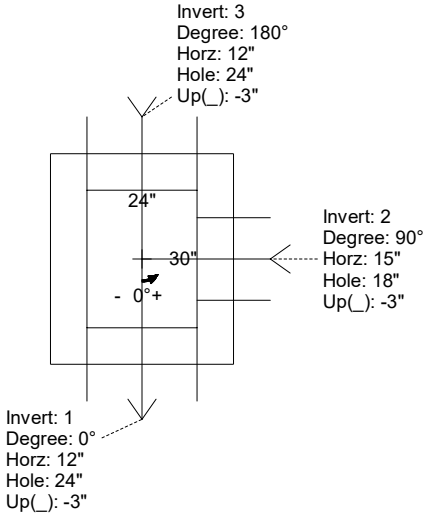

INSIDE WALL DIMENSIONS

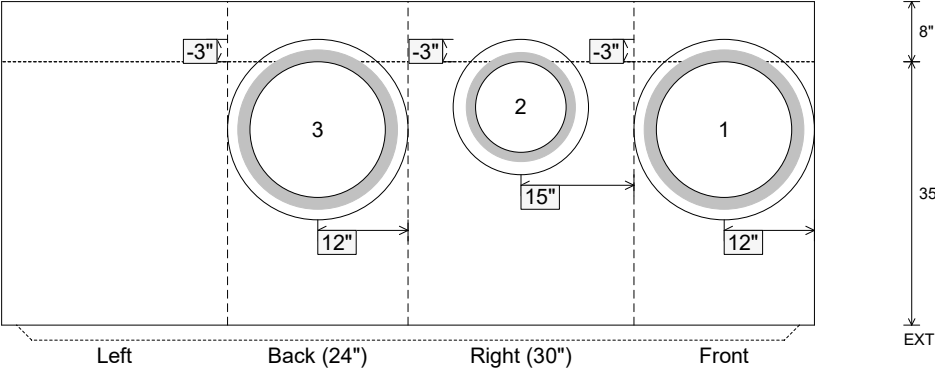

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 35" Height (Ext): 43"	Weight (Net): 3898 lb Volume (Net): 1cu.yd
----------------------------------	---------------------------------	--	--	---
