




Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:11:08 PM		Tech: J. Horsley - A PC: J. Jarvis					
Structure ID: 73												
P2		BX2430-08R30		BOX RISER 8inW F/G								
P4) 15" x 27" - P.I.P. - BY OTHERS - 8" P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P2) 24" x 30" - BOX RISER 8inW F/G - 30" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38" 2) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 18 2) Hole - 4					0 lb 963 lb 2803 lb 4636 lb 0 lb 0 lb 0 lb 0 lb ----- 8402 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS					
Rim: 551.7'					Rim to Invert: 7'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2	549.7'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	20"	0"		
Invert 3	549.7'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	20"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

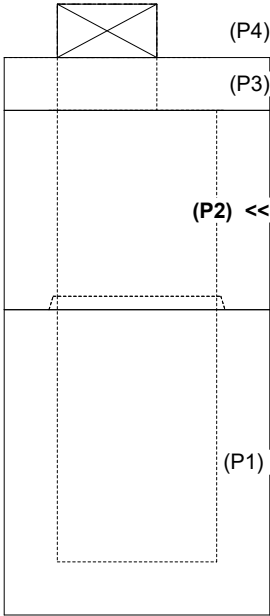

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

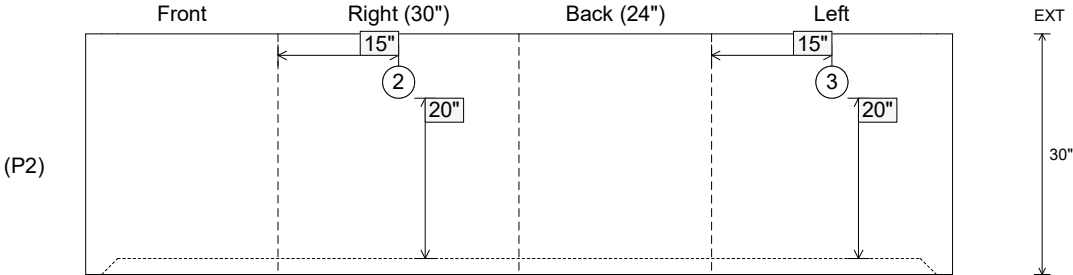

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 30" Height (Ext): 30"	Weight (Net): 2803 lb Volume (Net): 0.72cu.yd
----------------------------------	----------------------------------	--	--	--
