

Job Name: 25-2977 KYTC Hopkins CO Call 105 (255382)
 Job Location:
 Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

1/12/2026 1:59:12 PM

Tech: J. Coppage

PC: Celina Goff



Structure ID: 1978L

P1 BX3636-08BA24

BOX BASE 8inW, 8inF

- P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P1) 36" x 36" - BOX BASE 8inW, 8inF - 24"
- 1) 36" x 36" - Conseal CS-102 1.00"
- 1) DOGHOUSE INVRTD - 26"x28"

Structure Total:

0 lb
 4211 lb
 0 lb
 0 lb

 4211 lb

Structure Notes:



- **KYTC STATE PROJECT**
- 1. JR HOE KY-316 PROVIDED BY ICAST.
- 2. KYTC DBI TYPE 1 / ASTM C913 SPECIFICATIONS.
- 3. CONCRETE = 4,000 PSI AT 28 DAYS.
- 4. NO STEPS.
- 5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
- 6. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)

Rim: 378.8' Rim to Invert: 2.8' Slack: 1.6" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	376'	0°	26"	18" RCP B WALL	23"	DOGHOUSE INVRTD 26"x28"	26" x 28"	26"	-4"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

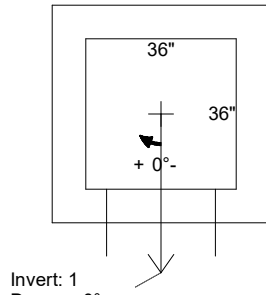


Invert: 1
 Degree: 0°
 Horz: 18"
 Hole: 26" x 28"
 Up(): -4"



Invert: 1
 Degree: 0°
 Horz: 18"
 Hole: 26" x 28"
 Up(): -4"

INSIDE WALL DIMENSIONS



Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 24"
 Height (Ext): 32"

Weight (Net): 4211 lb
 Volume (Net): 1.08cu.yd
