



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 7/1/2026 12:29:38 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 469											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht											
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 44" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 2) Hole - 24 2) Hole - 4						0 lb 963 lb 4705 lb 237 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5905 lb		Structure Notes: **KYTC STATE PROJECT** 1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST. 2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB (SPACED AT 12" CC) AROUND THE 15" X 27" HOLE			
Rim: 894.5' Rim to Invert: 5.07' Slack: 0.84" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	889.43'	340°	15.885"	18" ADS N-12	22"	Hole 24	24"	23.567", 5.421"	-3"	4"	
Invert 2	889.43'	90°	23"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 3	892.5'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36.84"	0"	
Invert 4	892.5'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36.84"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

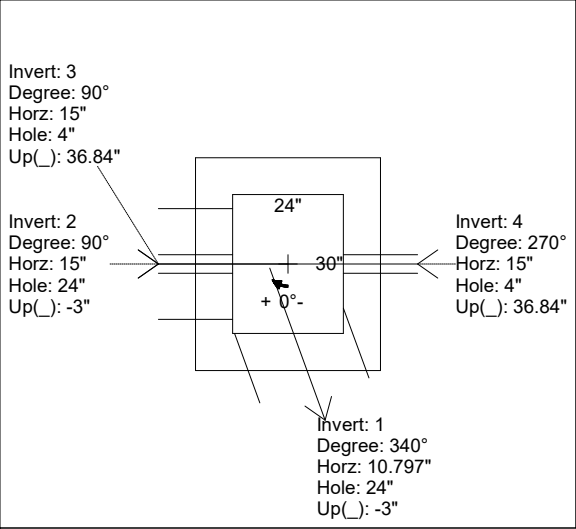

UPSIDE-DOWN VIEW (int. dimensions)

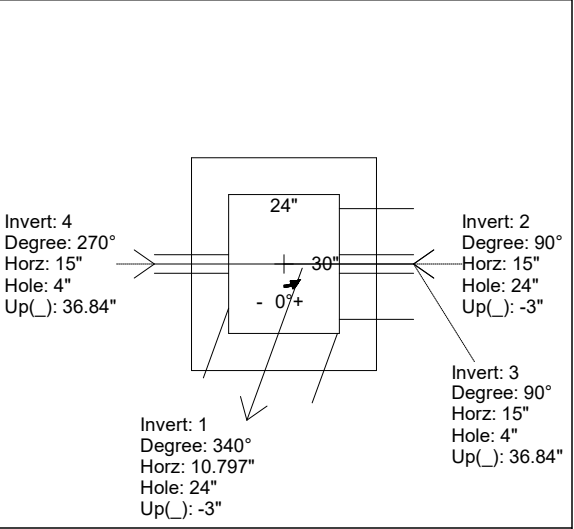

INSIDE WALL DIMENSIONS

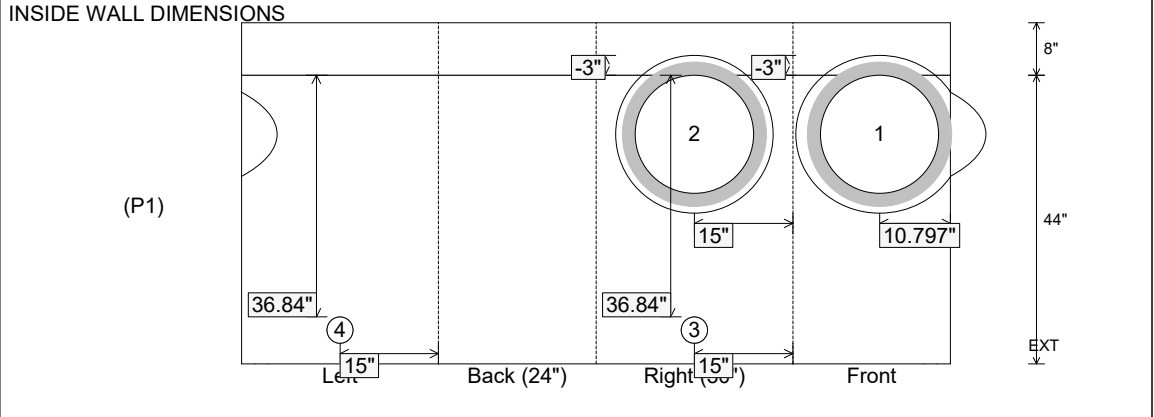

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 44" Height (Ext): 52"	Weight (Net): 4705 lb Volume (Net): 1.2cu.yd
----------------------------------	-------------------------------	--	--	---
