



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 7/1/2026 12:29:17 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 474											
P1 BX3636-08BA54 BOX BASE 8inW, 8inF											
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF - 54" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 32 1) Hole - 24 2) Hole - 8						3400 lb 5270 lb 1235 lb 6701 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 16812 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. HOE KY 206 F/C (KY TY1) PROVIDED BY ICAST. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 892.7' Rim to Invert: 7.56' Slack: 0.72' Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	885.14'	110°	29.078"	24" ADS N-12	28"	Hole 32	32"	34.054"	-4"	-6"	
Invert 2	885.14'	0°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 3	885.14'	260°	24.462"	24" ADS N-12	28"	Hole 32	32"	32.494"	-4"	3"	
Invert 4	888.81'	0°	26"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	42.04"	0"	
Invert 5	888.81'	180°	26"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	42.04"	0"	
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

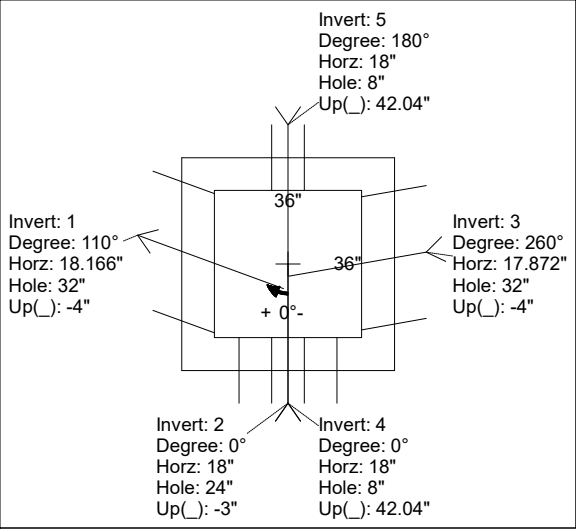

UPSIDE-DOWN VIEW (int. dimensions)

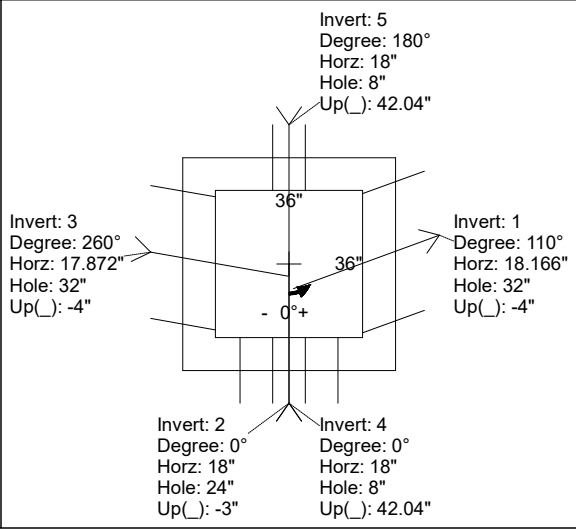

INSIDE WALL DIMENSIONS

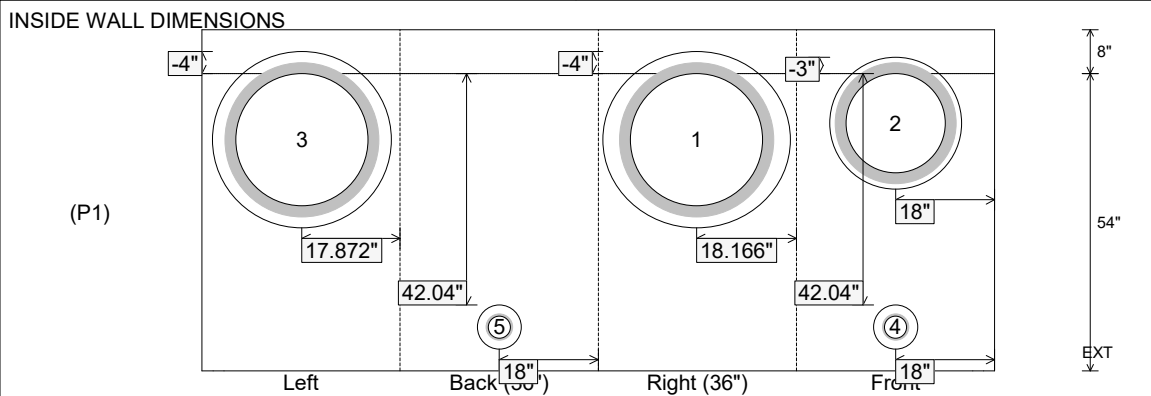

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 54" Height (Ext): 62"	Weight (Net): 6701 lb Volume (Net): 1.71cu.yd
----------------------------------	-------------------------------	--	--	--
