



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 7/1/2026 12:30:40 PM		Tech: Jared - A PC: J. Jarvis			
Structure ID: 475										
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht										
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 40" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 4					0 lb 963 lb 4767 lb 237 lb 0 lb 0 lb 0 lb 0 lb 0 lb 5967 lb Structure Total:		Structure Notes: **KYTC STATE PROJECT** 1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST. 2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB (SPACED AT 12" CC) AROUND THE 15" X 27" HOLE			
Rim: 894.04' Rim to Invert: 4.67' Slack: 0.04" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	889.37'	0°	20"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"
Invert 2	892.04'	0°	20"	4" WEEP HOLE	4"	Hole 4	4"	4"	32.04"	0"
Invert 3	892.04'	180°	20"	4" WEEP HOLE	4"	Hole 4	4"	4"	32.04"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

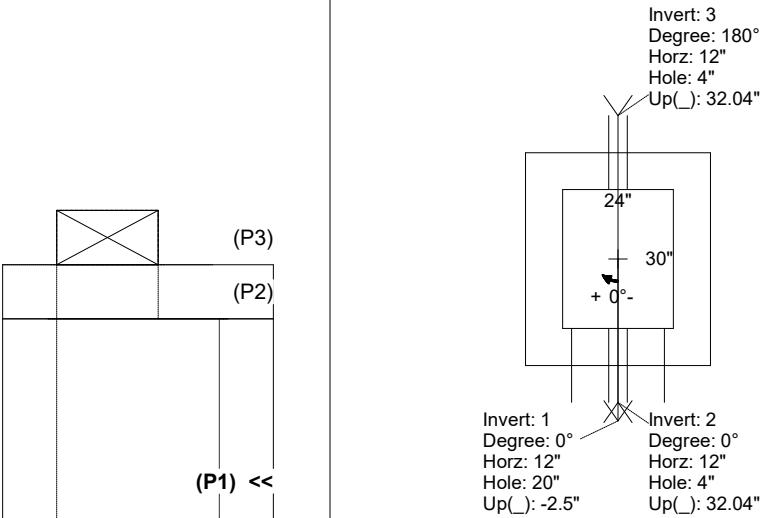

UPSIDE-DOWN VIEW (int. dimensions)

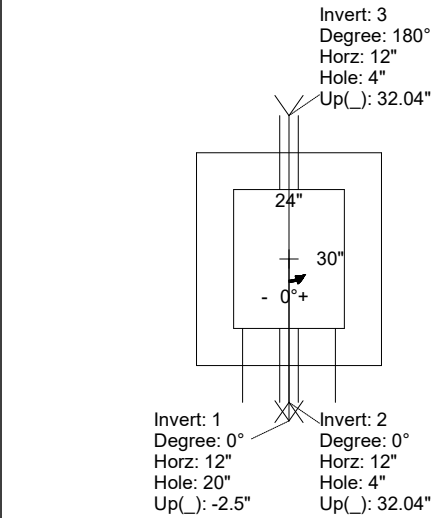

INSIDE WALL DIMENSIONS

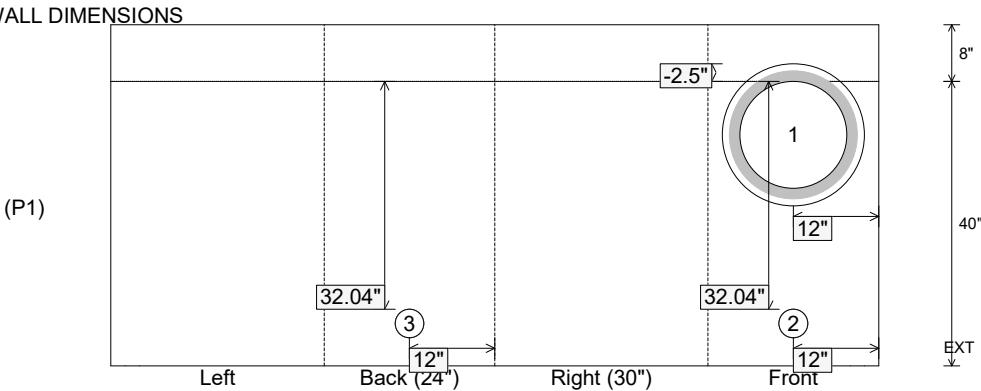

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 4767 lb Volume (Net): 1.22cu.yd
----------------------------------	-------------------------------	--	--	--
