



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 6/4/2026 4:52:36 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 483											
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P3) 24" x 60" - CB INLET KY A 5' TOP LEFT F/G - 10" P2) 24" x 60" - CB INLET KY A 5' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 56" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 8					1895 lb 2670 lb 6832 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- 11603 lb Structure Total:		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 890.32' Rim to Invert: 7.07' Slack: 0.84" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	883.25'	270°	26"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"	
Invert 2	887.08'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	44"	0"	
Invert 3	887.08'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	44"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

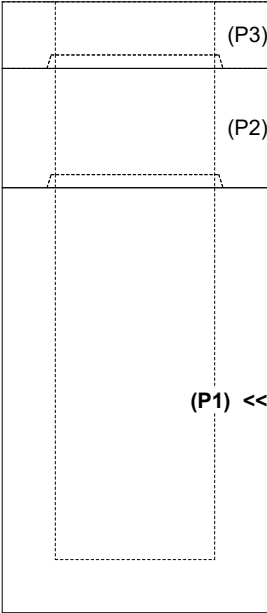

UPSIDE-DOWN VIEW (int. dimensions)

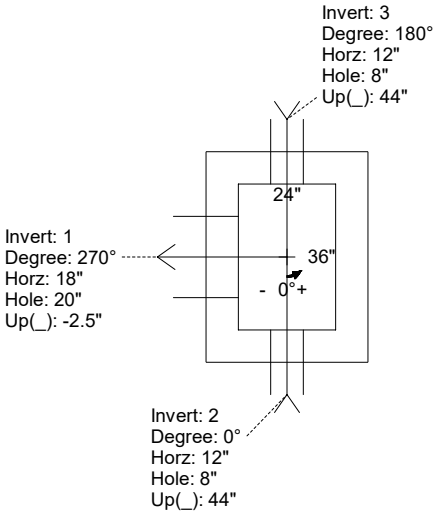

INSIDE WALL DIMENSIONS

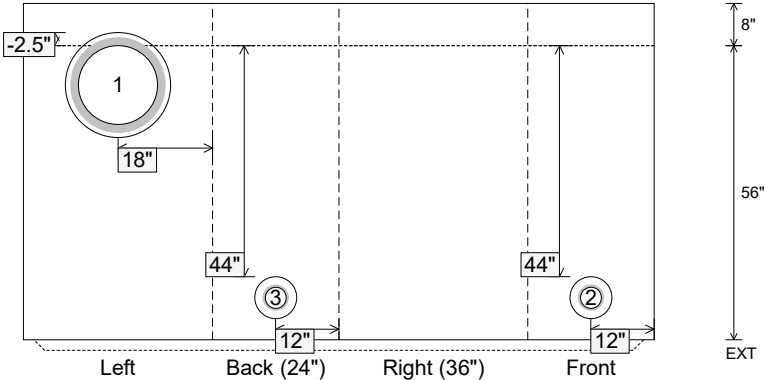

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 56" Height (Ext): 64"	Weight (Net): 6832 lb Volume (Net): 1.74cu.yd
----------------------------------	---------------------------------	--	--	--
