


Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

6/5/2026 12:00:23 PM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 529

P2 BX036036-08TS024036

CB TRANSITION SLAB 24"X36" HOLE T/F

P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18"
P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE T/F - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25"

1) CASTING - HOE KY-206 F/C (KY TY1)

1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast)

1) 36" x 36" - Conseal CS-102 1.00"

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 24

2) Hole - 8

3400 lb

5270 lb

1235 lb

4446 lb

206 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total:

14556 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TY A / ASTM C-913 SPECS



2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: DOUBLE MAT #5 BAR @ 6" C.C.
E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE
(TYP)

4. KY-206 FRAME & COVER "STORM" SUPPLIED BY
ICAST - FRAME TO BE CAST INTO TOP PHASE TOP
FLANGE SIDE UP

5. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE
ANCHORS FOR PLANT & FIELD HANDLING

6. TOP SURFACE TO RECEIVE FLOATED FINISH

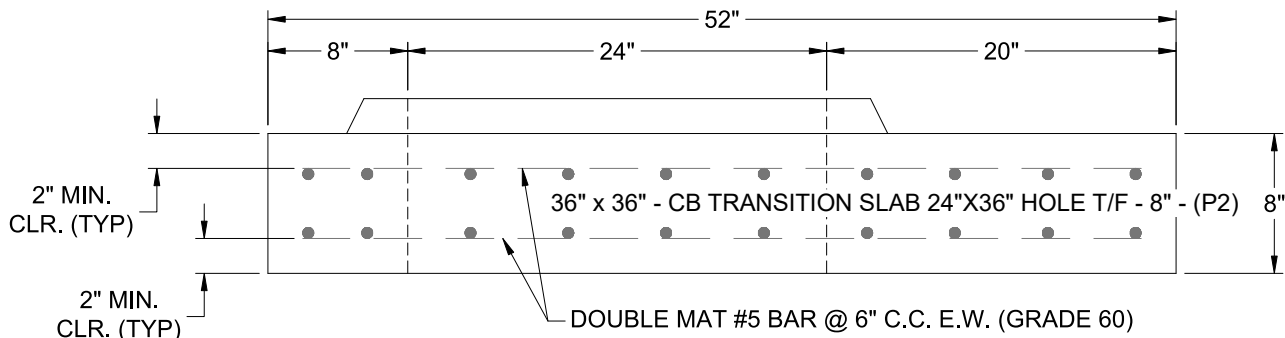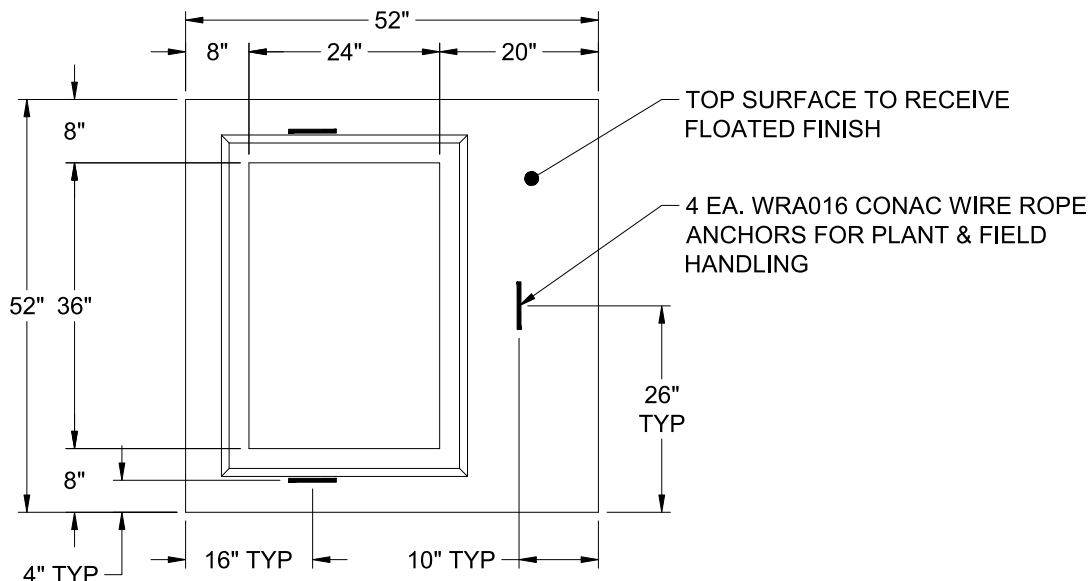

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1235 lb
Volume (Net): 0.32cu.yd
