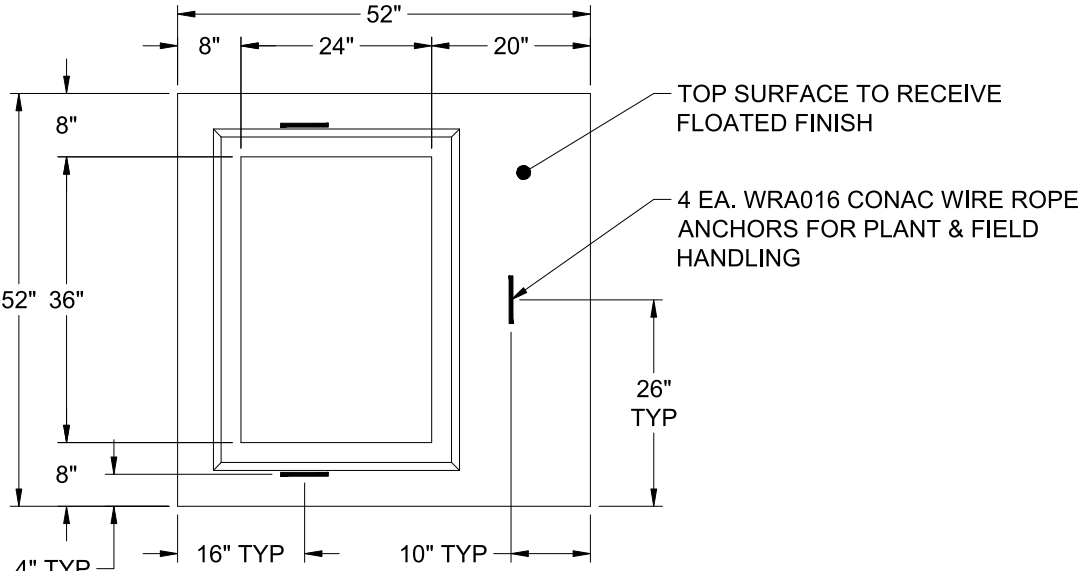
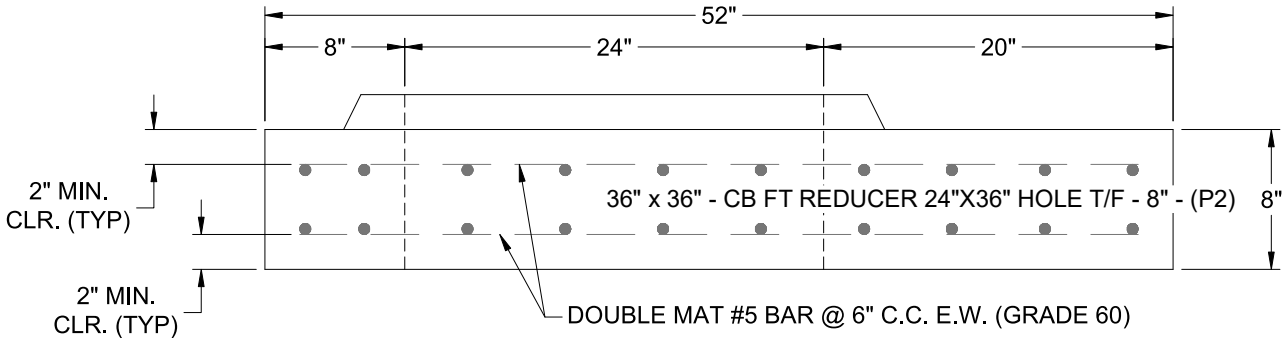


Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt		Plant: 100 6/4/2026 4:55:40 PM	Tech: Jared - A PC: J. Jarvis	
Structure ID: 537				
P2 BX036036-08TS024036		CB FT REDUCER 24"X36" HOLE T/F		
P4) 24" x 60" - CB INLET KY A 5' TOP SAG F/G - 10" P3) 24" x 60" - CB INLET KY A 5' BOTTOM SAG T/G - 18" P2) 36" x 36" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 47" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 32 1) Hole - 24 2) Hole - 8		1895 lb 2670 lb 1235 lb 5883 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 11889 lb	<u>Structure Notes:</u> ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. KY-206 FRAME & COVER "STORM" SUPPLIED BY iCAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP 5. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING 6. TOP SURFACE TO RECEIVE FLOATED FINISH	
				
				
Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 1235 lb Volume (Net): 0.32cu.yd
