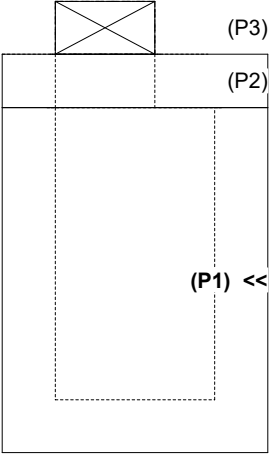
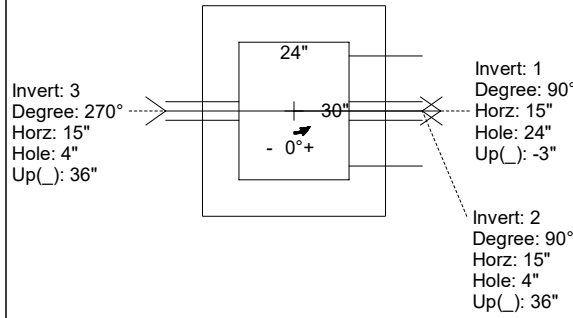
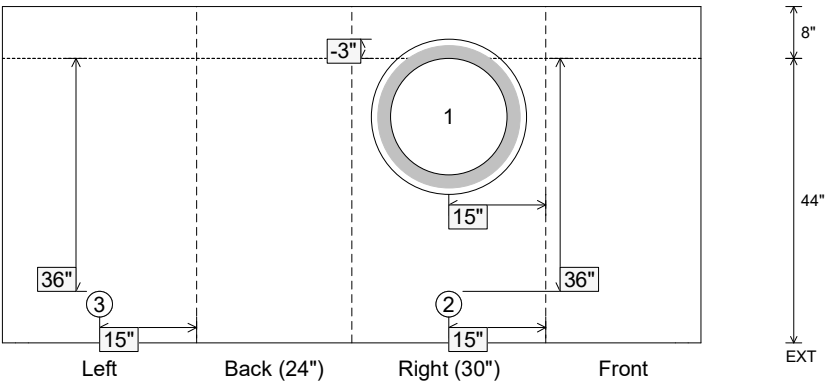


Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 6/5/2026 9:03:59 AM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 544											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 24 2) Hole - 4 Structure Total: 6250 lb						Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TY 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-230G FRAME & GRATE SUPPLIED BY ICAST - POURED IN PLACE BY OTHERS					
Rim: 833.62' Rim to Invert: 5' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	828.62'	90°	23"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2	831.62'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 3	831.62'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 44" Height (Ext): 52"		Weight (Net): 5050 lb Volume (Net): 1.29cu.yd		
