



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt				Plant: 100 6/4/2026 4:53:21 PM		Tech: Jared - A PC: J. Jarvis						
Structure ID: 547												
P1 BX2436-08BVF				BOX BASE 8inW, 8inF, Variable Ht T/n								
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 33" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 24 2) Hole - 8						3398 lb 5270 lb 4392 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 13266 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 832.68' Rim to Invert: 5.09' Slack: 0.08" Sump: 0" Step Position:												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	827.59'	270°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"		
Invert 2	829.51'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	0"		
Invert 3	829.51'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

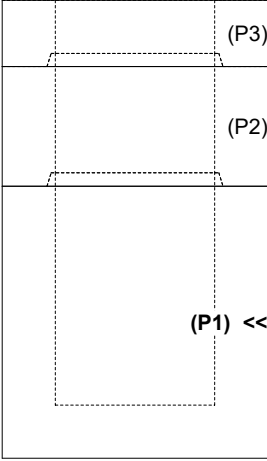


(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

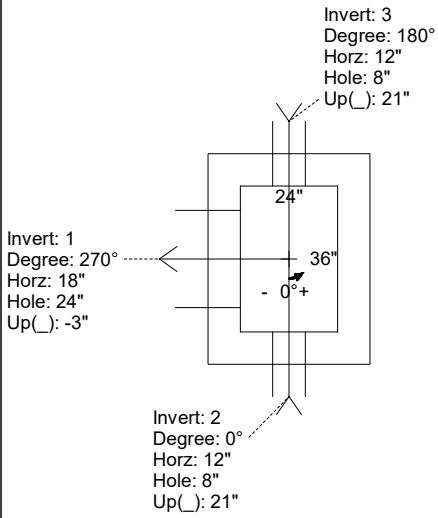

INSIDE WALL DIMENSIONS

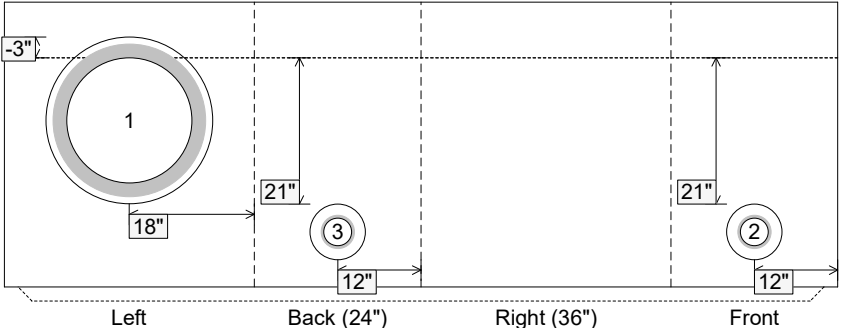

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4392 lb Volume (Net): 1.12cu.yd
----------------------------------	---------------------------------	--	--	--
