



Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 6/4/2026 4:52:25 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 558											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 33" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 2) Hole - 8					3398 lb 5270 lb 4089 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 12962 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 838.54' Rim to Invert: 5.09' Slack: 0.08" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	833.45'	270°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2	833.45'	90°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 3	835.37'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	0"	
Invert 4	835.37'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

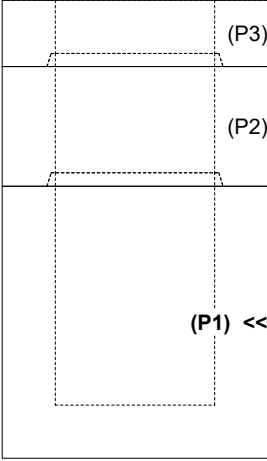

UPSIDE-DOWN VIEW (int. dimensions)

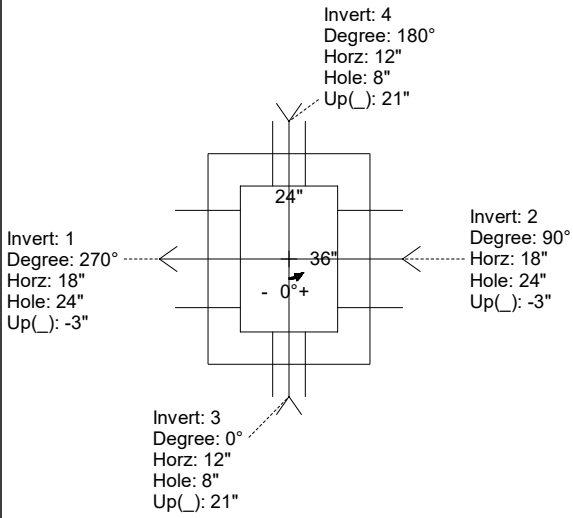

INSIDE WALL DIMENSIONS

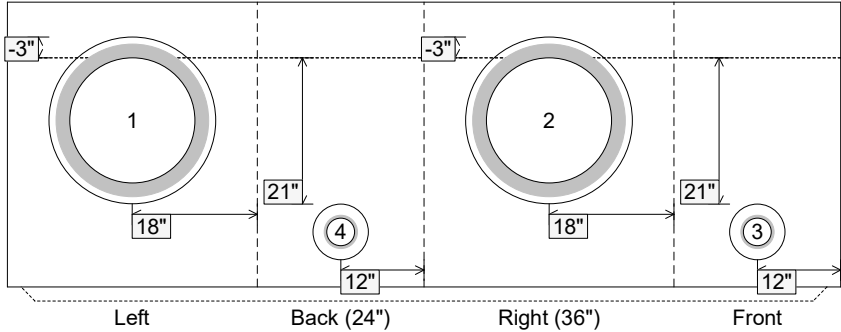

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4089 lb Volume (Net): 1.04cu.yd
----------------------------------	---------------------------------	--	--	--
