




Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt				Plant: 100 6/4/2026 4:50:59 PM		Tech: Jared - A PC: J. Jarvis						
Structure ID: 567												
P1 BX2436-08BVF				BOX BASE 8inW, 8inF, Variable Ht T/n								
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - BOX RISER 8inW T/G - 24" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 40" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 20 2) Hole - 8						3398 lb 5270 lb 2381 lb 4660 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY iCAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 854.04' Rim to Invert: 7.67' Slack: 0.04" Sump: 0" Step Position:												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	846.37'	90°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"		
Invert 2	846.37'	270°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"		
Invert 3	846.37'	0°	20"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

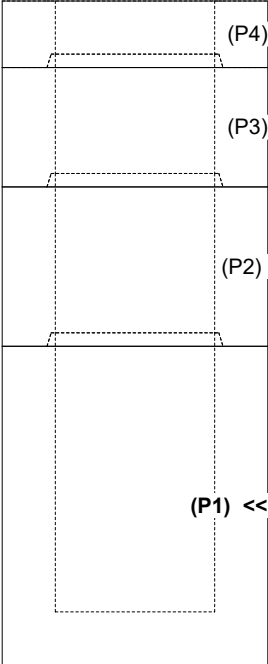

UPSIDE-DOWN VIEW (int. dimensions)

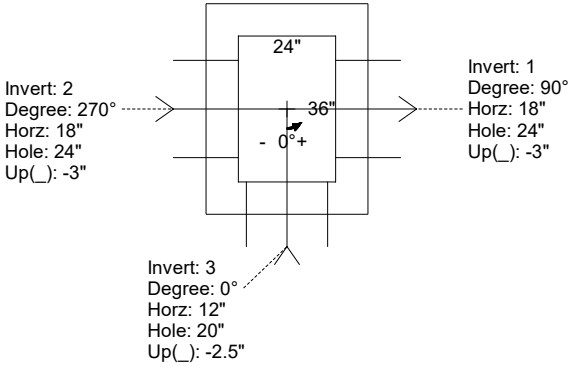

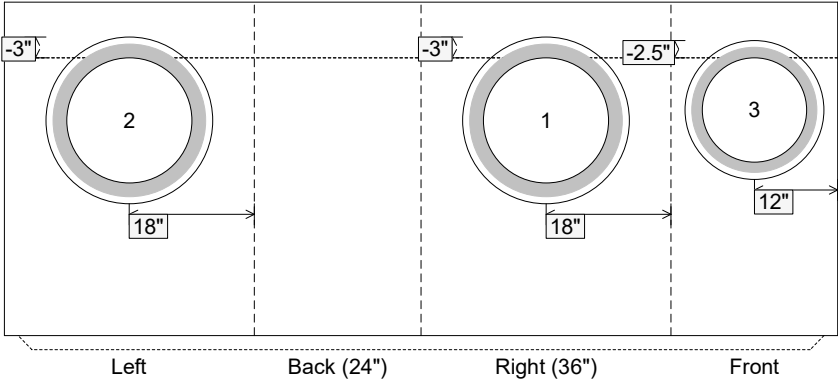INSIDE WALL DIMENSIONS			
			
Left	Back (24")	Right (36")	Front

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 4660 lb Volume (Net): 1.19cu.yd
----------------------------------	---------------------------------	--	--	--
