

Contractor: The Allen Company, Inc.

Plant: 100




Slack: 0.04"

1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS.
2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. NO STEPS.
6. REINFORCING PER ASTM A615 (GRADE 60).
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 24" - CASTING HEIGHT - 5"
P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 51"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 60"
1) CASTING - HOE KY-465 SET (CBI TY F)
2) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 24
1) Hole - 20
1) Hole - 12

0 lb
4382 lb
5684 lb
465 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 10531 lb

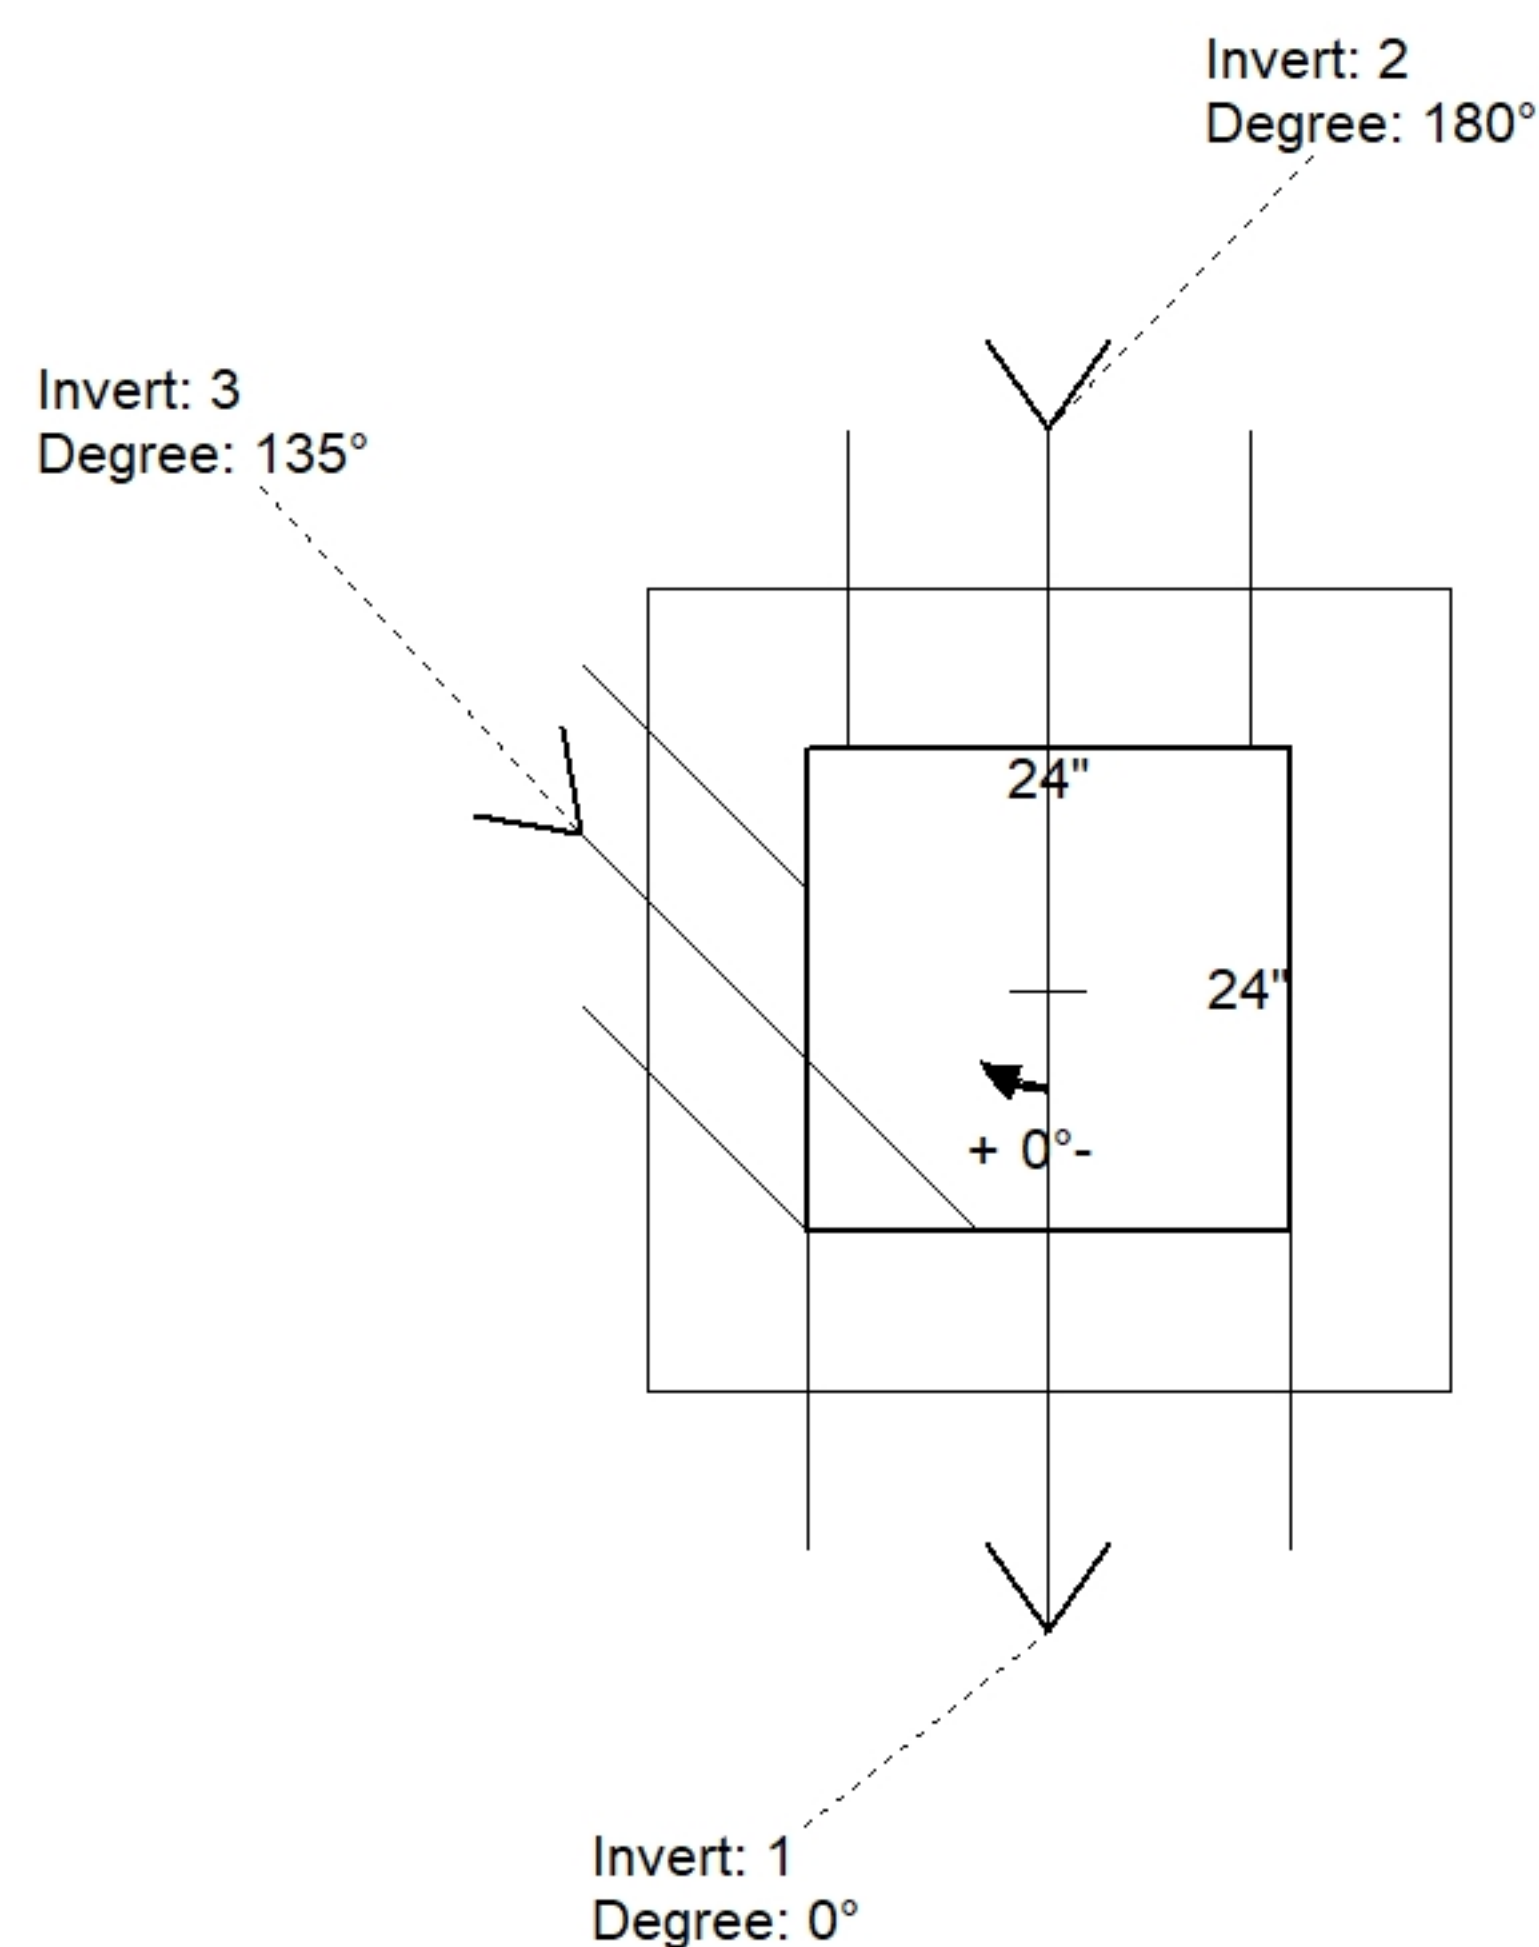

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1006.45'							
Reducer								
Invert 1	996.78'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	996.78'	180°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3	997.38'	135°	8" HDPE	9.1"	12"	Hole 12	6.65"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

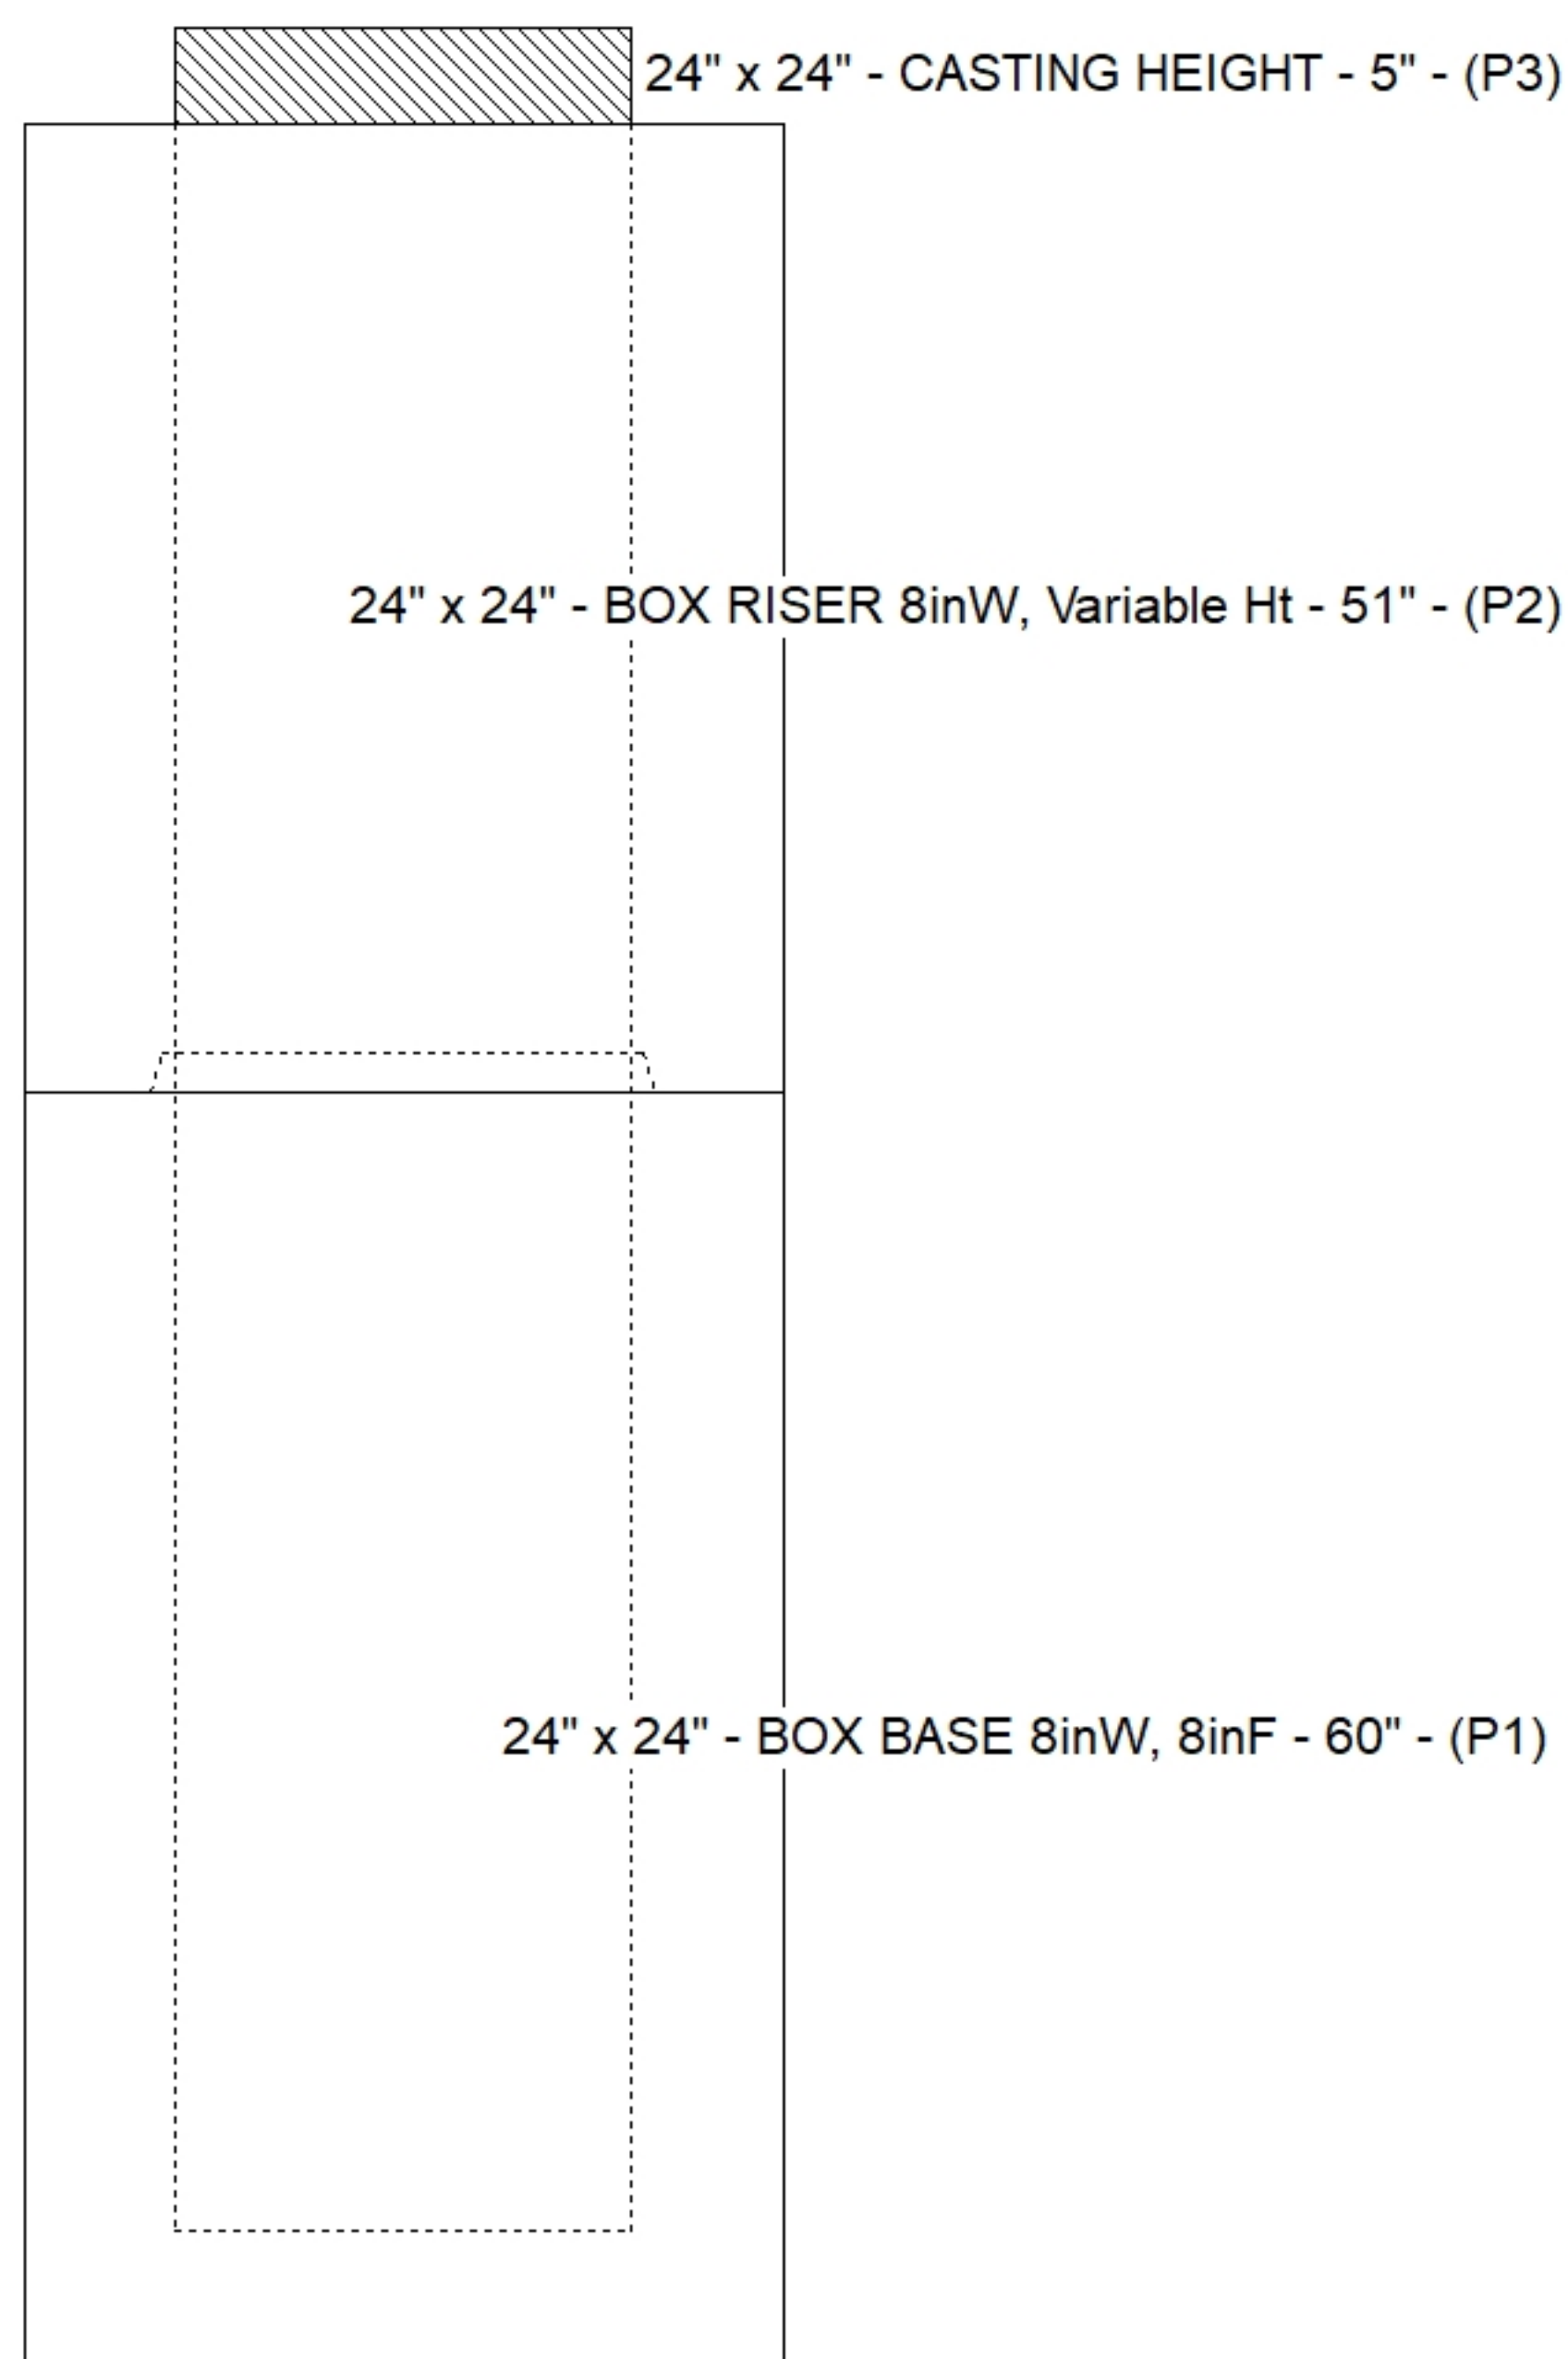

Default - Interior Dimensions

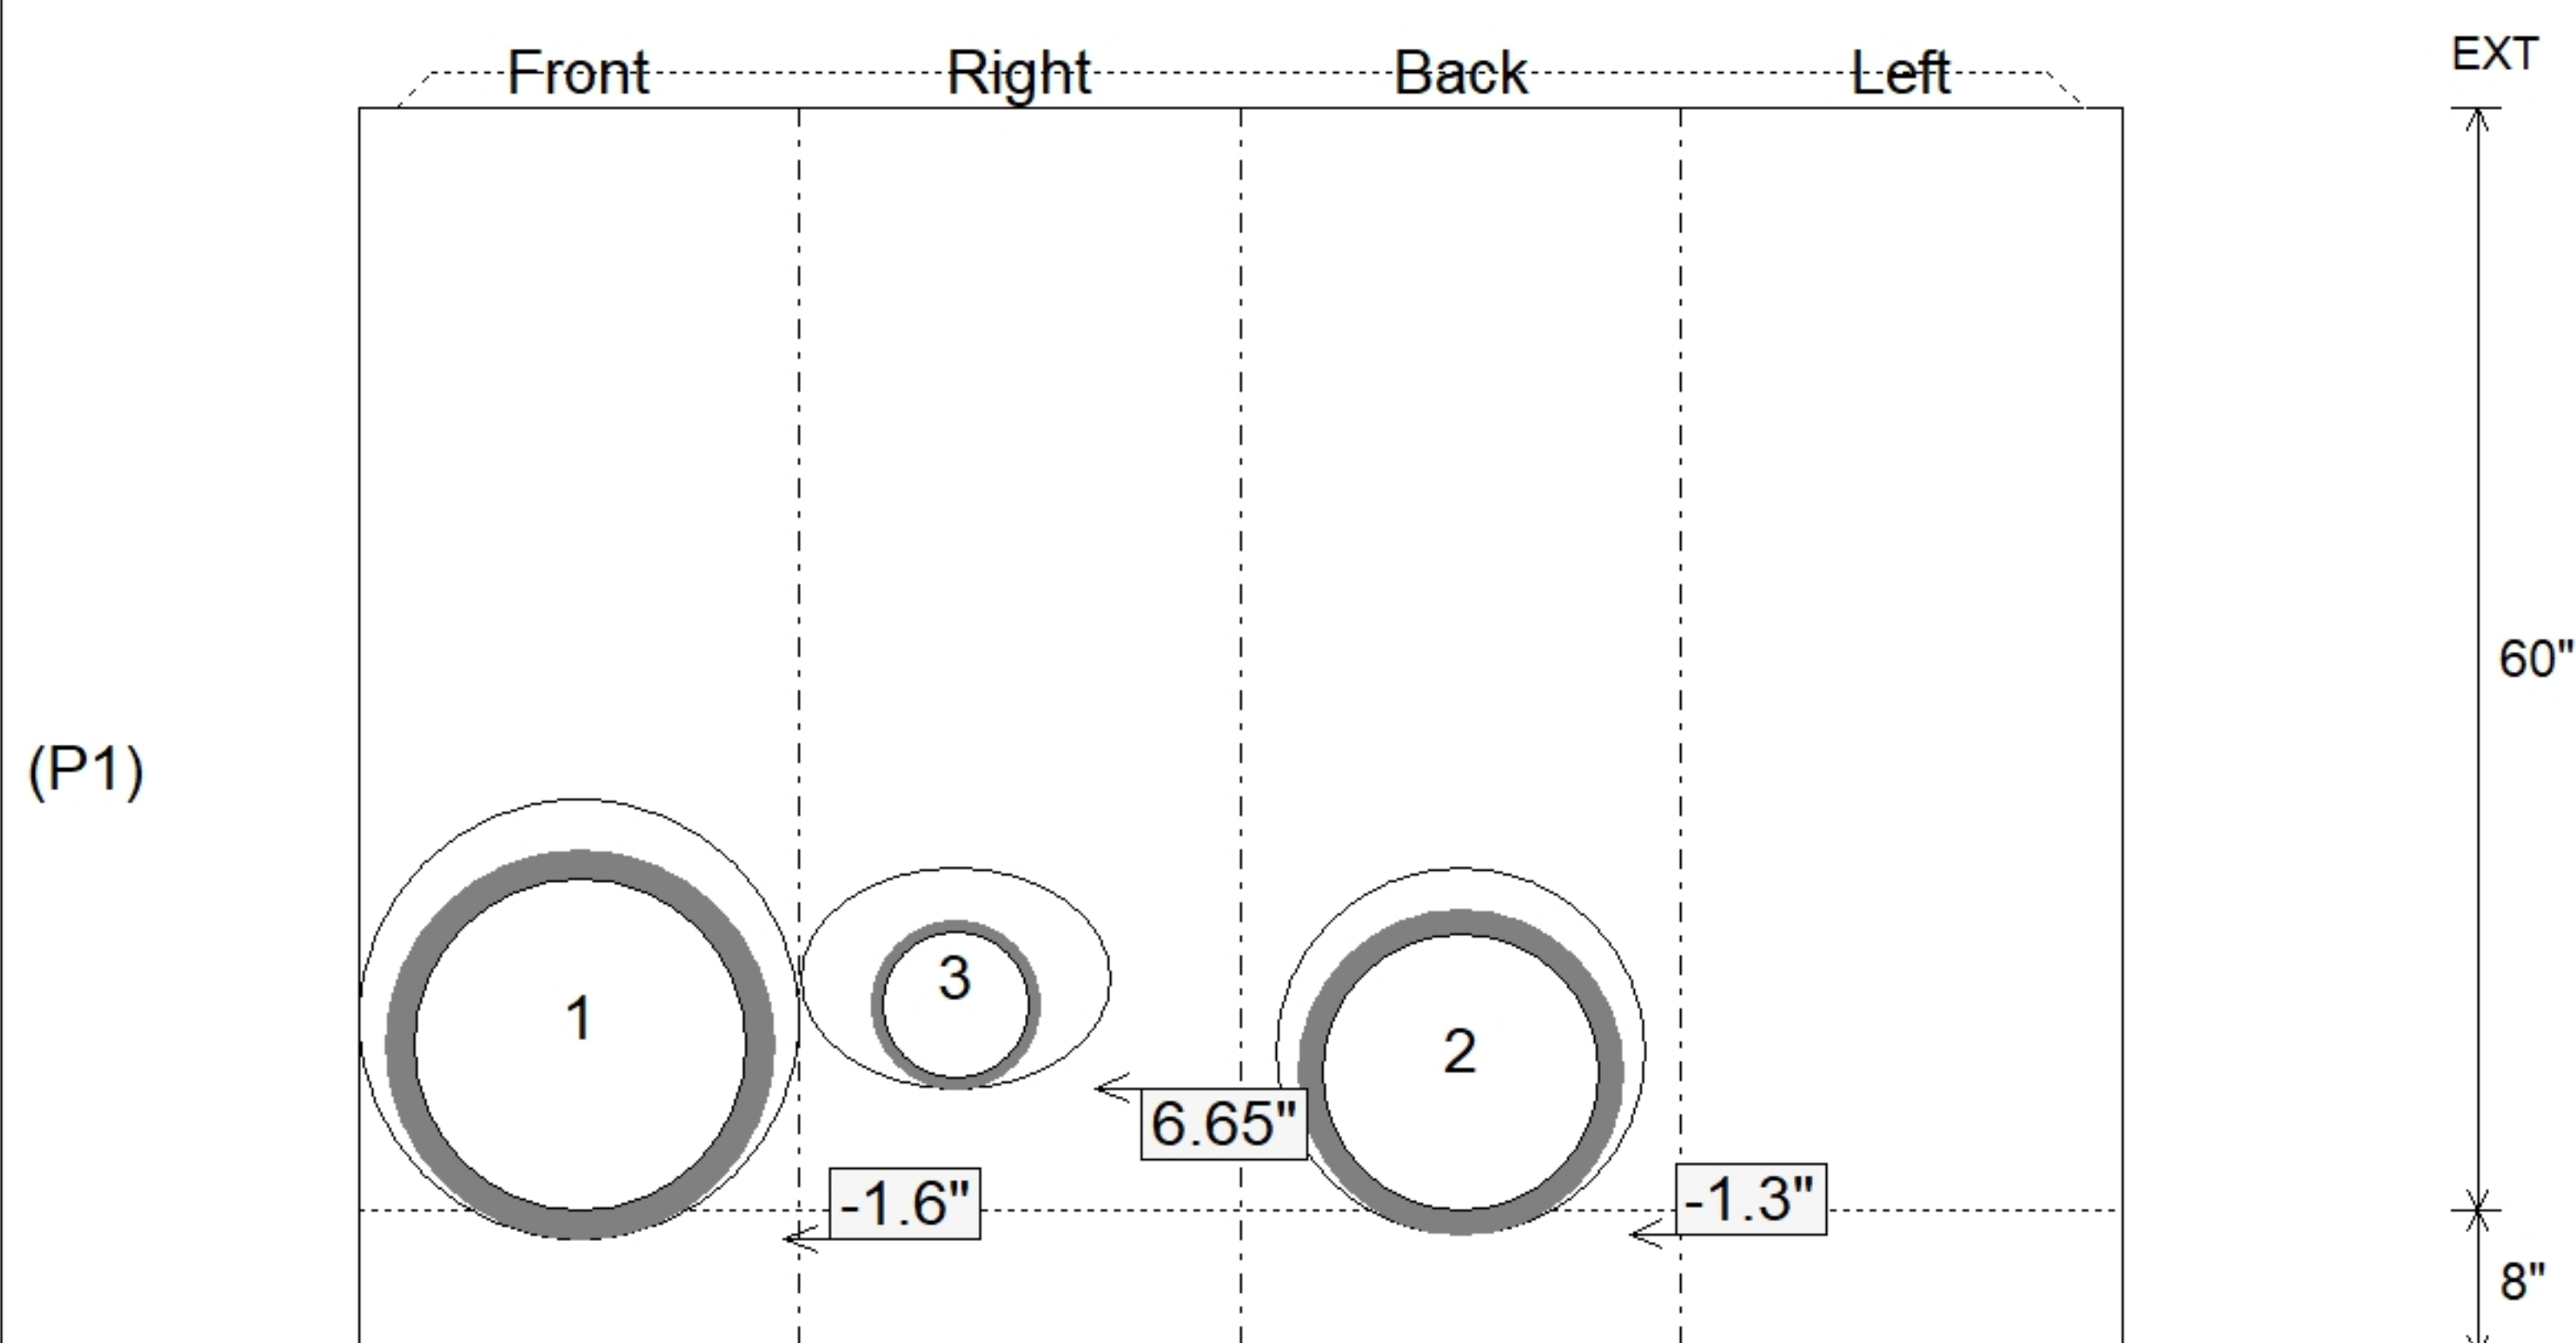

SUBMITTAL
APPROVED BY:
