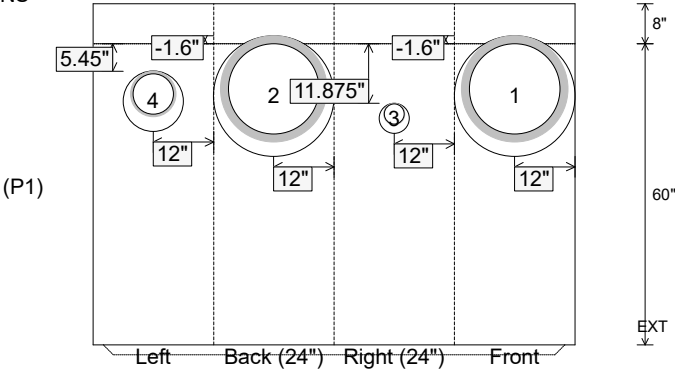
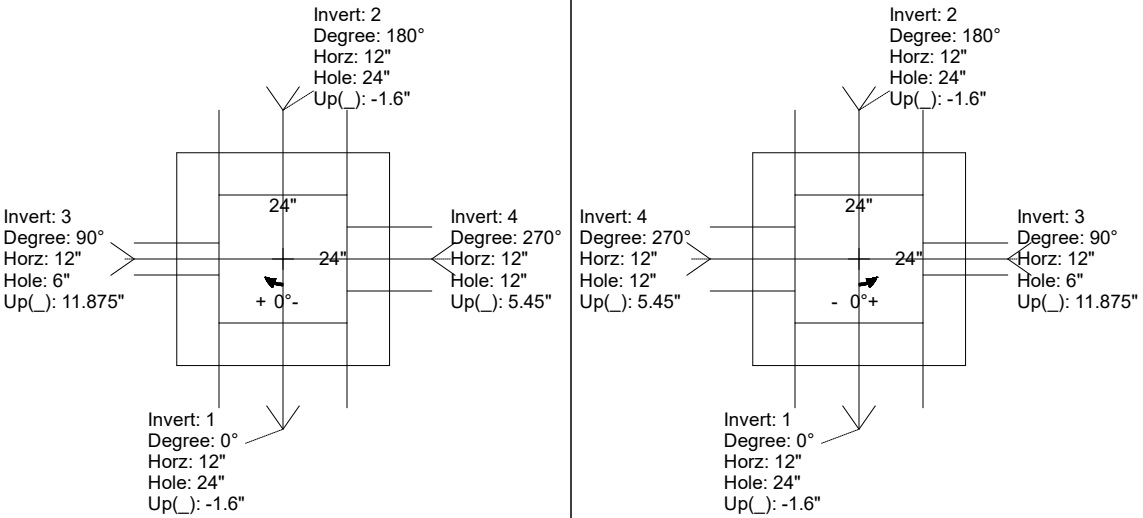
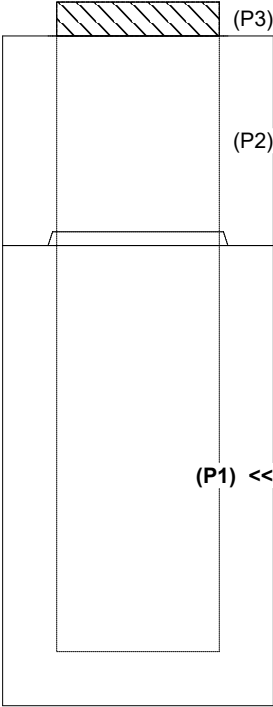


Job Name: 25-3664-Hallmark Communities Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: 100 9/9/2026 2:13:36 PM		Tech: Jared - A PC: Erica Bradley				
Structure ID: CI3											
P1 BX2424-08BA60 BOX BASE 8inW, 8inF											
P3) 24" x 24" - CASTING HEIGHT - 5" P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 31" P1) 24" x 24" - BOX BASE 8inW, 8inF - 60" 1) CASTING - HOE KY-465 SET (CBI TY F) 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 6 1) Hole - 12						0 lb 2664 lb 5679 lb 465 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8808 lb		Structure Notes: 1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS. 2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. NO STEPS. 6. REINFORCING PER ASTM A615 (GRADE 60). - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1016'		Rim to Invert: 8'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1008'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-1.6"	0"	
Invert 2	1008'	180°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-1.6"	0"	
Invert 3	1009'	90°	20"	4" PVC SDR35	4.25"	Hole 6	6"	6"	11.875"	0"	
Invert 4	1008.5'	270°	20"	8" HDPE	9.1"	Hole 12	12"	12"	5.45"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions) INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 60" Height (Ext): 68"		Weight (Net): 5679 lb Volume (Net): 1.45cu.yd		
