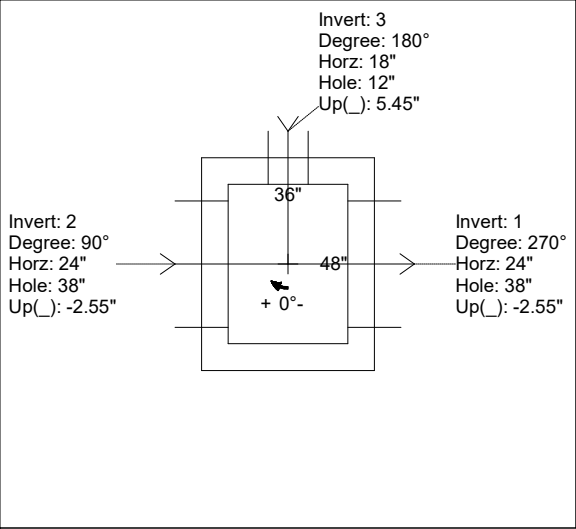
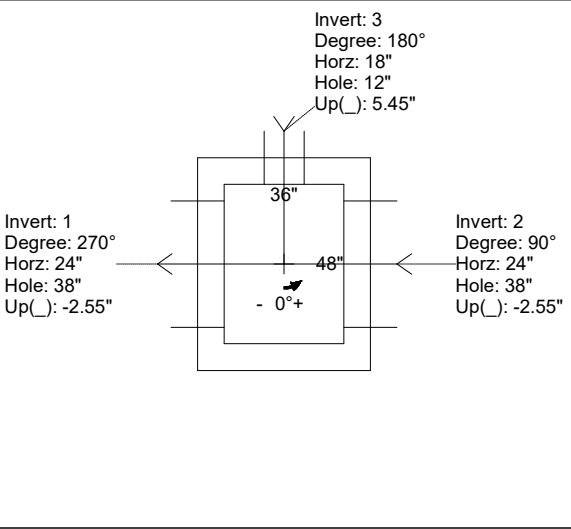
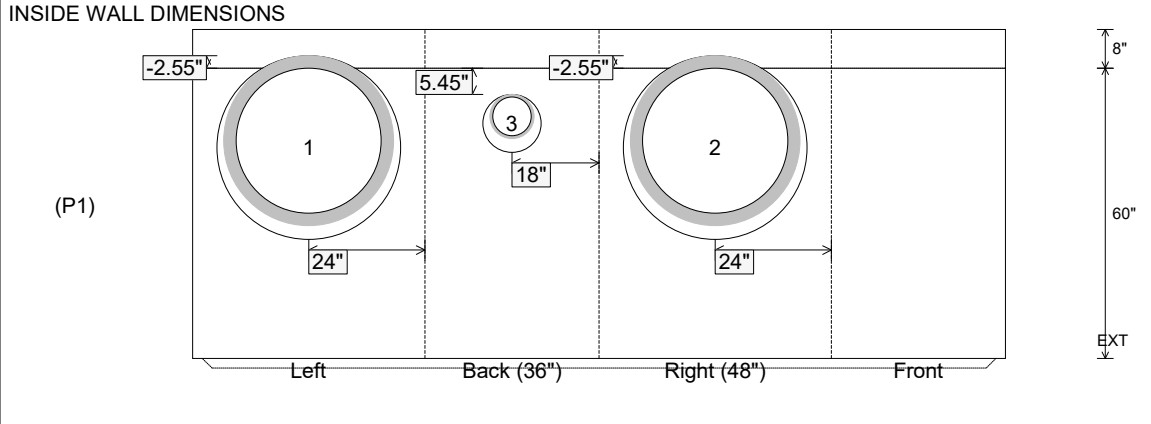


Job Name: 25-3664-Hallmark Communities Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: 100 9/9/2026 2:13:24 PM		Tech: Jared - A PC: Erica Bradley					
Structure ID: CI6												
P1 BX3648-08BA60 BOX BASE 8inW, 8inF												
P4) 24" x 24" - CASTING HEIGHT - 5" P3) 36" x 48" - CB FT REDUCER 24"x24" HOLE - 8" P2) 36" x 48" - BOX RISER 8inW, Variable Ht - 32" P1) 36" x 48" - BOX BASE 8inW, 8inF - 60" 1) CASTING - HOE KY-465 SET (CBI TY F) 2) 36" x 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 38" 1) Hole - 12"					0 lb 1847 lb 4296 lb 8691 lb 465 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 15300 lb		Structure Notes: 1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS. 2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. NO STEPS. 6. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W - RISER/WALLS (As .18) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 1004.4'					Rim to Invert: 8.75'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	995.65'	270°	32"	30" HDPE	35.1"	Hole 38	38"	38"	-2.55"	0"		
Invert 2	995.65'	90°	32"	30" HDPE	35.1"	Hole 38	38"	38"	-2.55"	0"		
Invert 3	996.15'	180°	26"	8" HDPE	9.1"	Hole 12	12"	12"	5.45"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 												
INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Tongue Seam Dn: n/a Wall Thickness: 8" Floor Height: 8" Height (Int): 60" Height (Ext): 68" Weight (Net): 8691 lb Volume (Net): 2.22cu.yd												
