

Job Name: 25-4288 - Project Wave

Job Location: Franklin, KY 42134

Contractor: Cumberland Pipeline LLC

Plant: 100

7/10/2026 8:14:26 AM

Tech: Jared - A

PC: Erica Bradley



Structure ID: A10

P2 MH048RS60X

MH RISER w/XYPEX

P6) 24" - CASTING HEIGHT - 7"

P5) 24" - XYPEX GRADE RING - 3"

P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 36"

P3) 48" - MH RISER w/XYPEX - 60"

P2) 48" - MH RISER w/XYPEX - 60"

P1) 48" - MH BASE w/XYPEX - 24"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT

1) CASTING - JBS 1150 F/C SANITARY

3) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-08 NYLO

15) MH Step ML-10-TDS-NCR - 10"

0 lb

202 lb

2251 lb

4192 lb

4192 lb

2911 lb

0 lb

0 lb

1440 lb

250 lb

0 lb

0 lb

16 lb

0 lb

Structure Total: 15454 lb

Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: PER ASTM A615

4. INVERT CHANNEL REQUIRED

5. STEPS AT 0 DEGREES

6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST

Rim: 726.26'

Rim to Invert: 15.74'

Slack: 0.88"

Sump: 2"

Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

(P6)

(P5)


(P4)

(P3)

(P2) <<


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

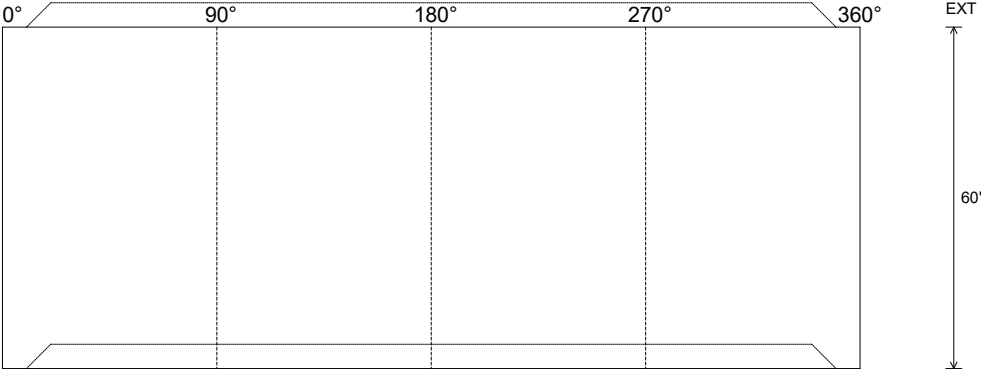

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 5"

Floor Height: 0"

Height (Int): 60"

Height (Ext): 60"

Weight (Net): 4192 lb

Volume (Net): 1.07cu.yd
