




Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:14:30 AM		Tech: Jared - A PC: Erica Bradley						
Structure ID: A13.2													
P2		MH048RS36X		MH RISER w/XYPEX									
P5) 24" - CASTING HEIGHT - 7" P4) 24" - XYPEX GRADE RING - 4" P3) 48" - ECC XYPEX CONE w/ 24" HOLE - 24" P2) 48" - MH RISER w/XYPEX - 36" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"						0 lb 270 lb 1738 lb 2515 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- 9140 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST					
Rim: 732.04' Rim to Invert: 7.82' Slack: 0.84" Sump: 2" Step Position: 0°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

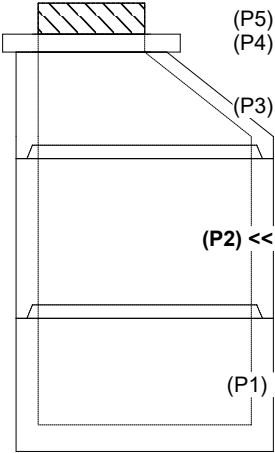

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 2515 lb Volume (Net): 0.64cu.yd
----------------------------------	------------------------------------	--	--	--
