

Job Name: 25-4288 - Project Wave

Job Location: Franklin, KY 42134

Contractor: Cumberland Pipeline LLC

Plant: 100

7/10/2026 8:14:31 AM

Tech: Jared - A

PC: Erica Bradley



Structure ID: A14


P3 MH048RS60X

MH RISER w/XYPEX

P5) 24" - CASTING HEIGHT - 7"					0 lb	<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST
P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 30"					1981 lb	
P3) 48" - MH RISER w/XYPEX - 60"					4192 lb	
P2) 48" - MH RISER w/XYPEX - 60"					4192 lb	
P1) 48" - MH BASE w/XYPEX - 24"					2863 lb	
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212					0 lb	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)					0 lb	
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT					1440 lb	
1) CASTING - JBS 1150 F/C SANITARY					250 lb	
3) 48" - Conseal CS-102 1.00" (Double)					0 lb	
1) 24" - Conseal CS-102 1.00" (Double)					0 lb	
2) PSX - 12-08 NYLO					16 lb	
1) PSX - 12-06 NYLO					8 lb	
15) MH Step ML-10-TDS-NCR - 10"					0 lb	

Structure Total:					14941 lb	
Rim: 730.91'		Rim to Invert: 14.98'	Slack: 0.76"	Sump: 2"	Step Position: 0°	

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

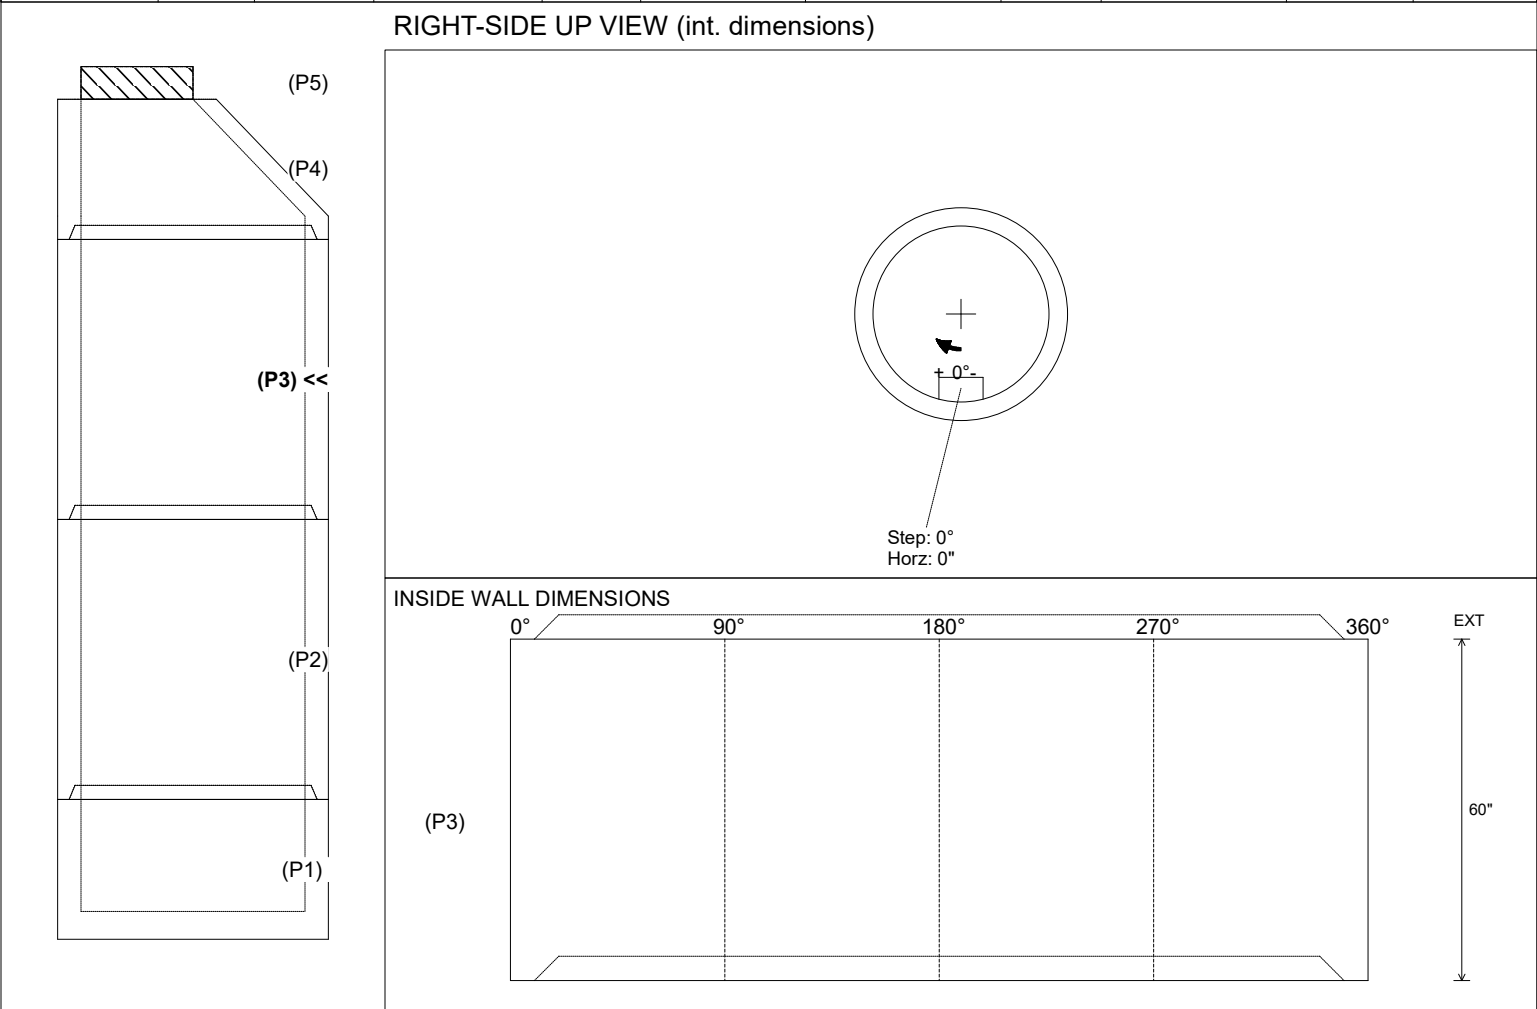

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
---	---	---	---	---
