

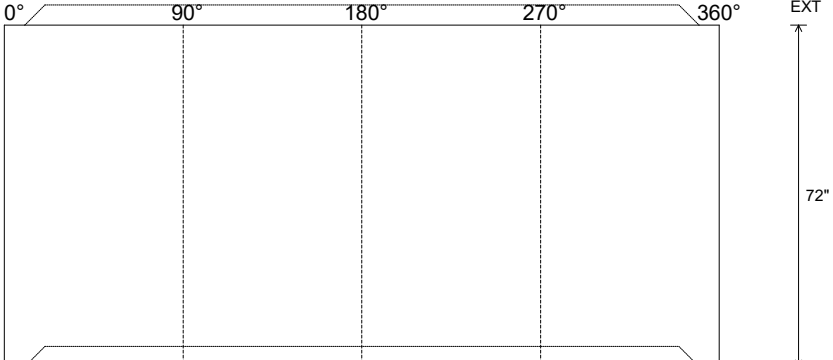


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:14:17 AM		Tech: Jared - A PC: Erica Bradley				
Structure ID: A3											
P2		MH048RS72X									
P7) 24" - CASTING HEIGHT - 7" P6) 24" - XYPEX GRADE RING - 4" P5) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P4) 48" - MH RISER w/XYPEX - 72" P3) 48" - MH RISER w/XYPEX - 72" P2) 48" - MH RISER w/XYPEX - 72" P1) 48" - MH BASE w/XYPEX - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 4) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 23) MH Step ML-10-TDS-NCR - 10"						0 lb 270 lb 1981 lb 5030 lb 5030 lb 5030 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 715.31' Rim to Invert: 23.75' Slack: 0" Sump: 2" Structure Total: 22377 lb Step Position: 0											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
 (P7) (P6) (P5) (P4) (P3) (P2) << (P1) RIGHT-SIDE UP VIEW (int. dimensions)  Step: 0° Horz: 0" INSIDE WALL DIMENSIONS  EXT 72"											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 5030 lb Volume (Net): 1.28cu.yd	
