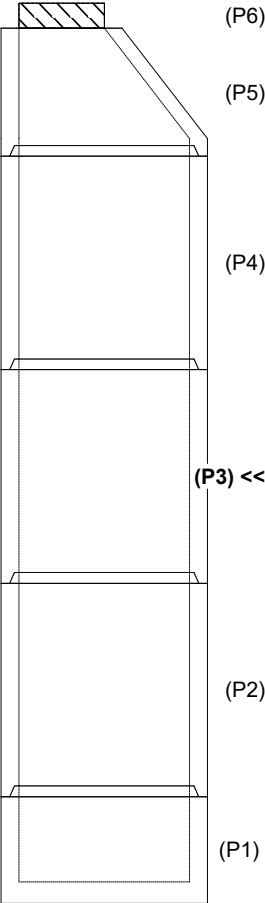

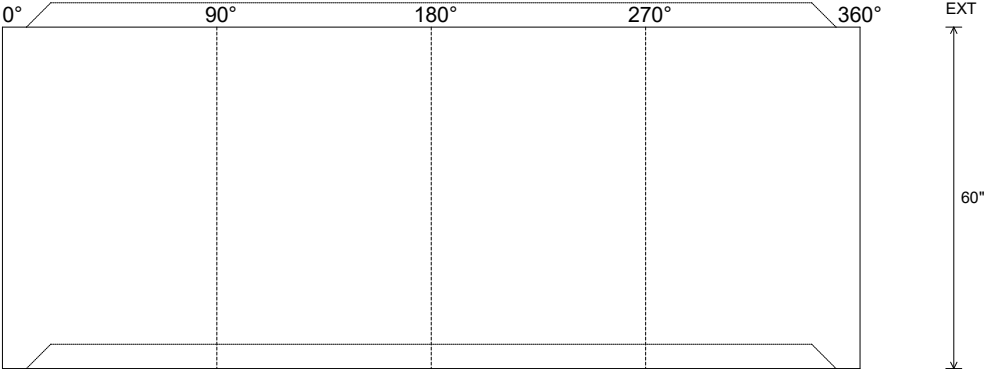


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 7/10/2026 8:14:22 AM		Tech: Jared - A PC: Erica Bradley				
Structure ID: A6											
P3		MH048RS60X									
P6) 24" - CASTING HEIGHT - 7" P5) 48" - ECC XYPEX CONE w/ 24" HOLE - 36" P4) 48" - MH RISER w/XYPEX - 60" P3) 48" - MH RISER w/XYPEX - 60" P2) 48" - MH RISER w/XYPEX - 60" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 4) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 20) MH Step ML-10-TDS-NCR - 10"						0 lb 2251 lb 4192 lb 4192 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- 19443 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 724.62' Rim to Invert: 20.6' Slack: 2.2" Sump: 2" Step Position: 0°						Structure Total: 19443 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 4192 lb Volume (Net): 1.07cu.yd		
