

Contractor: Pace Contracting, LLC

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 5.06'

Floor Height: 8"

Slack: -0.002"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .47) #5 BARS AT 12" C.C.E.W.


P4) 36" x 36" - CASTING HEIGHT - 0"
P3) 60" - MH FLAT TOP w/36"x36" Hatch - 13"
P2) 60" - MH RISER - 60"
P1) 60" - MH BASE Custom Ht - 47"
1) HATCH (Alum.) - HALLIDAY W1S 36"x36"
2) 60" - Conseal CS-102 1.00" (Double)
1) 36" x 36" - Conseal CS-102 1.00" (Double)
2) PSX - 8QRS DD

0 lb
2132 lb
6213 lb
7640 lb
78 lb
0 lb
0 lb
13 lb


Structure Total: 16075 lb

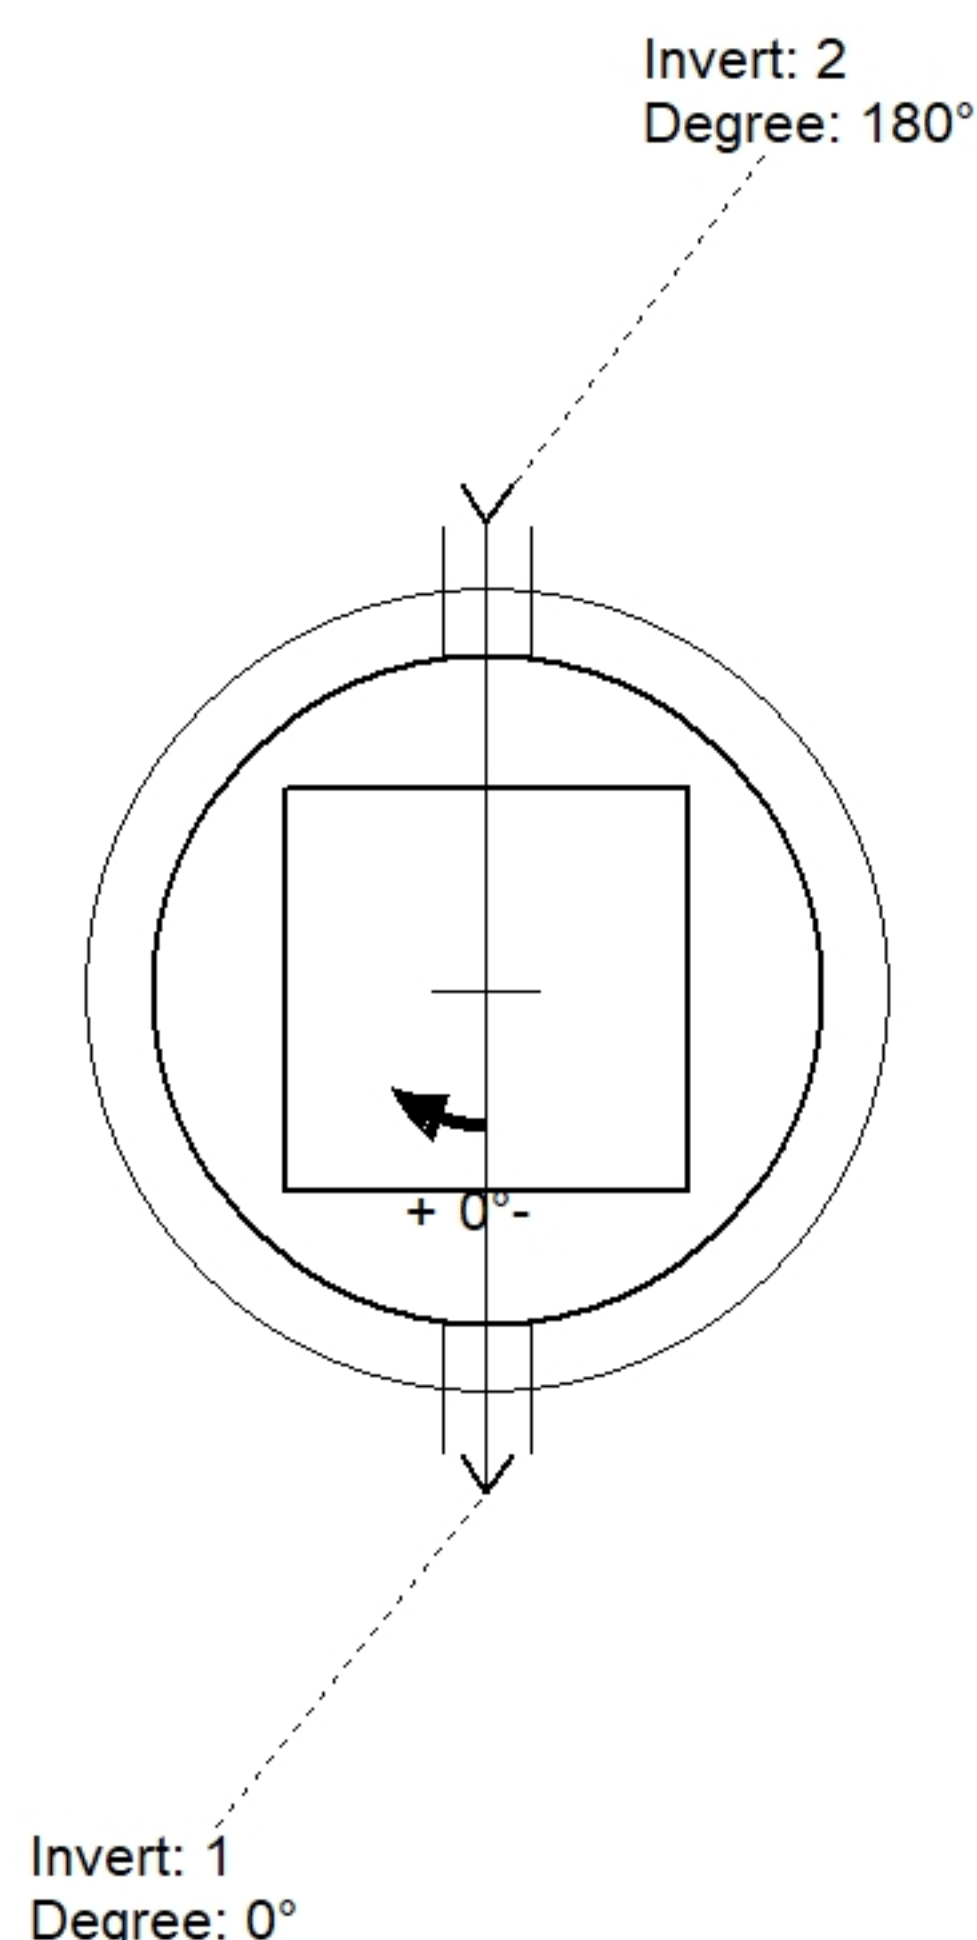

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	454'							
Reducer								
Invert 1	448.94'	0°	4" DI	4.75"	8"	PSX 8QRS DD	5.53"	P2
Invert 2	448.94'	180°	4" DI	4.75"	8"	PSX 8QRS DD	5.53"	P2
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

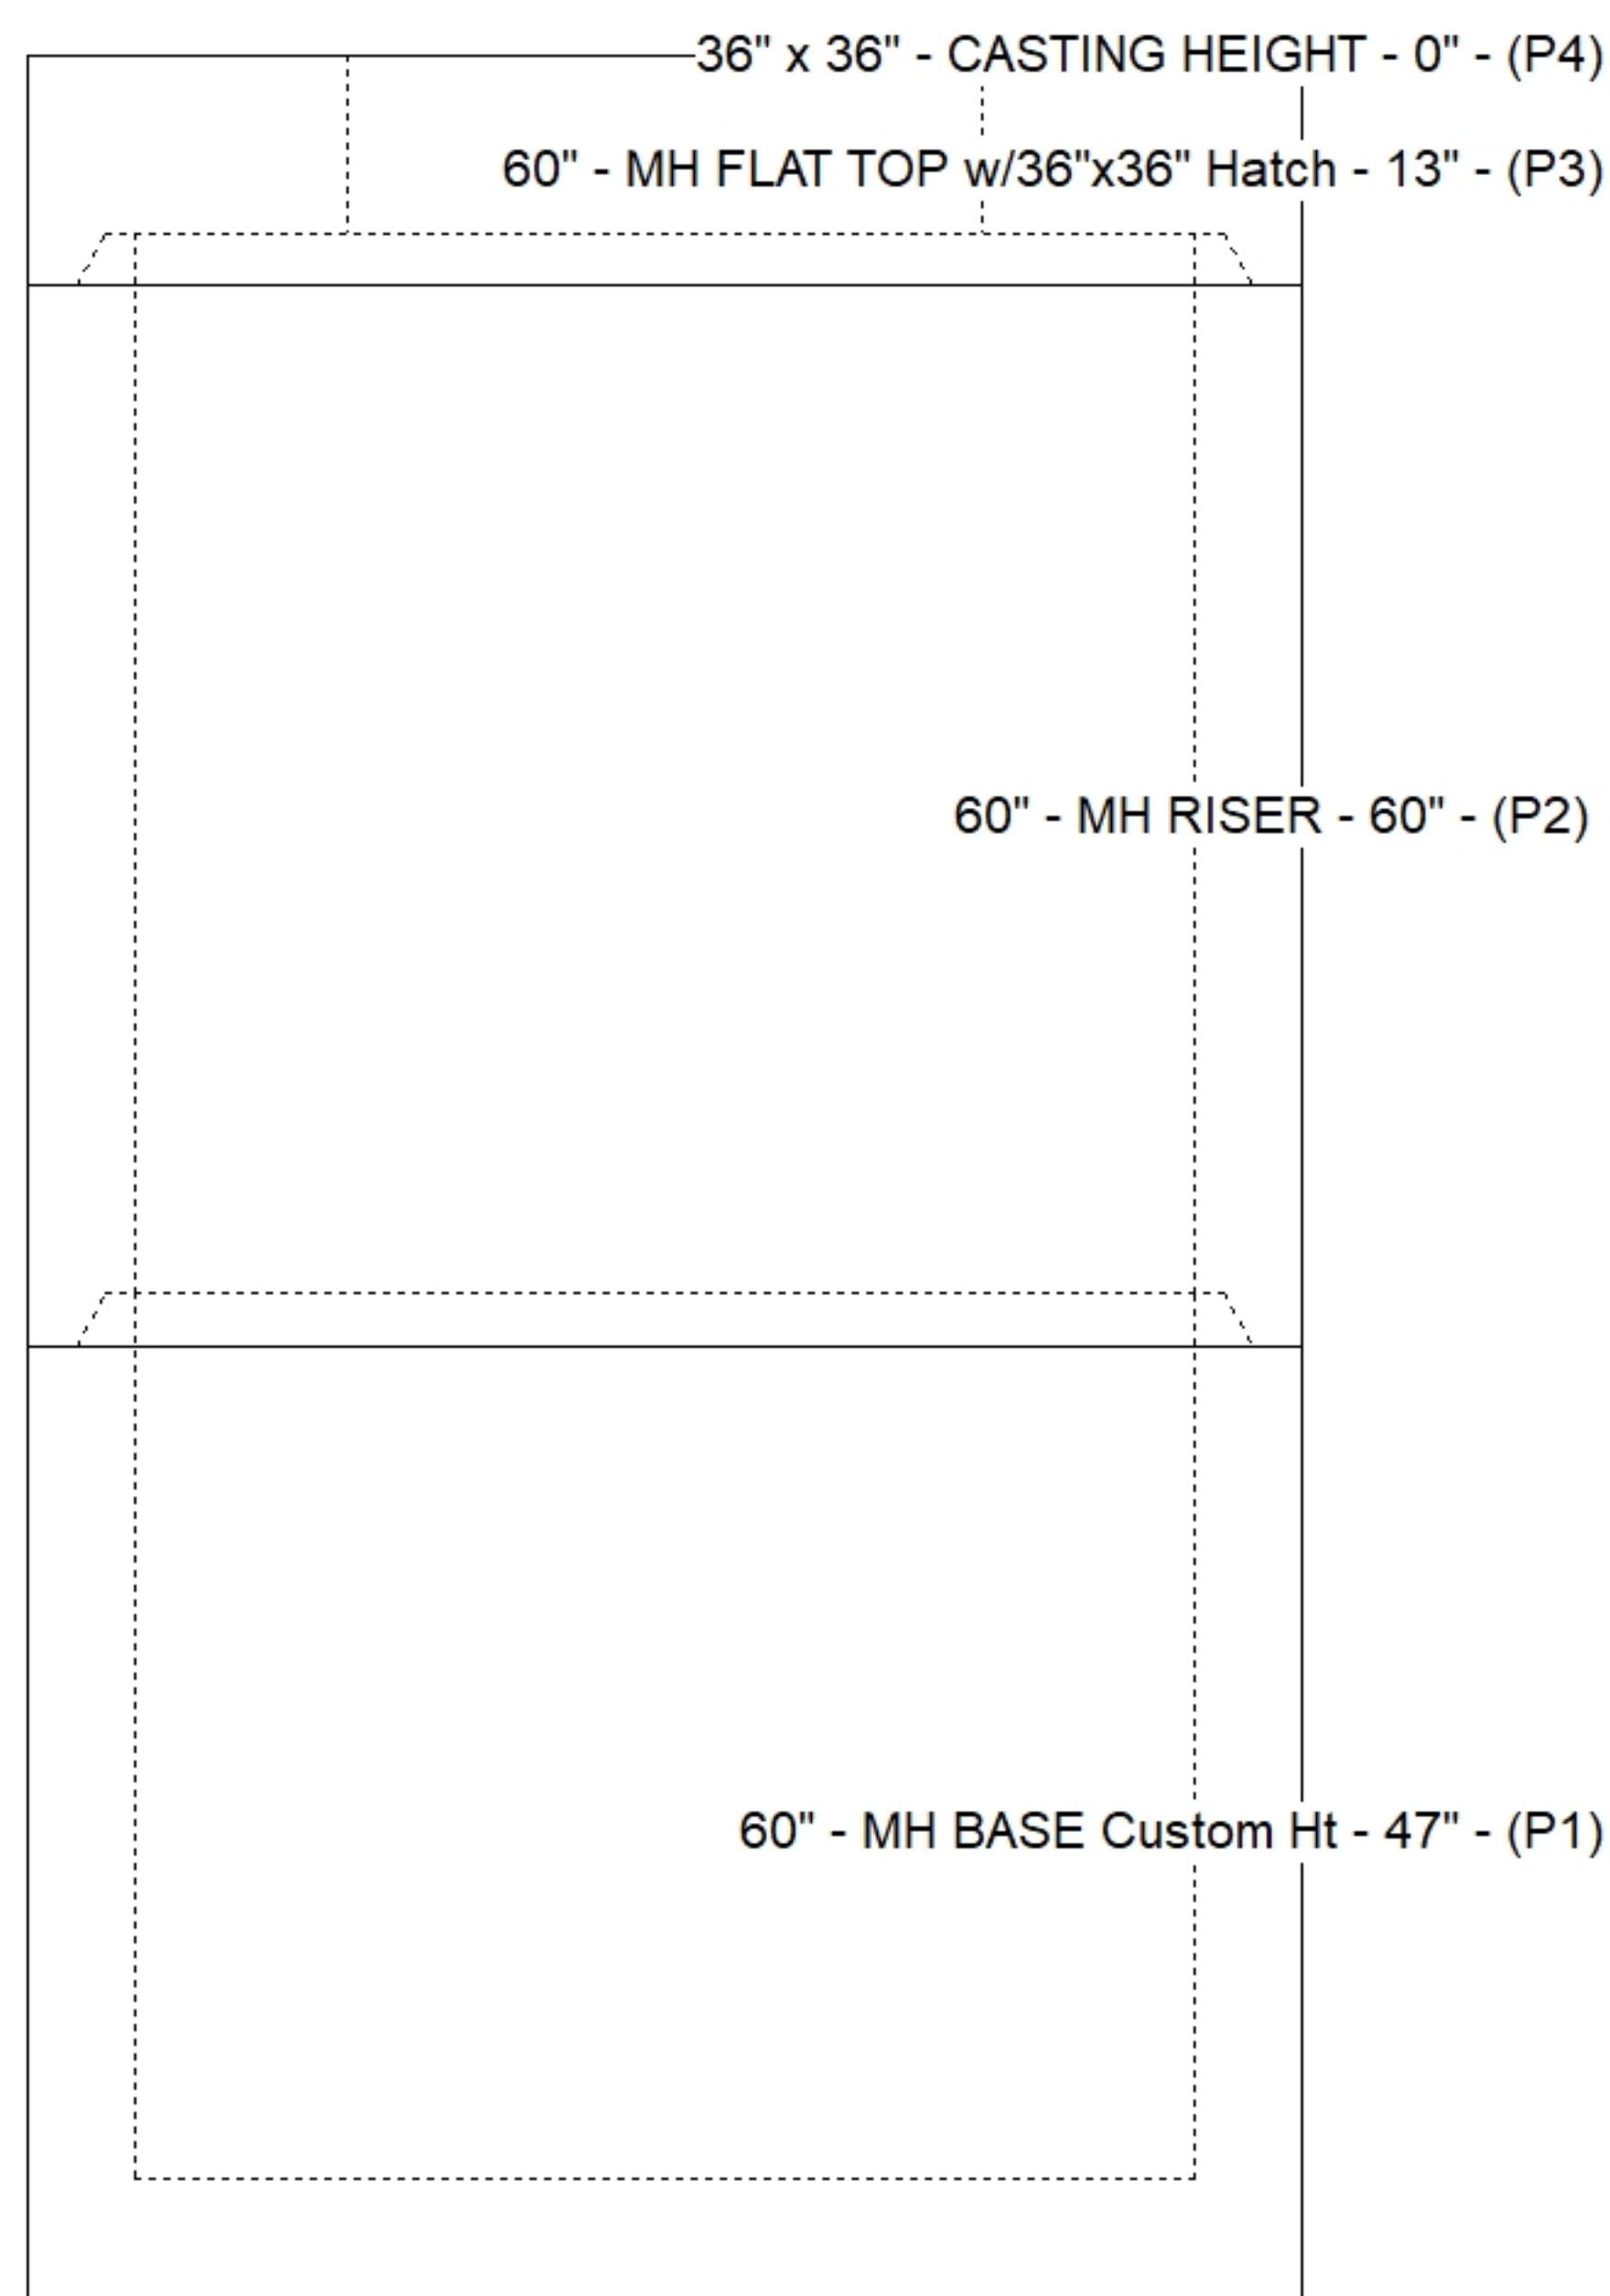

Default - Interior Dimensions

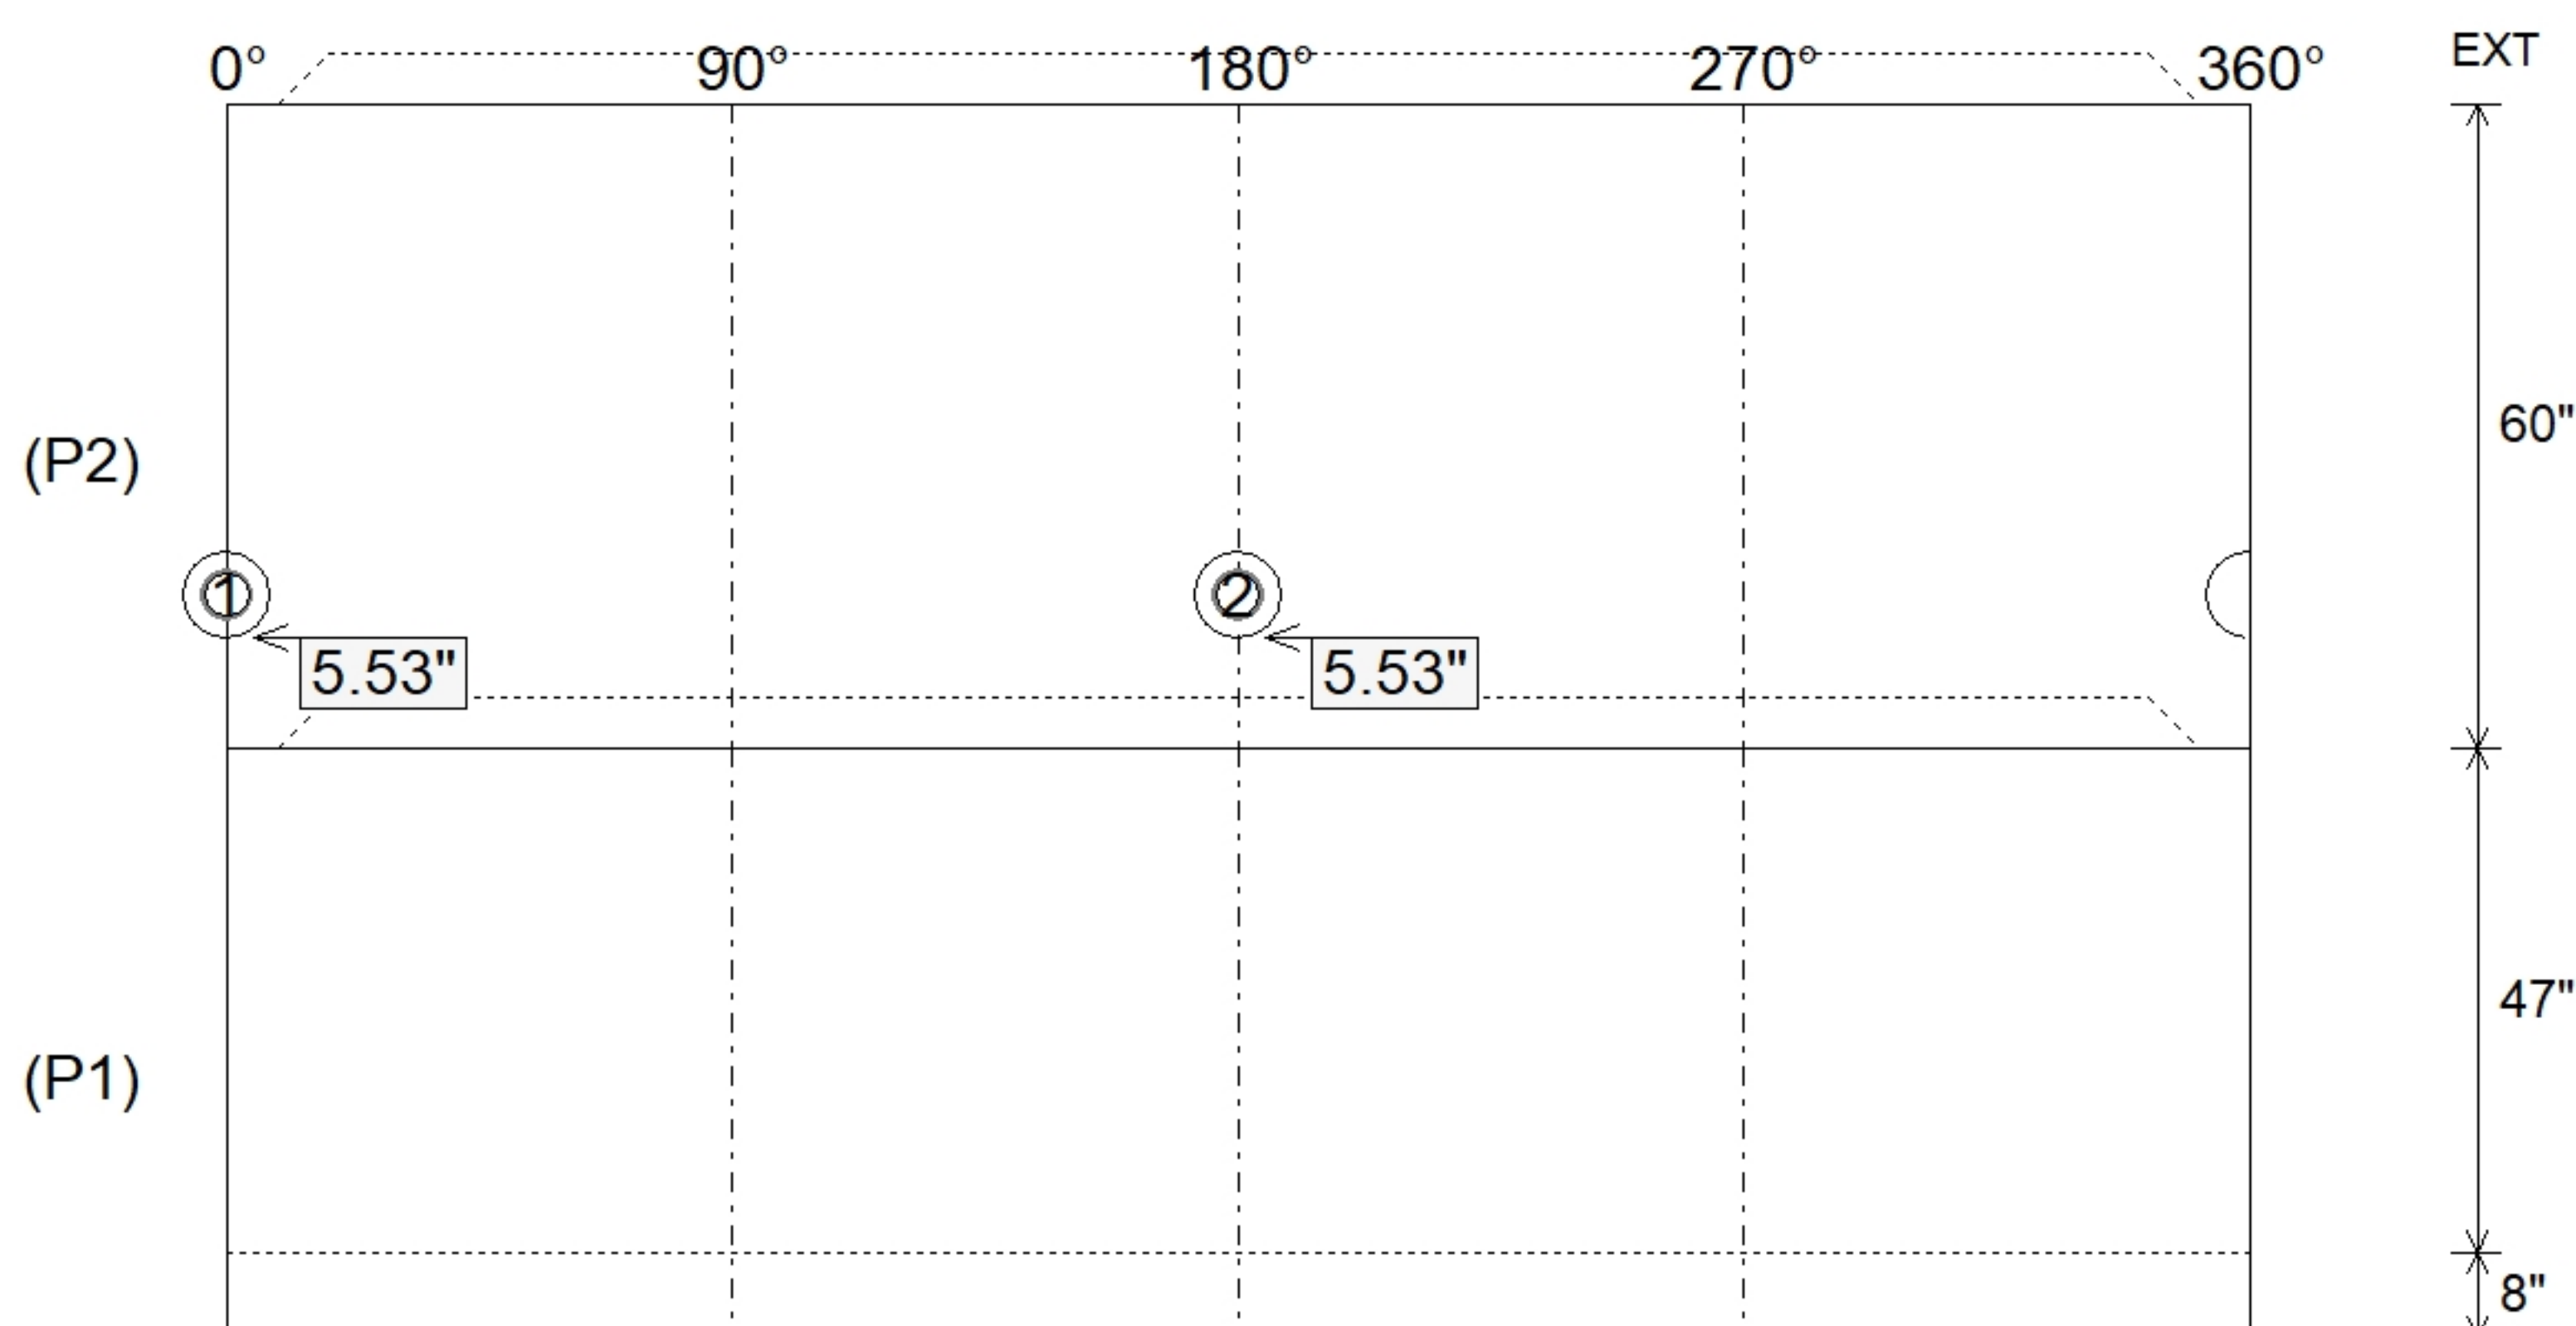

Submittal Drawing
6/8/2026 10:33:46 AM

SUBMITTAL
APPROVED BY:
