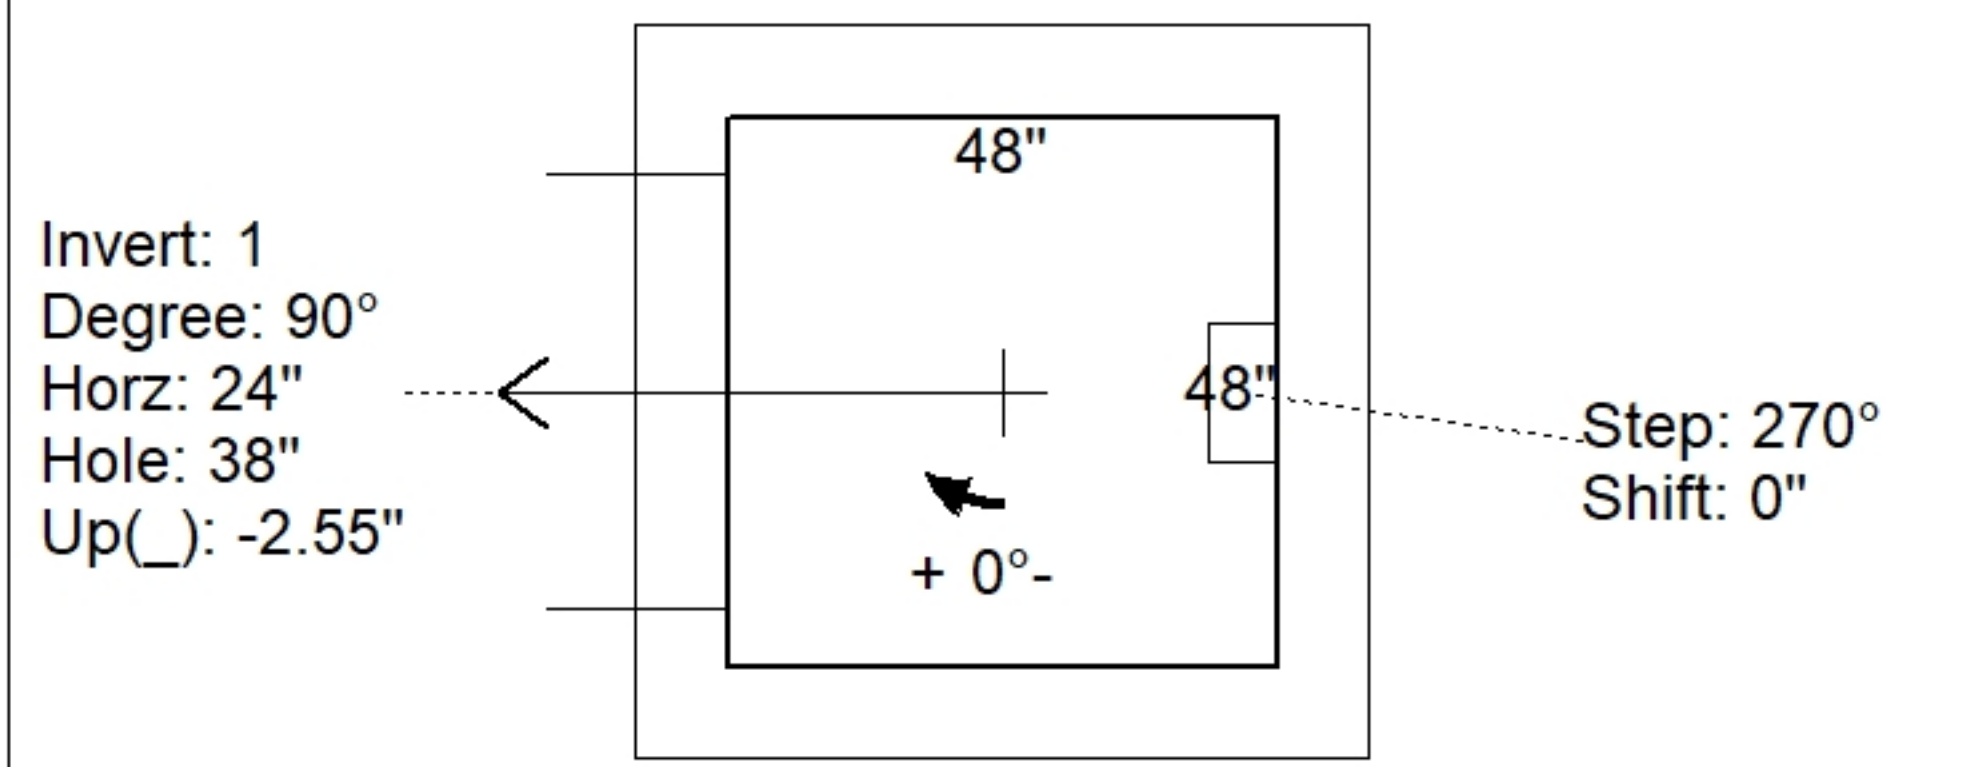
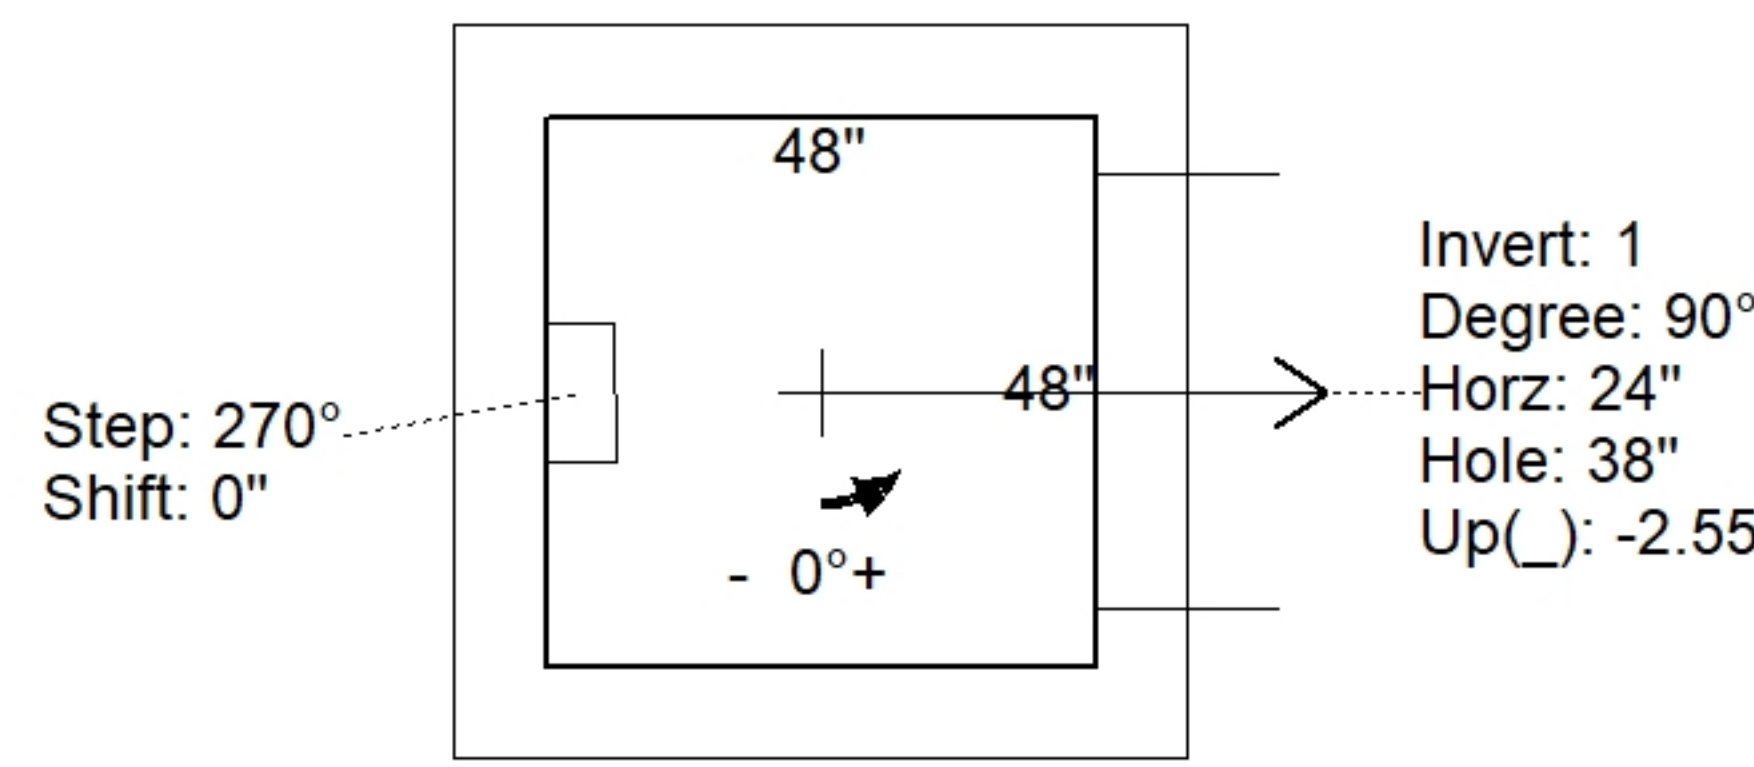
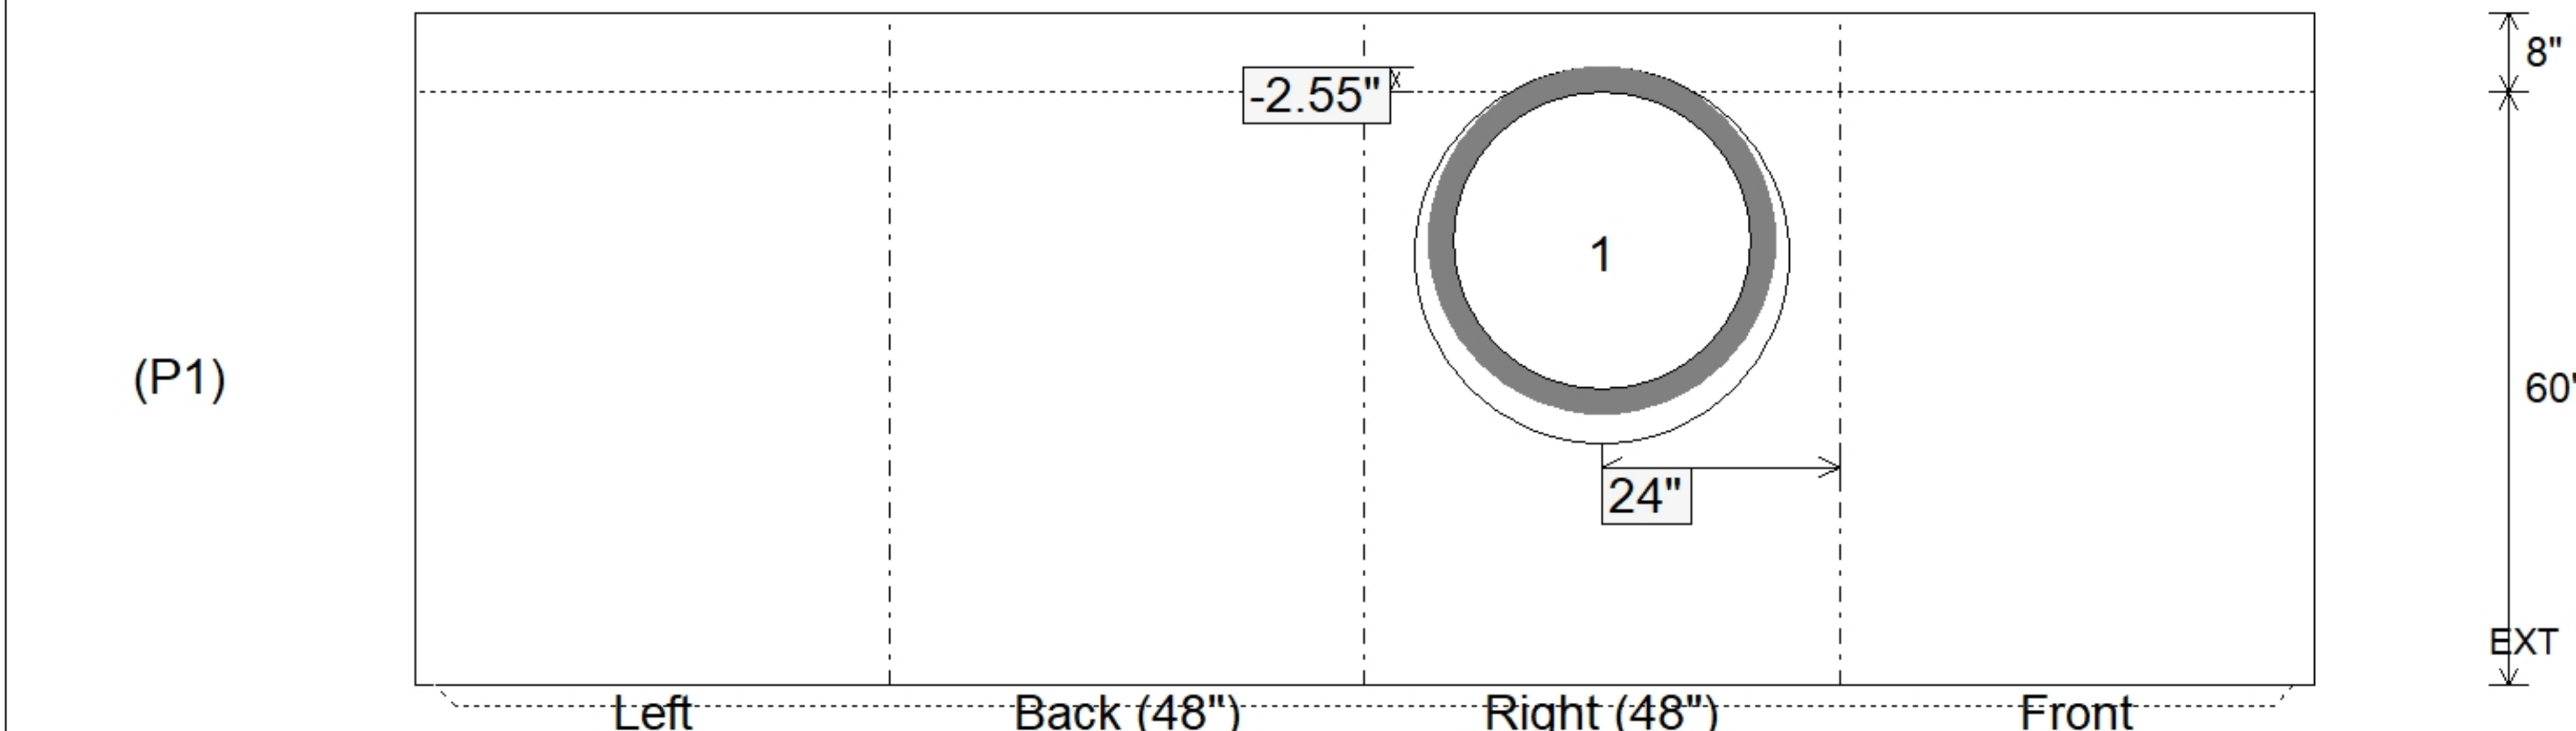


Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Bowling Green, KY					8/11/2026 9:19:04 AM		PC: M. Sullivan				
Contractor: Scotty's Contracting & Stone, LLC											
Structure ID: DBI-5											
P1		BX4848-08BA60		BOX BASE 8inW, 8inF T/n							
P3) 48" x 48" - CASTING HEIGHT - 4.5" P2) 48" x 48" - BOX RISER 8inW, Variable Ht F/G - 22" P1) 48" x 48" - BOX BASE 8inW, 8inF T/n - 60" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 2) 48" x 48" - Conseal CS-102 1.00" 1) Hole - 38 5) MH Step ML-10-TDS-NCR - 10"					0 lb 3308 lb 11011 lb 421 lb 0 lb 0 lb 0 lb ----- Structure Total: 14740 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 918 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 590.86' Rim to Invert: 7.28' Slack: 0.86" Sump: 0" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	583.58'	90°	32"	30" HDPE	35.1"	Hole 38	38"	38"	-2.55"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)						
											
INSIDE WALL DIMENSIONS											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 60" Height (Ext): 68"		Weight (Net): 11011 lb Volume (Net): 2.81cu.yd		
