

Job Name: 26-1227 - Project Colt
Job Location: Evansville, IN
Contractor: Russell's Excavating

Plant: 100

5/12/2026 11:30:53 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: 101-11 MHJ

P2 MH060LD08-24X36RECT

MH FLAT TOP w/24"x36" Hole F/F

- P3) 24" x 36" - CASTING HEIGHT - 4"
P2) 60" - MH FLAT TOP w/24"x36" Hole F/F - 8"
P1) 60" - MH BASE F/n - 60"
1) CASTING - HOE 518 F/G
1) 60" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 44
1) Hole - 38
2) Hole - 6
5) MH Step ML-10-TDS-NCR - 10"

0 lb
2153 lb
7517 lb
354 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb



10024 lb

Structure Total:

Structure Notes:

1. INDOT MH TYPE J / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 518 F/G).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

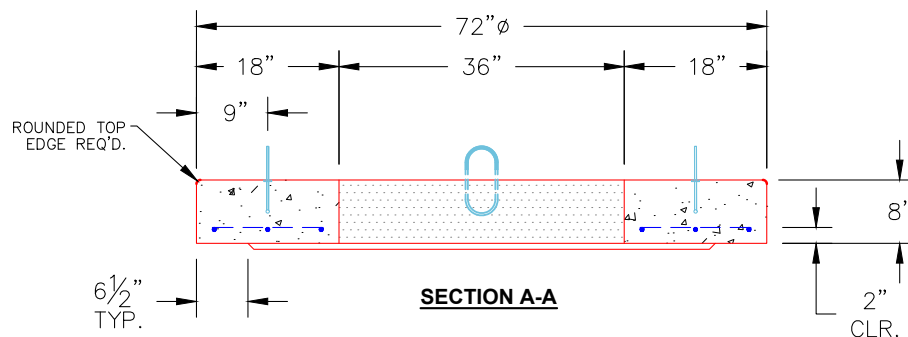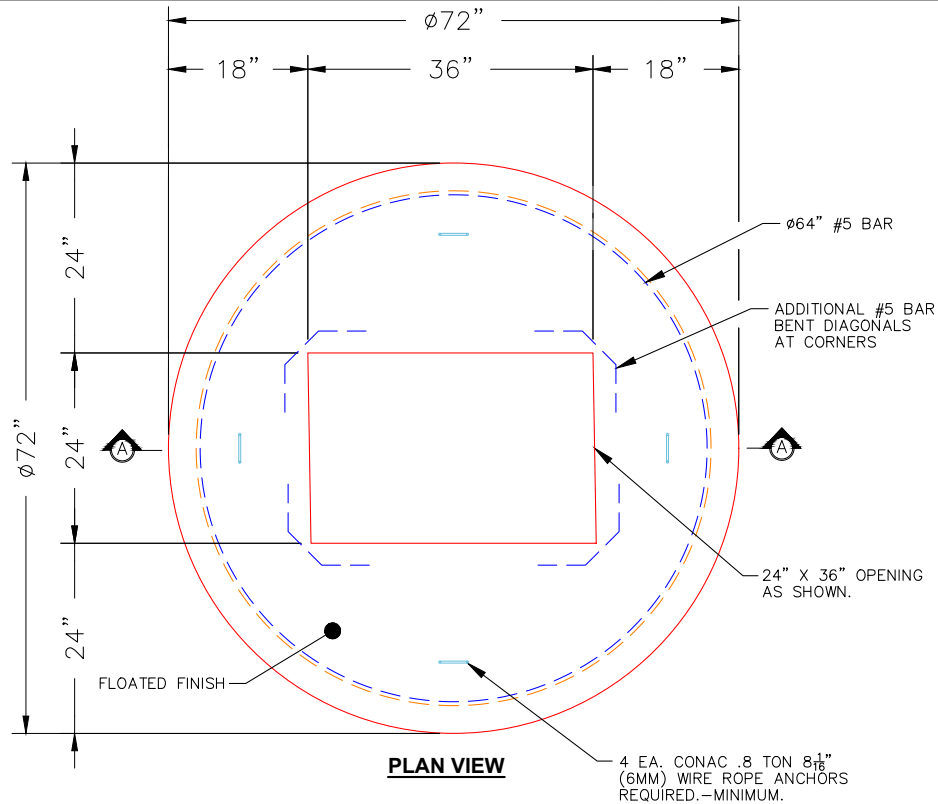

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 2153 lb
Volume (Net): 0.55cu.yd
