

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.17'

Floor Height: 8"

Slack: 3.04"


1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A))

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

354 11-

Structure Total: 12754 lb

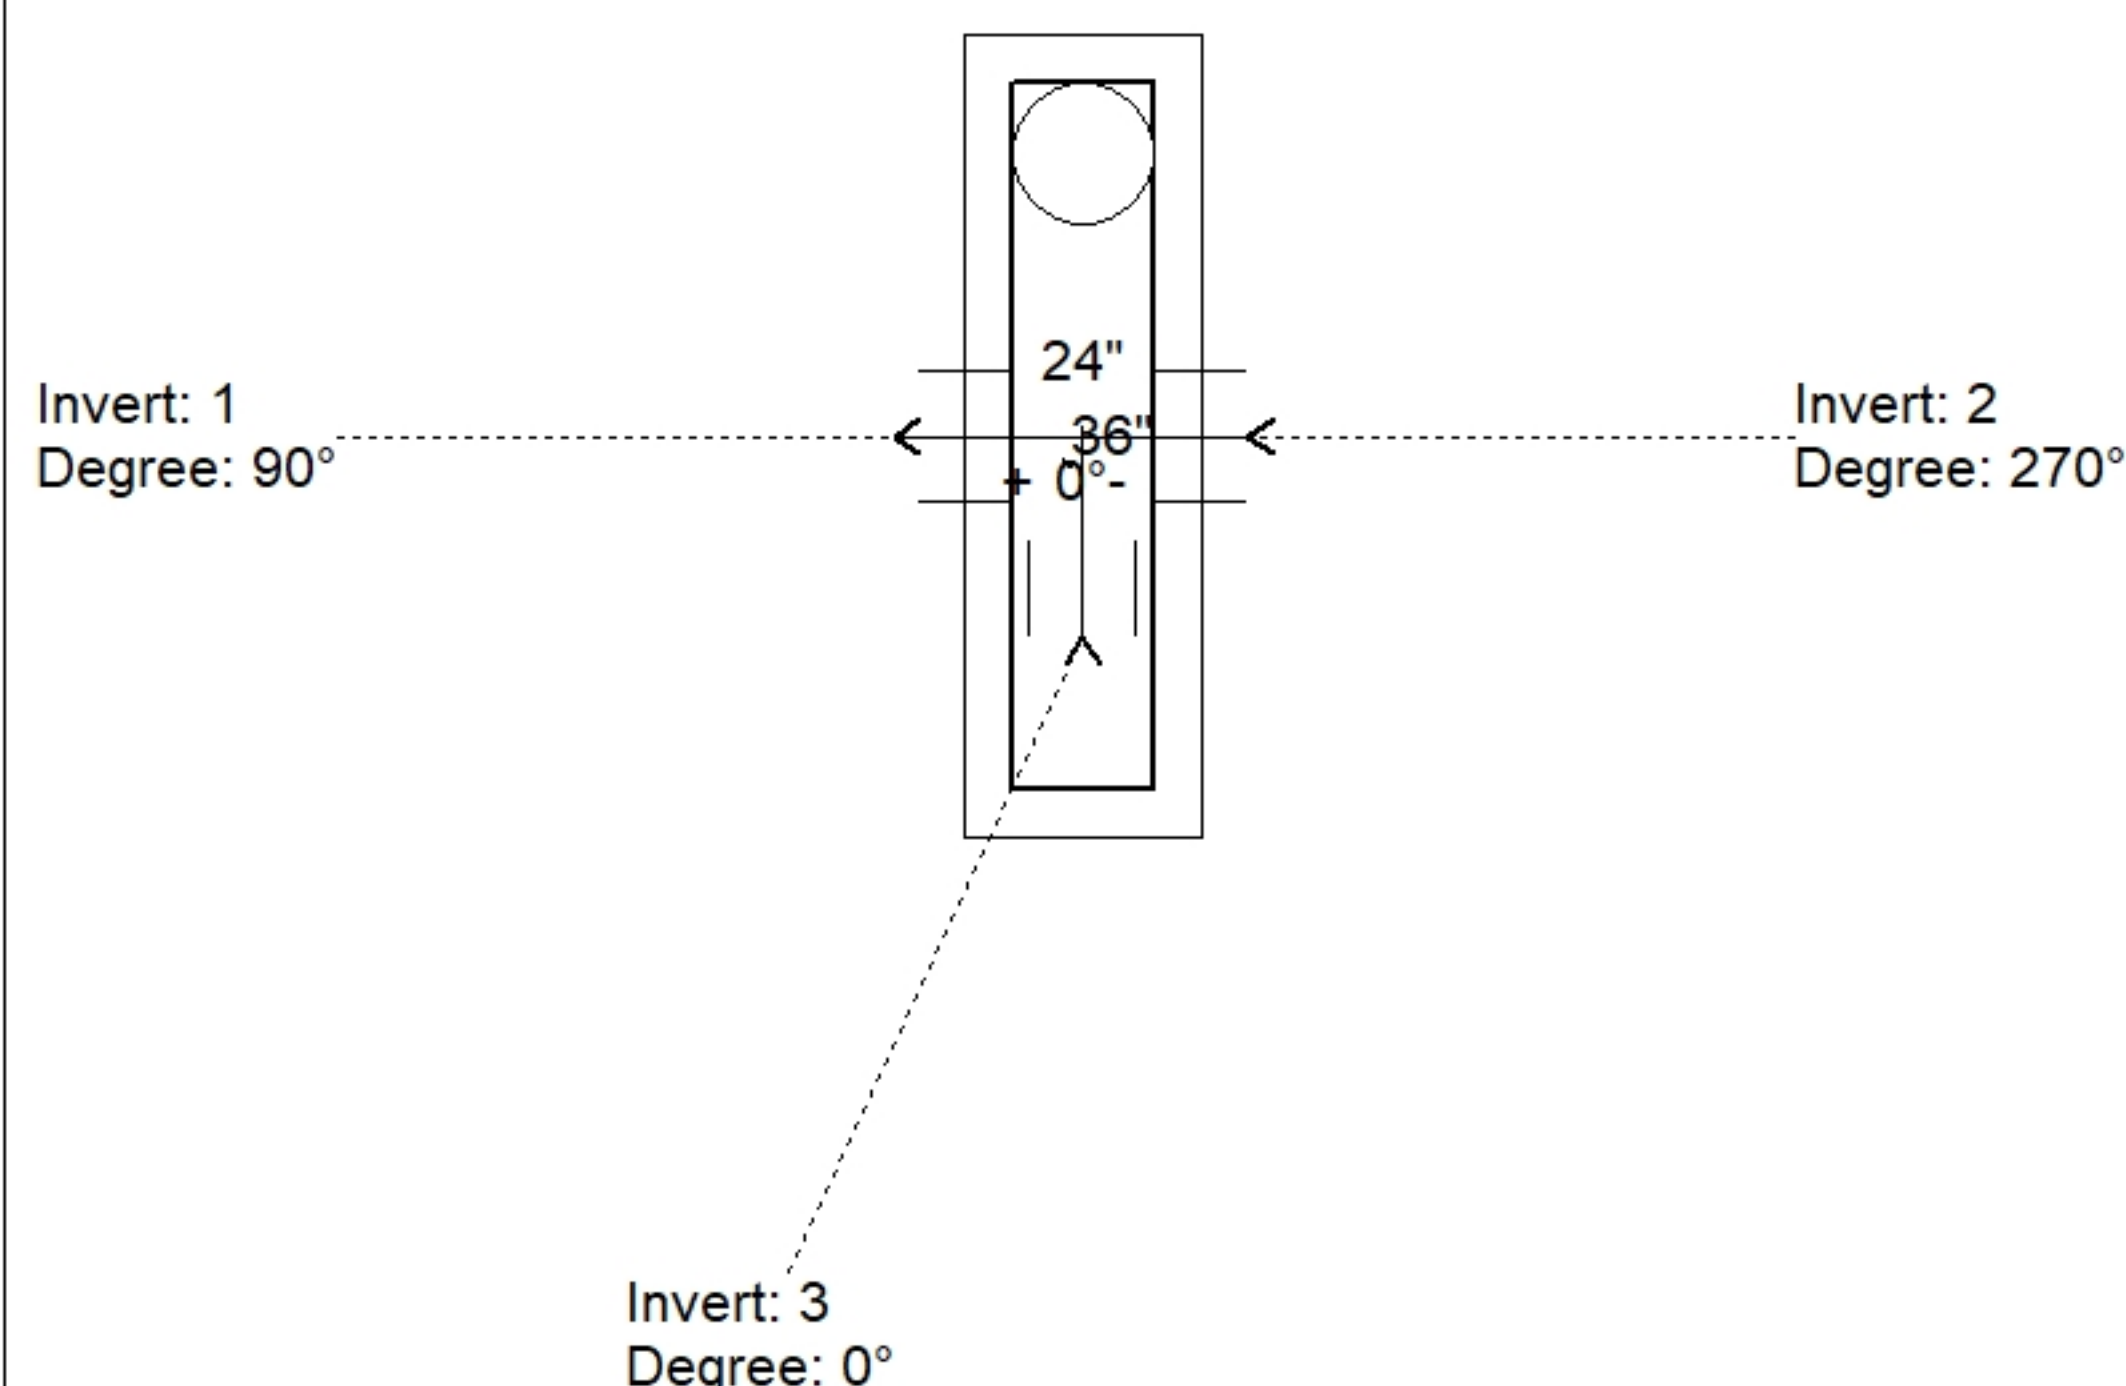


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	516.69'							
Reducer								
Invert 1	511.52'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	511.6'	270°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 3	511.6'	0°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31" - (P1)

Default - Interior Dimensions

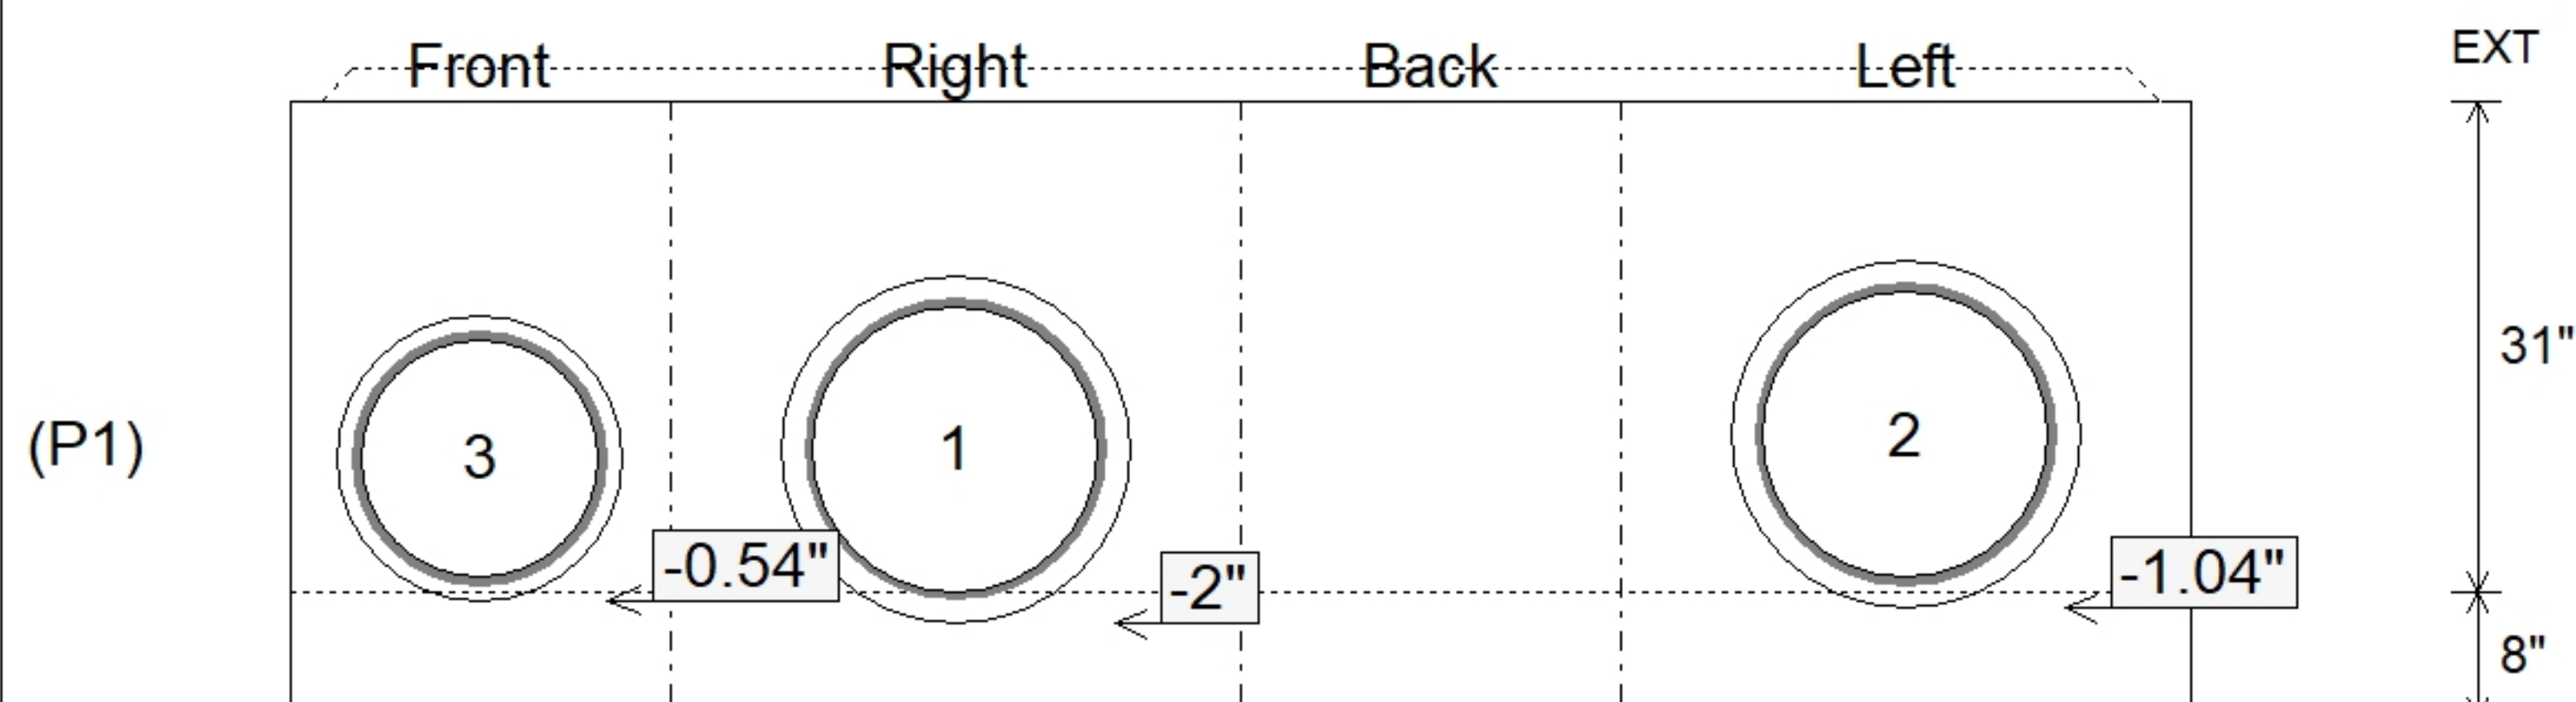

Submittal Drawing
9/8/2026 3:33:03 PM

SUBMITTAL
APPROVED BY:
