

Contractor: Hall Contracting of Kentucky Inc

TECH: J. Horsley

Plant: 100



Size: 77" x 6"

Rim to Invert: 3'


Floor Height: 0"

Slack: 0"

-HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)

0 lb

Structure Total: 3727 lb

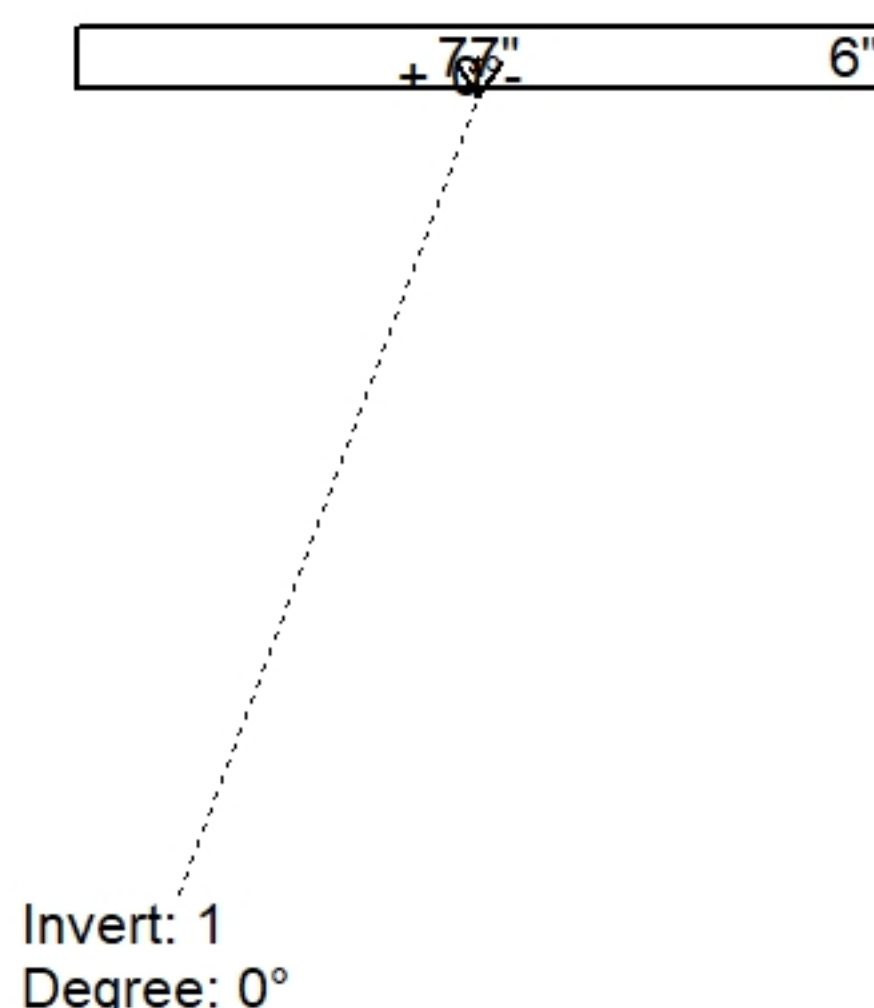


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	701'							
Reducer								
Invert 1	698'	0°	2" WEEP HOLE	2"	2"	Hole 2	24"	P2
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG - (P3)

77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG - (P2)

77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG - (P1)

Cast (Int. Dim.) - Interior Dimensions

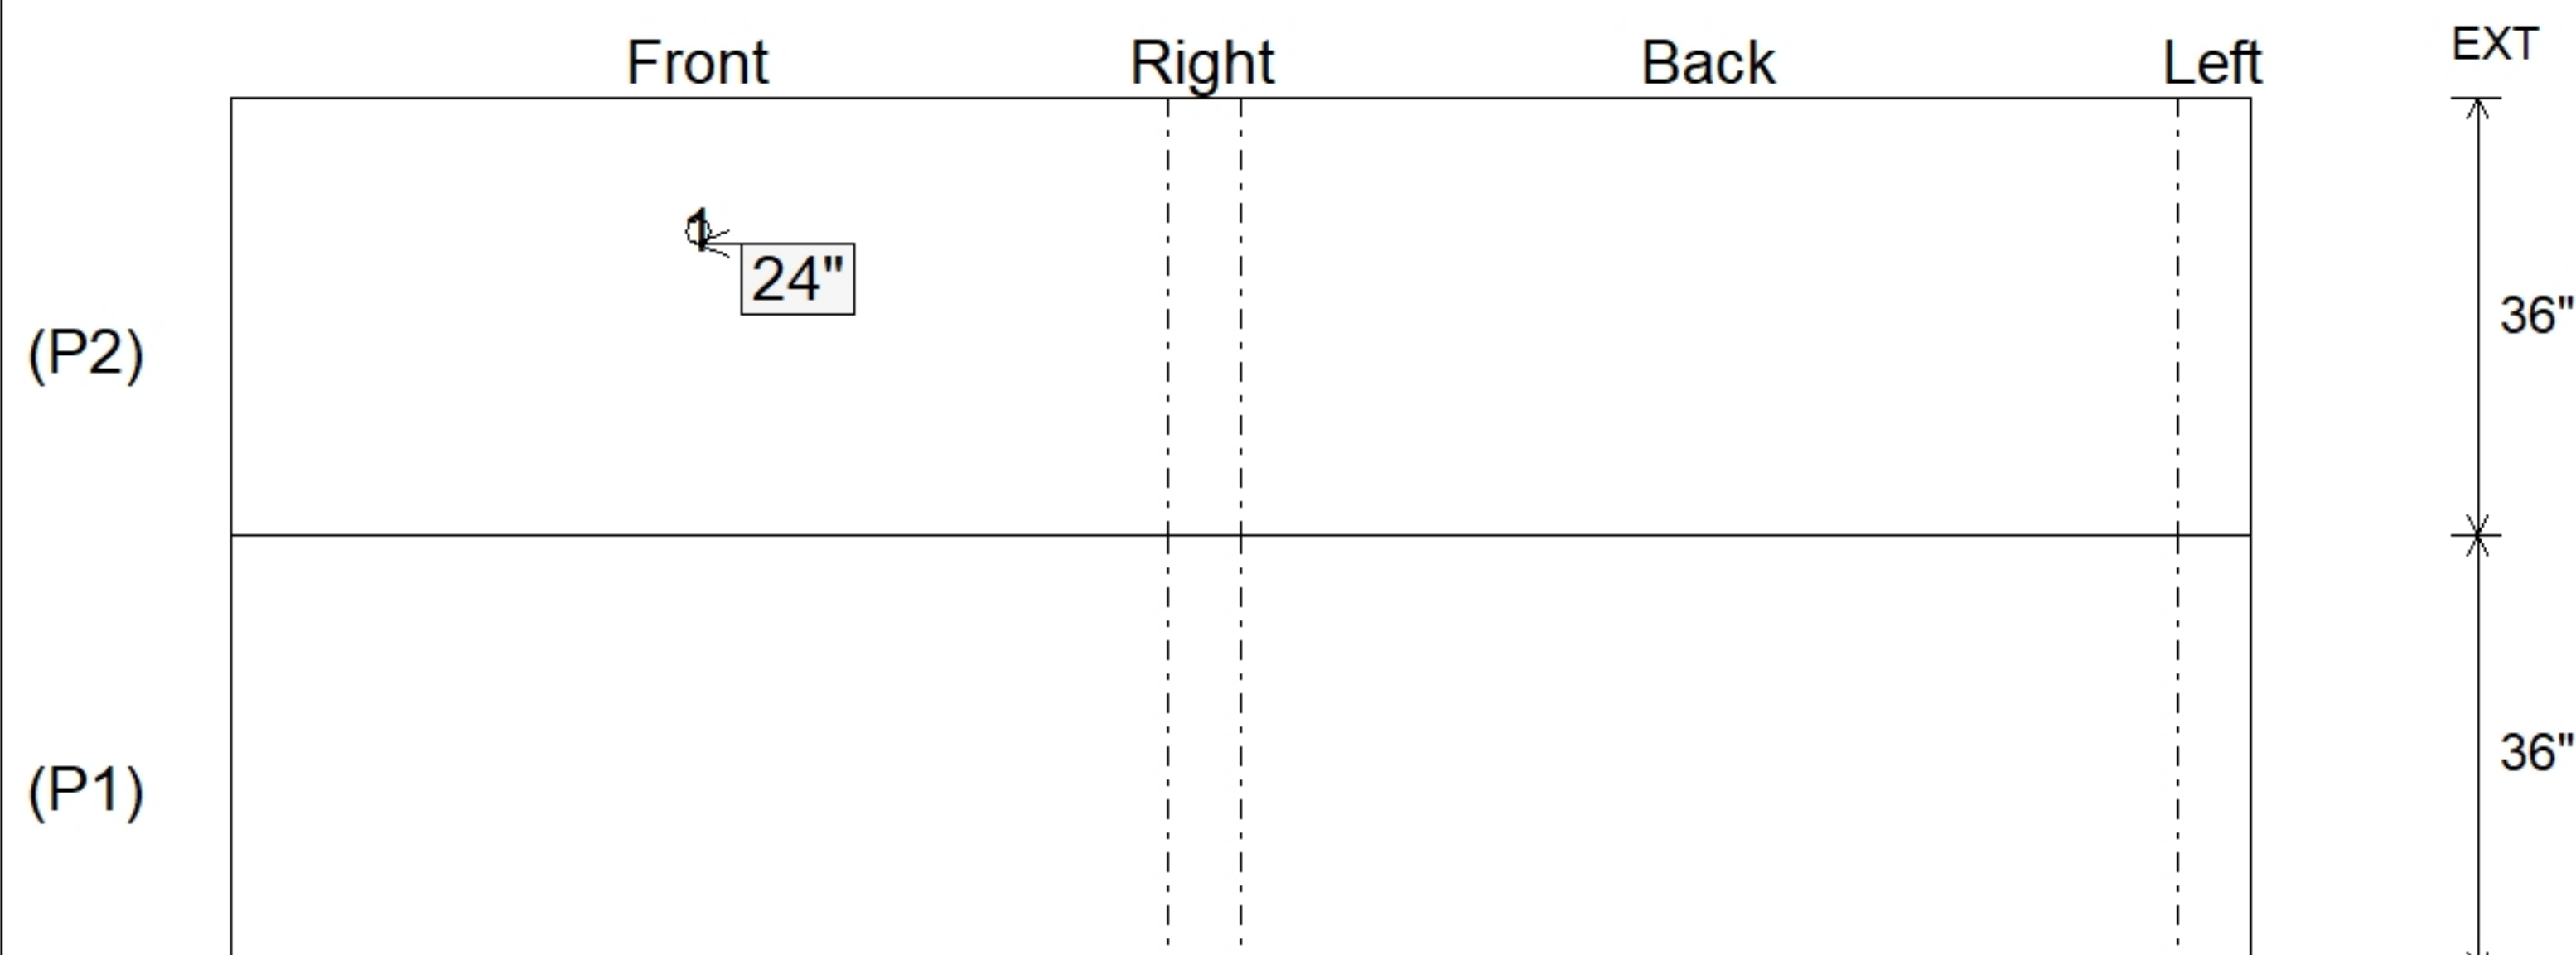

Submittal Drawing
6/16/2026 12:59:05 PM

SUBMITTAL
APPROVED BY:
