




Job Name: 26-1333B Mitchell Hill Road Project Job Location: Louisville, KY Contractor: Hall Contracting of Kentucky Inc				Plant: Beaver Dam 8/13/2026 3:43:16 PM		Tech: S. Felletter PC: J. Jarvis				
Structure ID: STR-1										
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 36" x 36" - P.I.P. - BY OTHERS - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" 1) CASTING - HOE KY-316 SET (DBI 1) 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 34				0 lb 5932 lb 317 lb 0 lb 0 lb ----- Structure Total: 6249 lb		Structure Notes: . 1. KYTC DBI TYPE 1 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING BY ICAST (HOE KY-316 SET) . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 693'		Rim to Invert: 4'		Slack: 1"		Sump: 1"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	689'	0°	26"	24" RCP B WALL	30"	Hole 34	34"	34"	-4"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



Invert: 1
Degree: 0°
Horz: 18"
Hole: 34"
Up(_): -4"




Invert: 1
Degree: 0°
Horz: 18"
Hole: 34"
Up(_): -4"

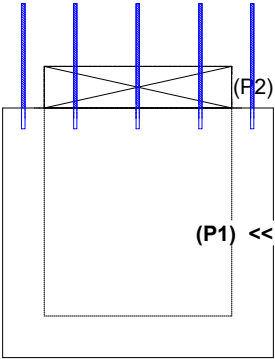

(P1) << (P2)

INSIDE WALL DIMENSIONS

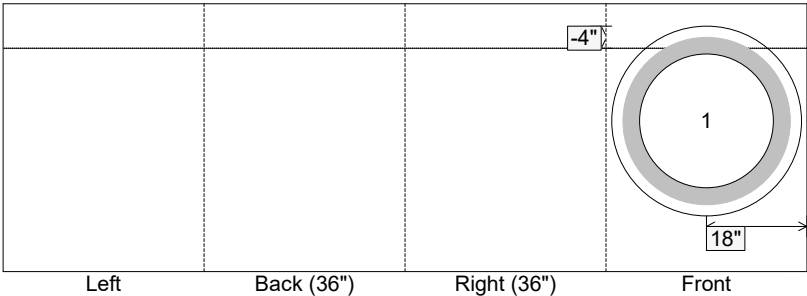

(P1)

Left Back (36") Right (36") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 5932 lb Volume (Net): 1.52cu.yd
----------------------------------	-------------------------------	--	--	--
