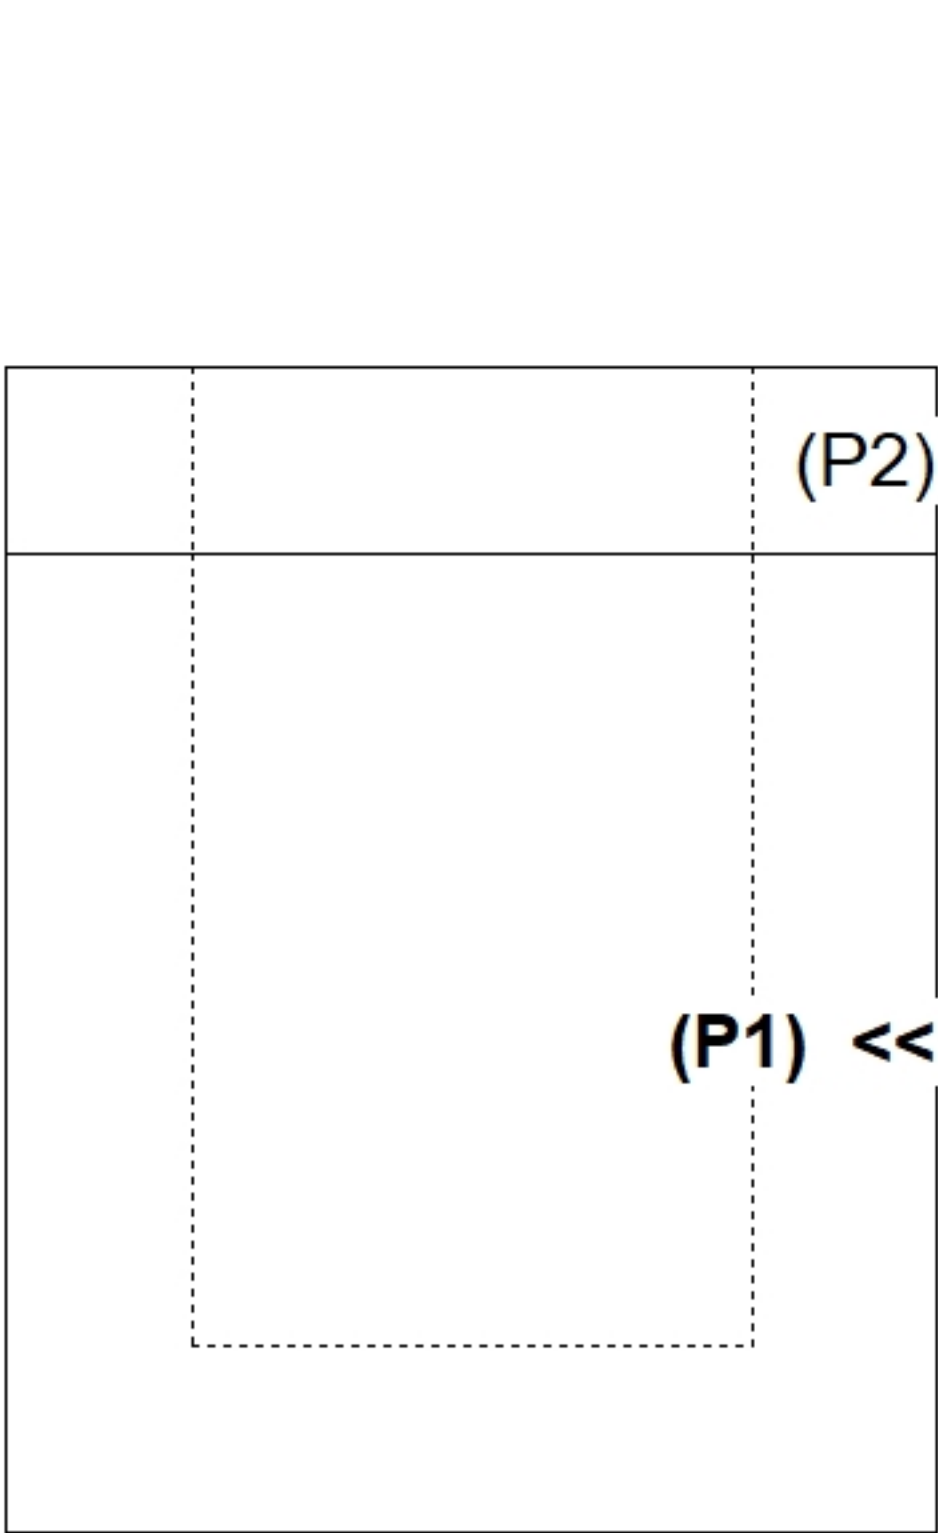
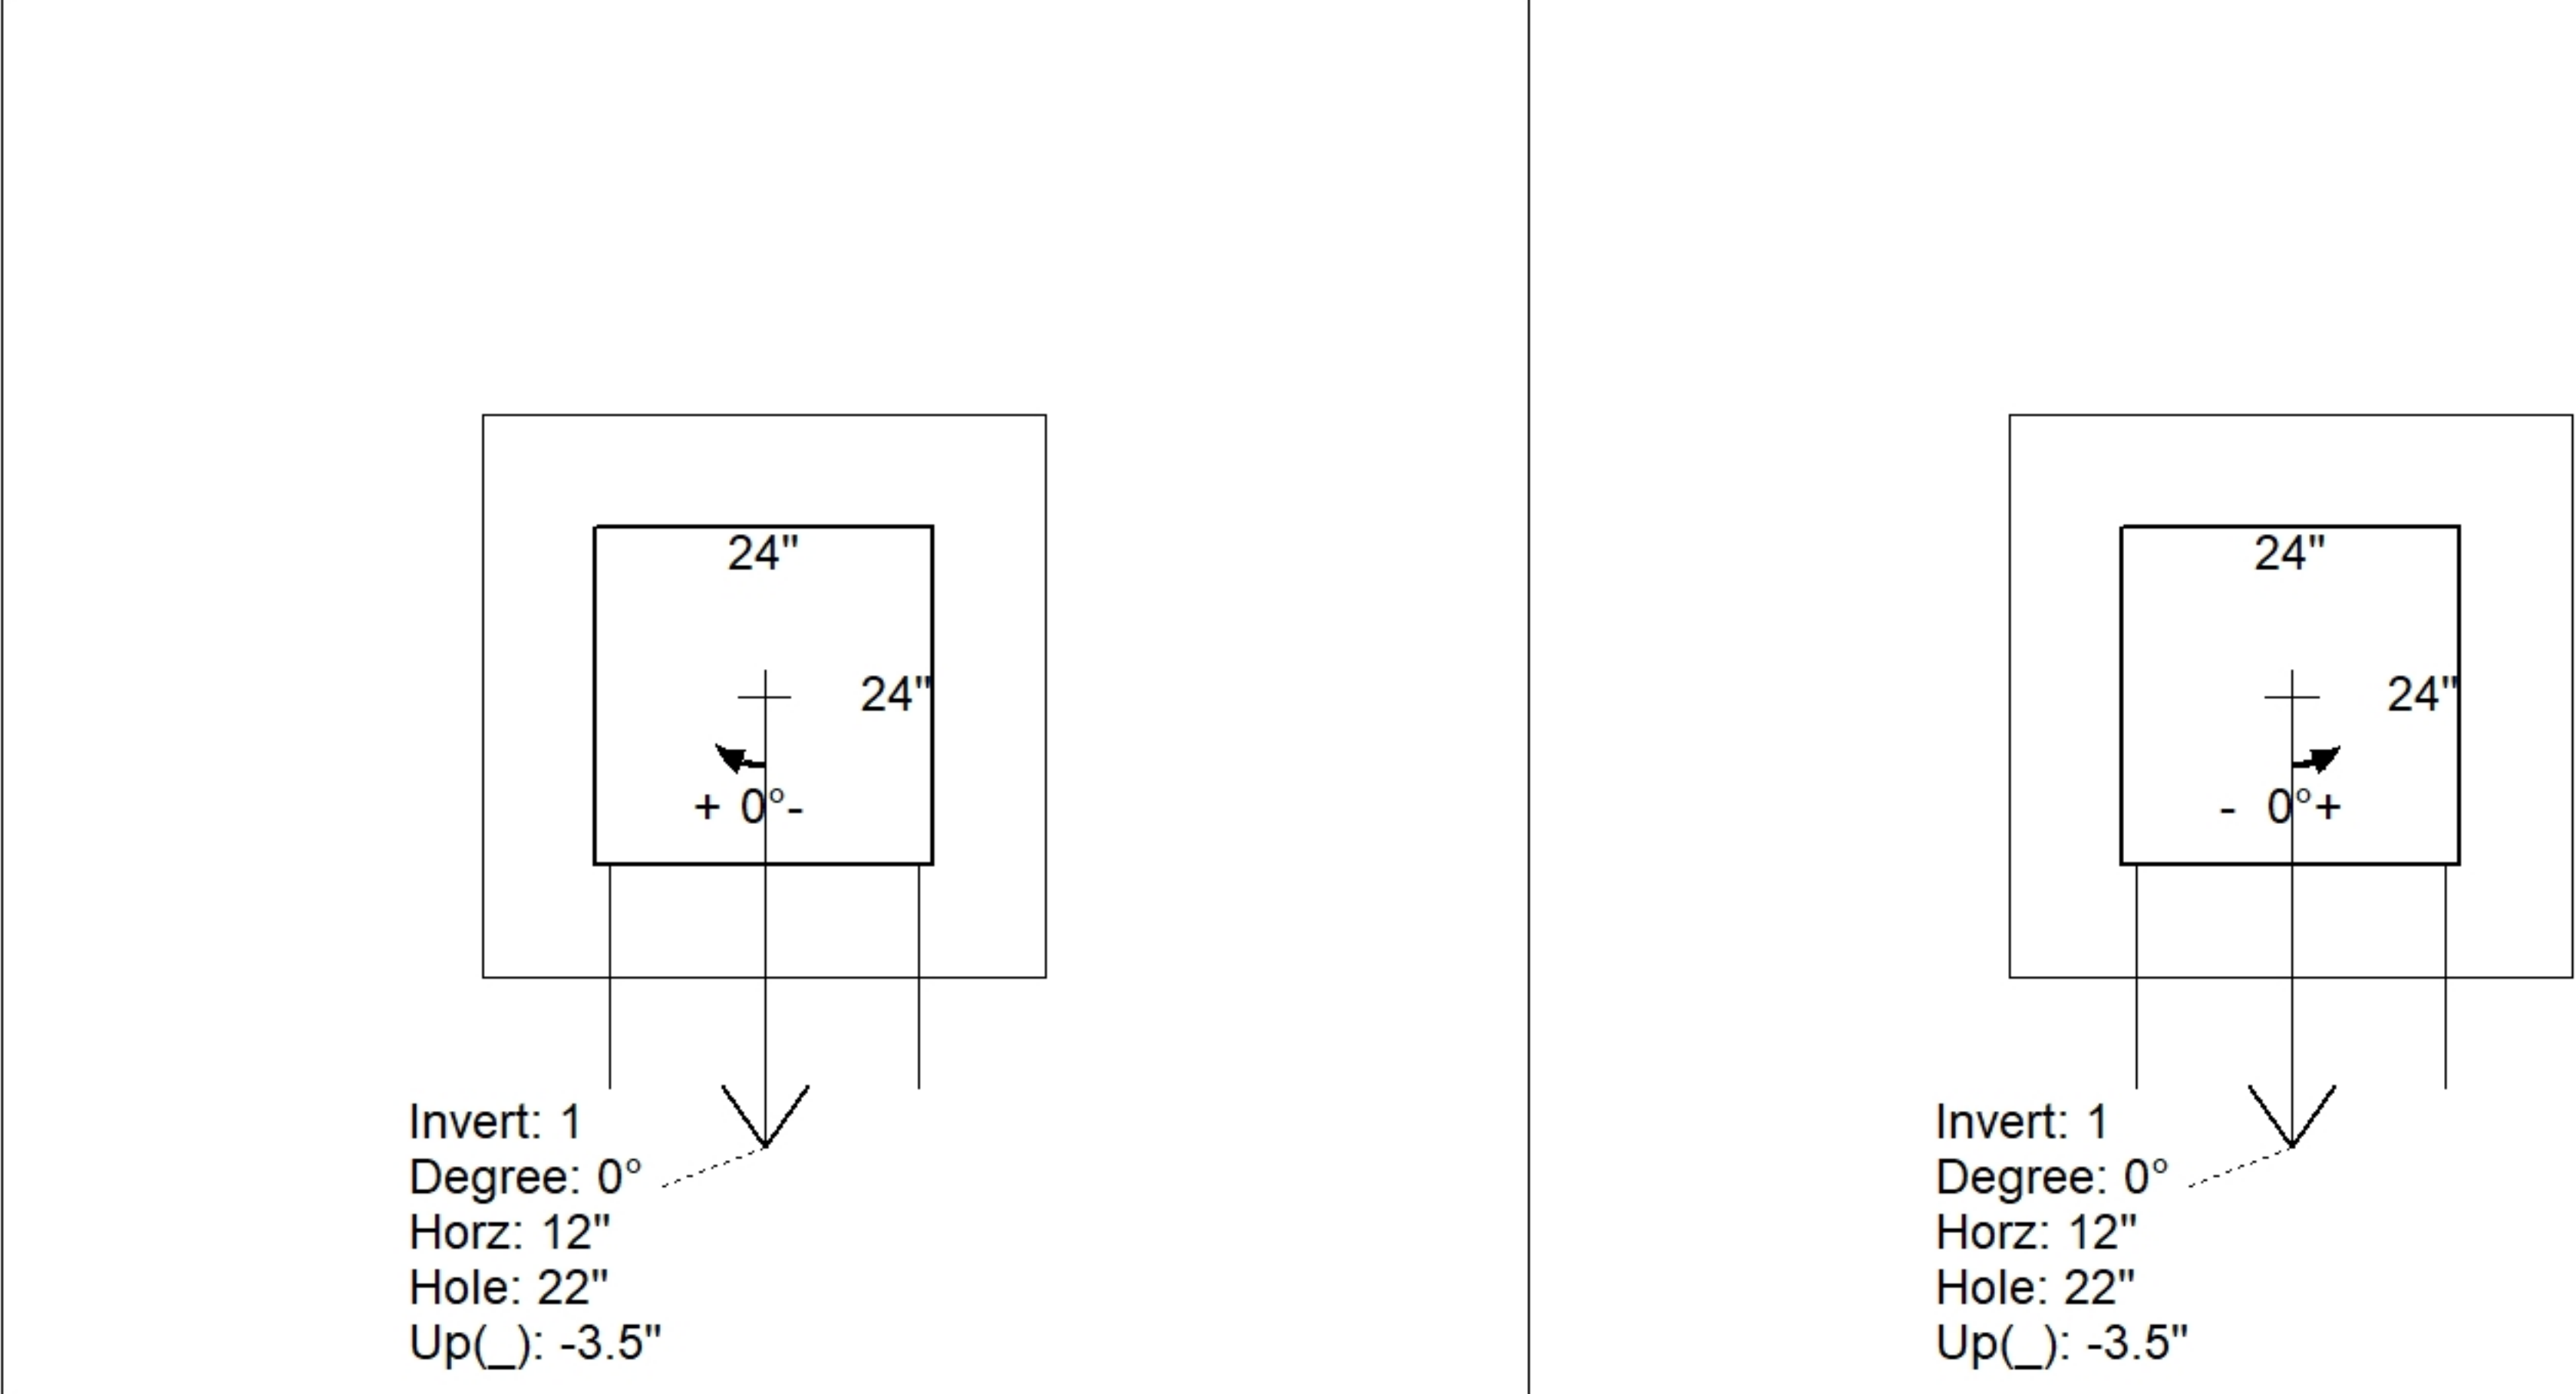
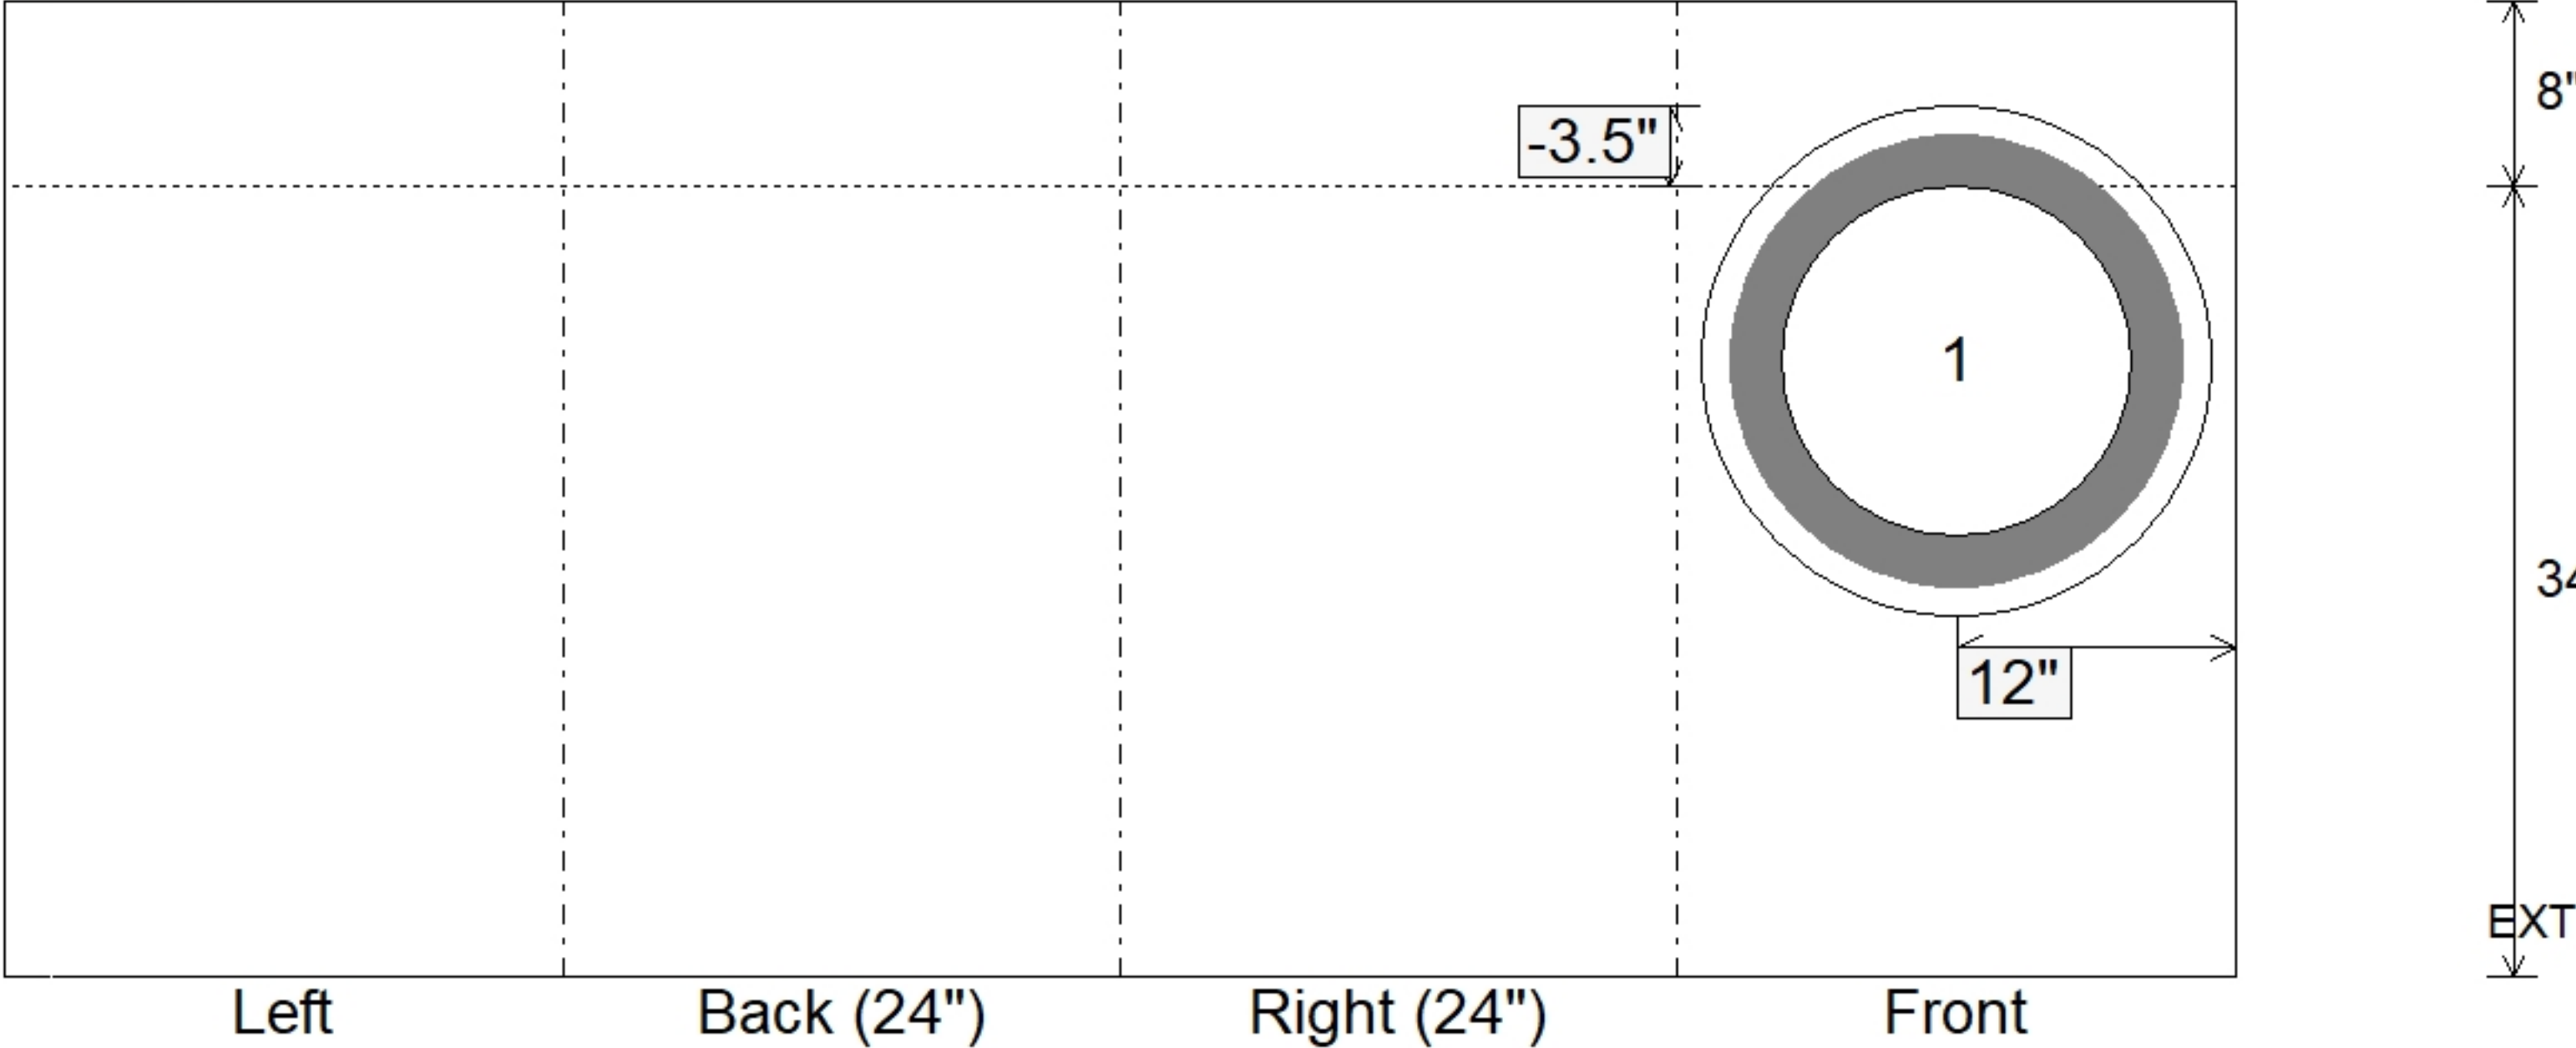


Job Name: 26-1333B Mitchell Hill Road Project Job Location: Louisville, KY Contractor: Hall Contracting of Kentucky Inc				Plant: Beaver Dam 8/13/2026 3:42:05 PM		Tech: S. Felletter PC: J. Jarvis				
Structure ID: STR-2										
P1		BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n					
P2) 24" x 24" - CB FLAT TOP 8"W (HOE KY-215 F&G) F/F - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 34" 1) This Structure Includes a Cast-in Item 1) CASTING - HOE KY-215 F/BEEHIVE (DBI 15) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 22					770 lb 3740 lb 0 lb 317 lb 0 lb 0 lb ----- Structure Total: 4828 lb		Structure Notes: . 1. KYTC DBI TYPE 15 / ASTM C913 SPECIFICATIONS 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. DBI-15 F/G CAST INTO TOP SLAB (HOE KY-215 F/G BEEHIVE). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 676.35'		Rim to Invert: 3.5'		Slack: 0"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	672.85'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-3.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)					
										
INSIDE WALL DIMENSIONS										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 34" Height (Ext): 42"		Weight (Net): 3740 lb Volume (Net): 0.96cu.yd	
