

Job Name: 26-1453 Clarksville, TN SPC13A
Job Location: Clarksville, TN
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam

6/23/2026 8:25:01 AM

Tech: J. Coppage

PC: C. Goff



Structure ID: 13A-SS-MH-001



P2 MH048LD12CDARED

MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red

- P3) 24" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 12"
P1) 48" - MH DH RISER Custom Ht, w/ConBlock-CDA Red - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) DOGHOUSE - 10"x10"
1) Z-Lok - C107-3
3) MH Step ML-10-TDS-NCR - 10"

Structure Total: 4007 lb

- 0 lb
1580 lb
2426 lb
0 lb
0 lb
0 lb
0 lb
0 lb
1 lb
0 lb
- Structure Notes:** 1. JBS-1155 SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

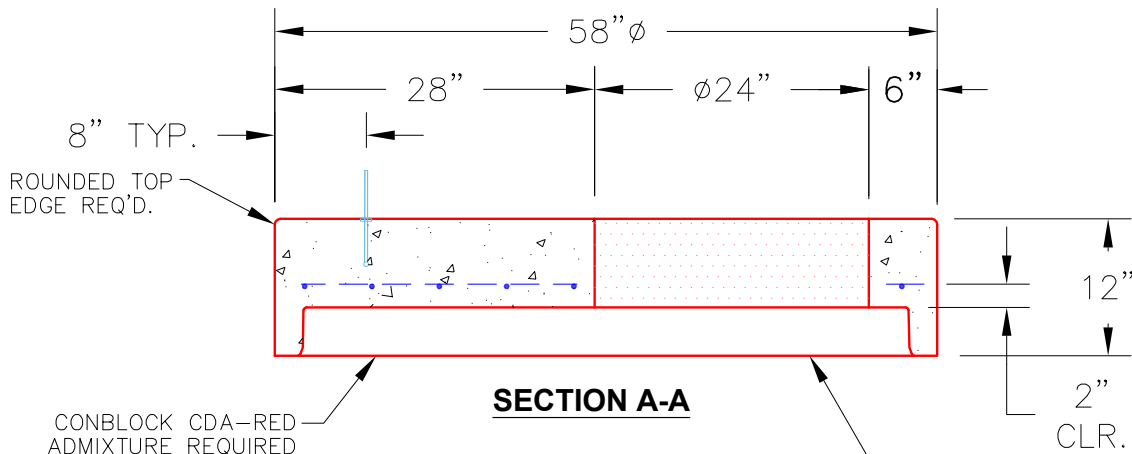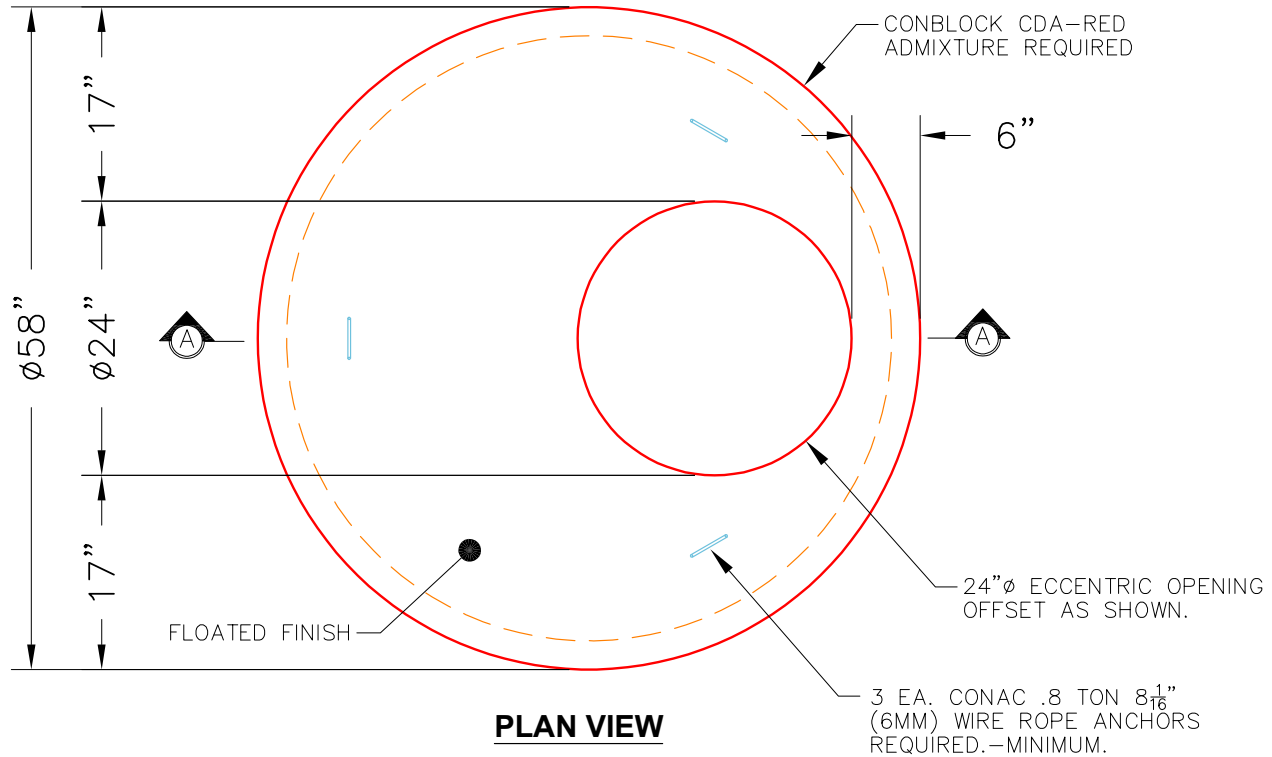

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. CONBLOCK CDA-RED ADMIXTURE REQUIRED.
4. REINFORCING: #4 BAR @ 10" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1580 lb
Volume (Net): 0.39cu.yd
