



Job Name: 26-1515 Ford High Tech Manufacturing Facility Job Location: Shelbyville, KY Contractor: Core & Main LP					Plant: Beaver Dam 5/8/2026 2:12:58 PM		Tech: S. Felletter PC: T. Lewis				
Structure ID: 2 SS-MH											
P1 MH048BA24		MH BASE T/n									
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE F/G - 42" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3200 lb 4192 lb 2959 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 8 lb 0 lb Structure Total: 12408 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12 C.C.E.W.				
Rim: 745.3' Rim to Invert: 11.37' Slack: 1.44" Sump: 2" Step Position: 180°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	733.93'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

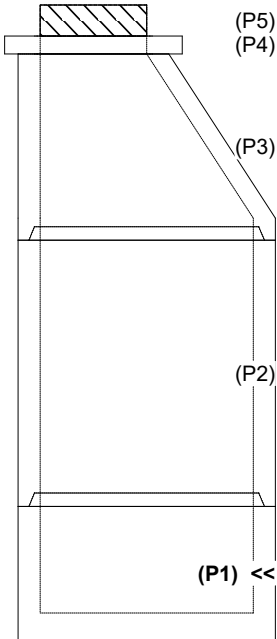

(P5)
(P4)
(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

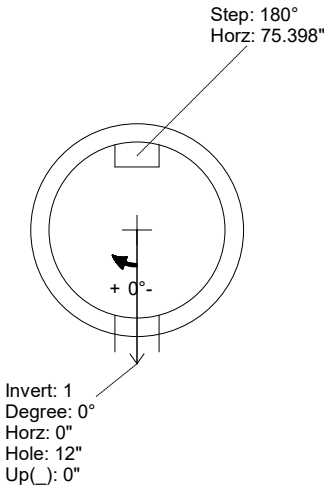

Step: 180°
Horz: 75.398"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)

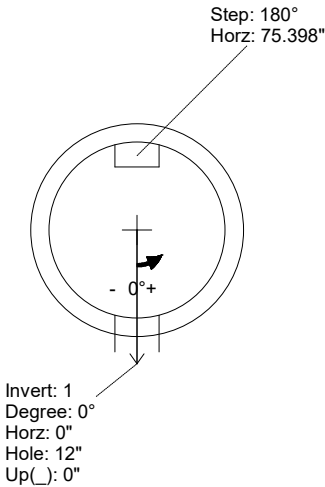

Step: 180°
Horz: 75.398"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

INSIDE WALL DIMENSIONS



(P1)


360° 270° 180° 90° 0°

6"
24"
EXT


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2959 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1515 Ford High Tech Manufacturing Facility Job Location: Shelbyville, KY Contractor: Core & Main LP					Plant: Beaver Dam 5/8/2026 2:12:58 PM		Tech: S. Felletter PC: T. Lewis						
Structure ID: 2 SS-MH													
P1 MH048BA24		MH BASE T/n											
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE F/G - 42" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3200 lb 4192 lb 2959 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 8 lb 0 lb Structure Total: 12408 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12 C.C.E.W.					Invert channel drawing Full height invert	
Rim: 745.3' Rim to Invert: 11.37' Slack: 1.44" Sump: 2" Step Position: 180°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	733.93'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"			
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													


RIGHT-SIDE UP VIEW (int. dimensions)

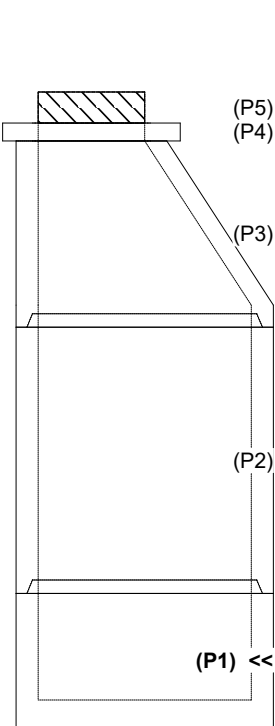

UPSIDE-DOWN VIEW (int. dimensions)

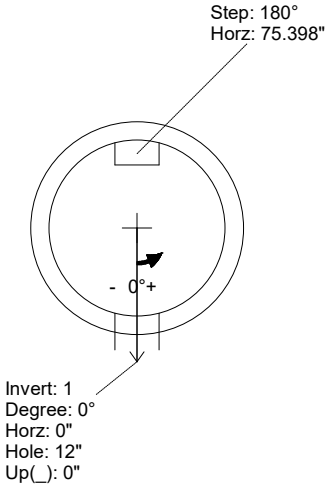

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2959 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--
