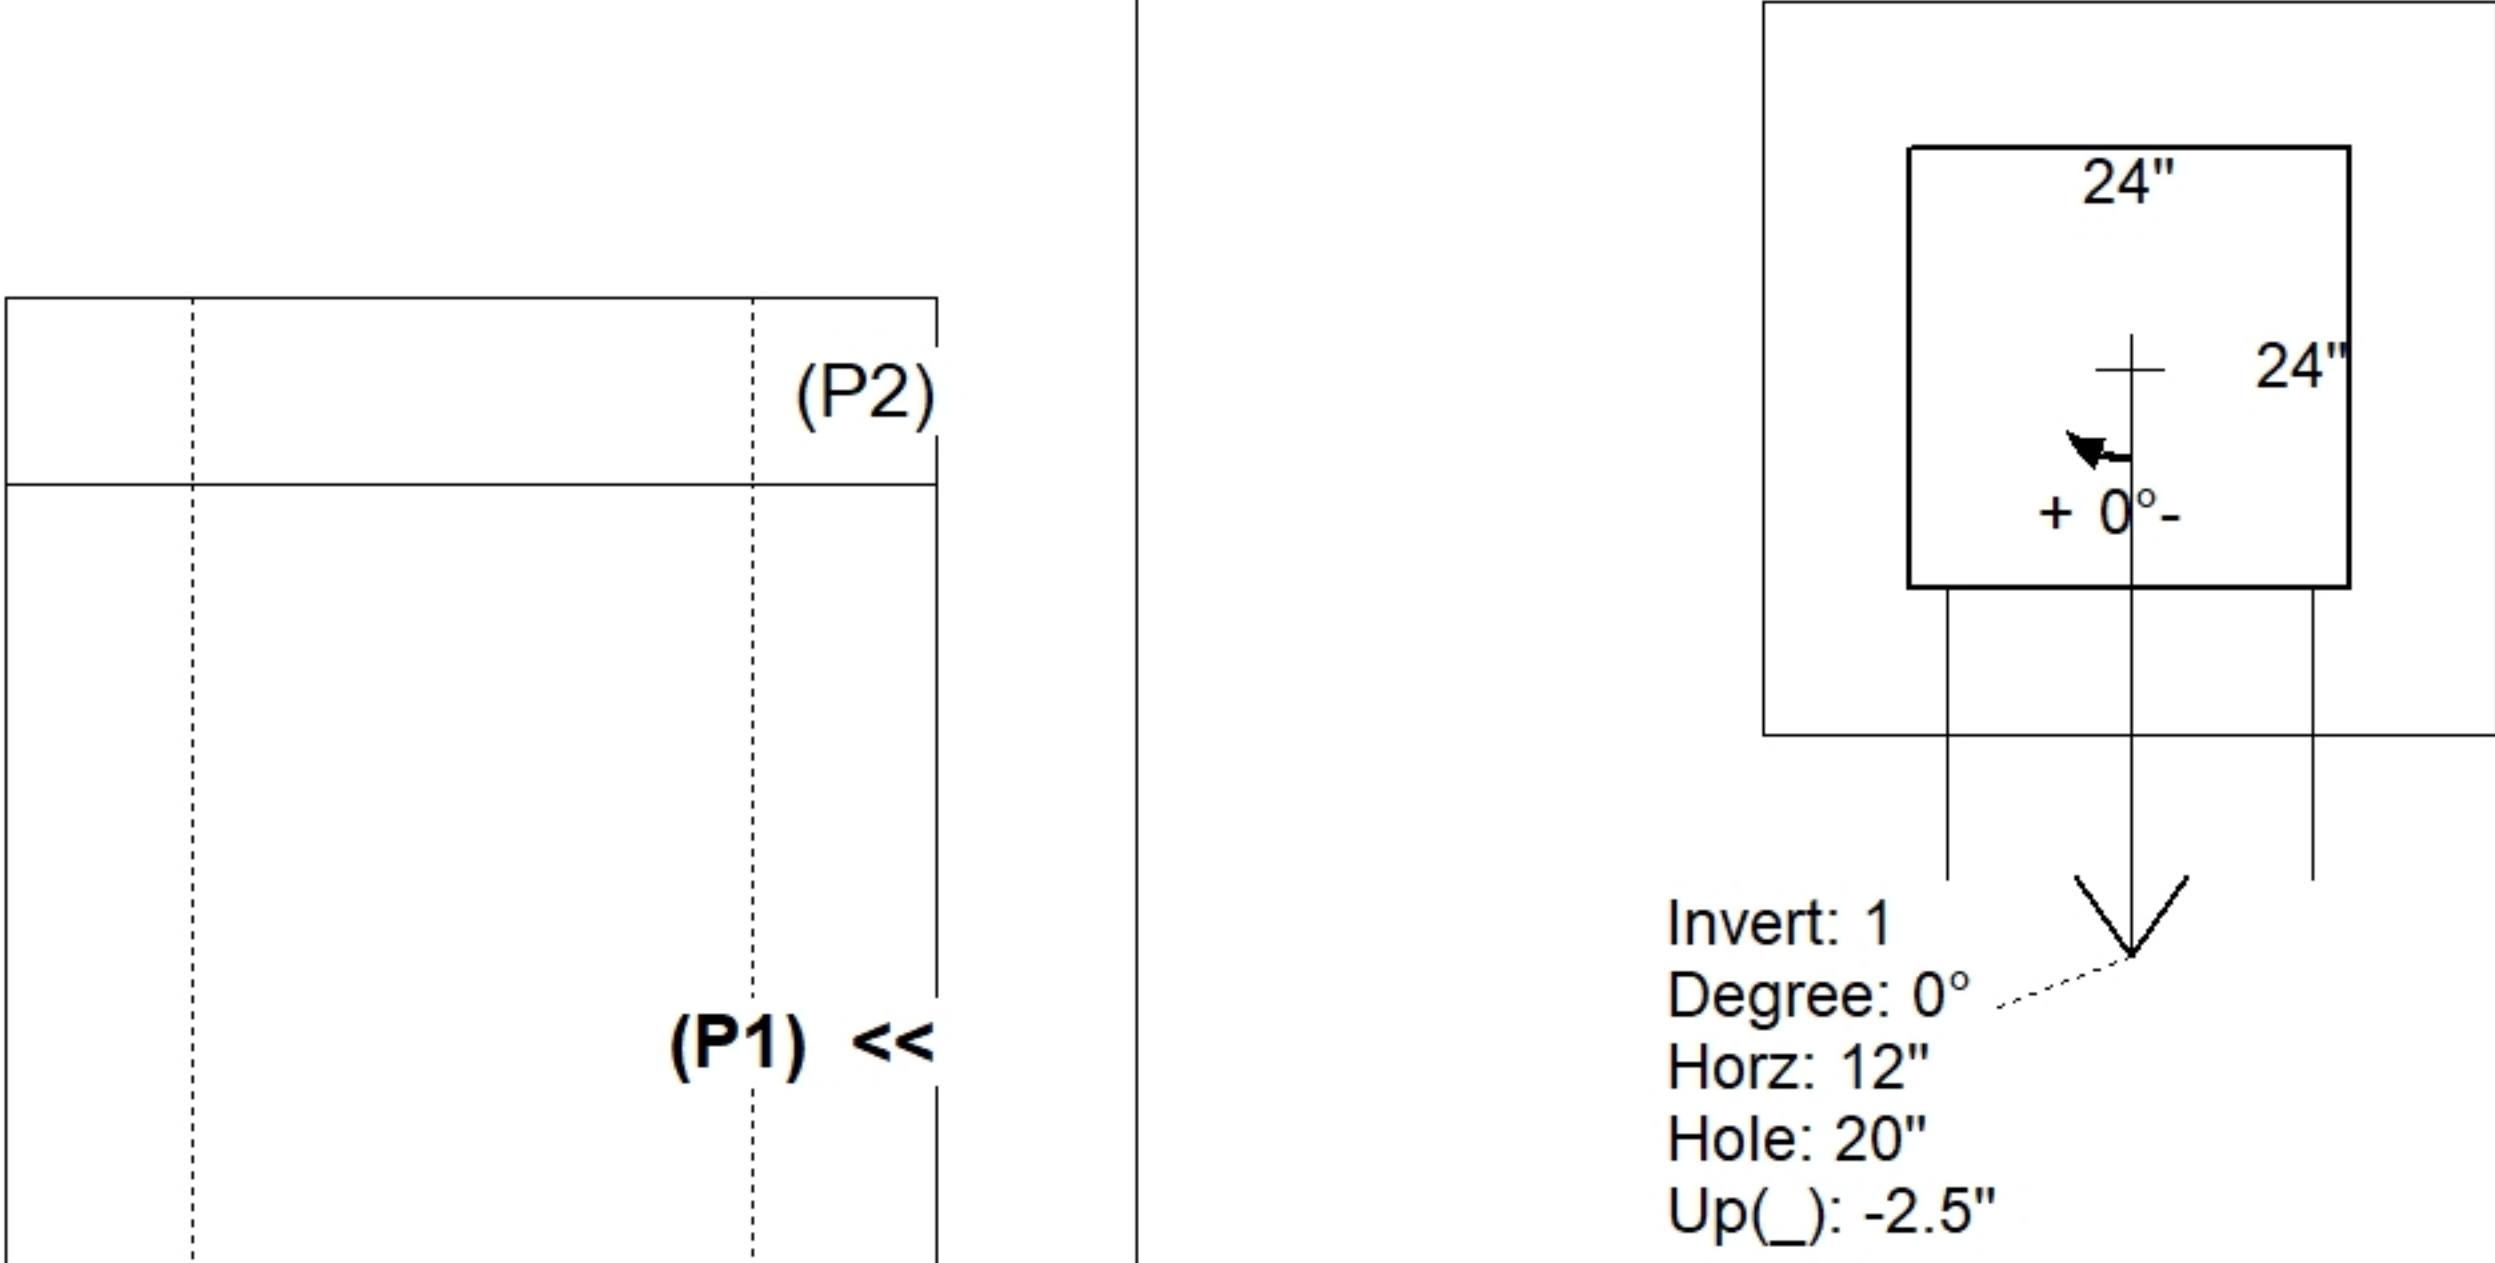
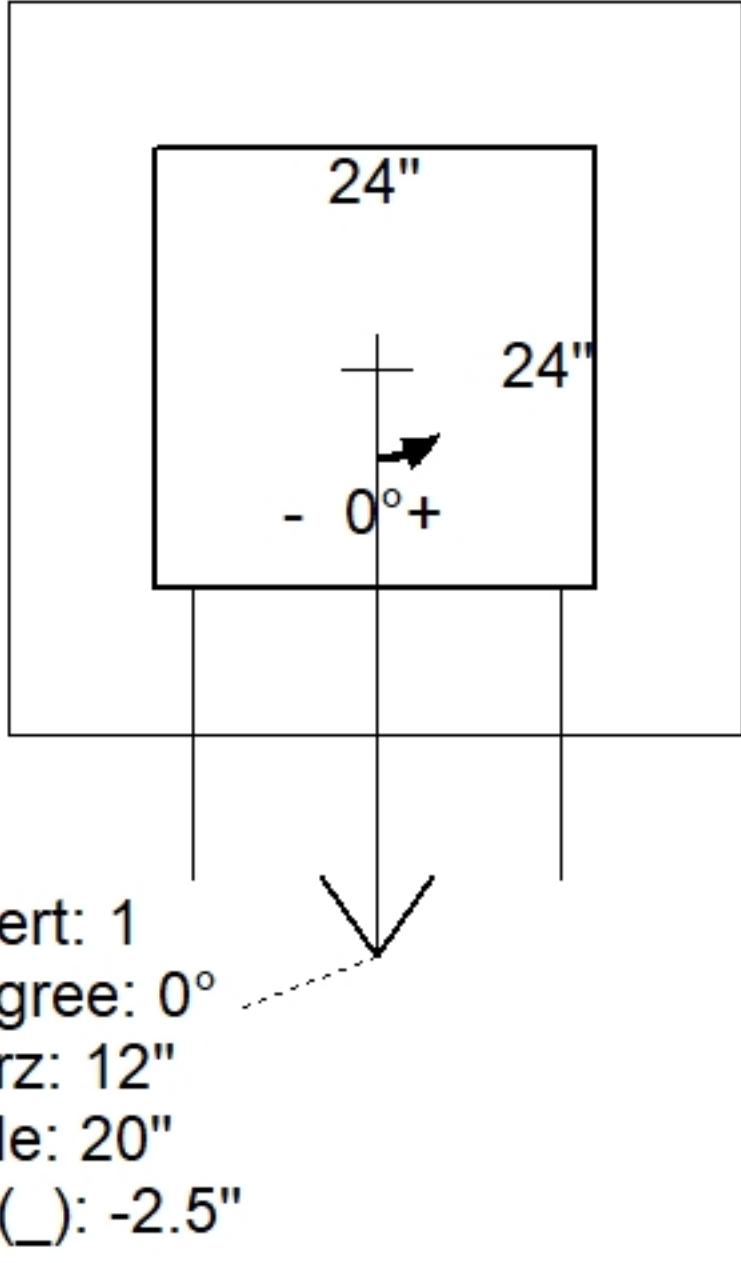
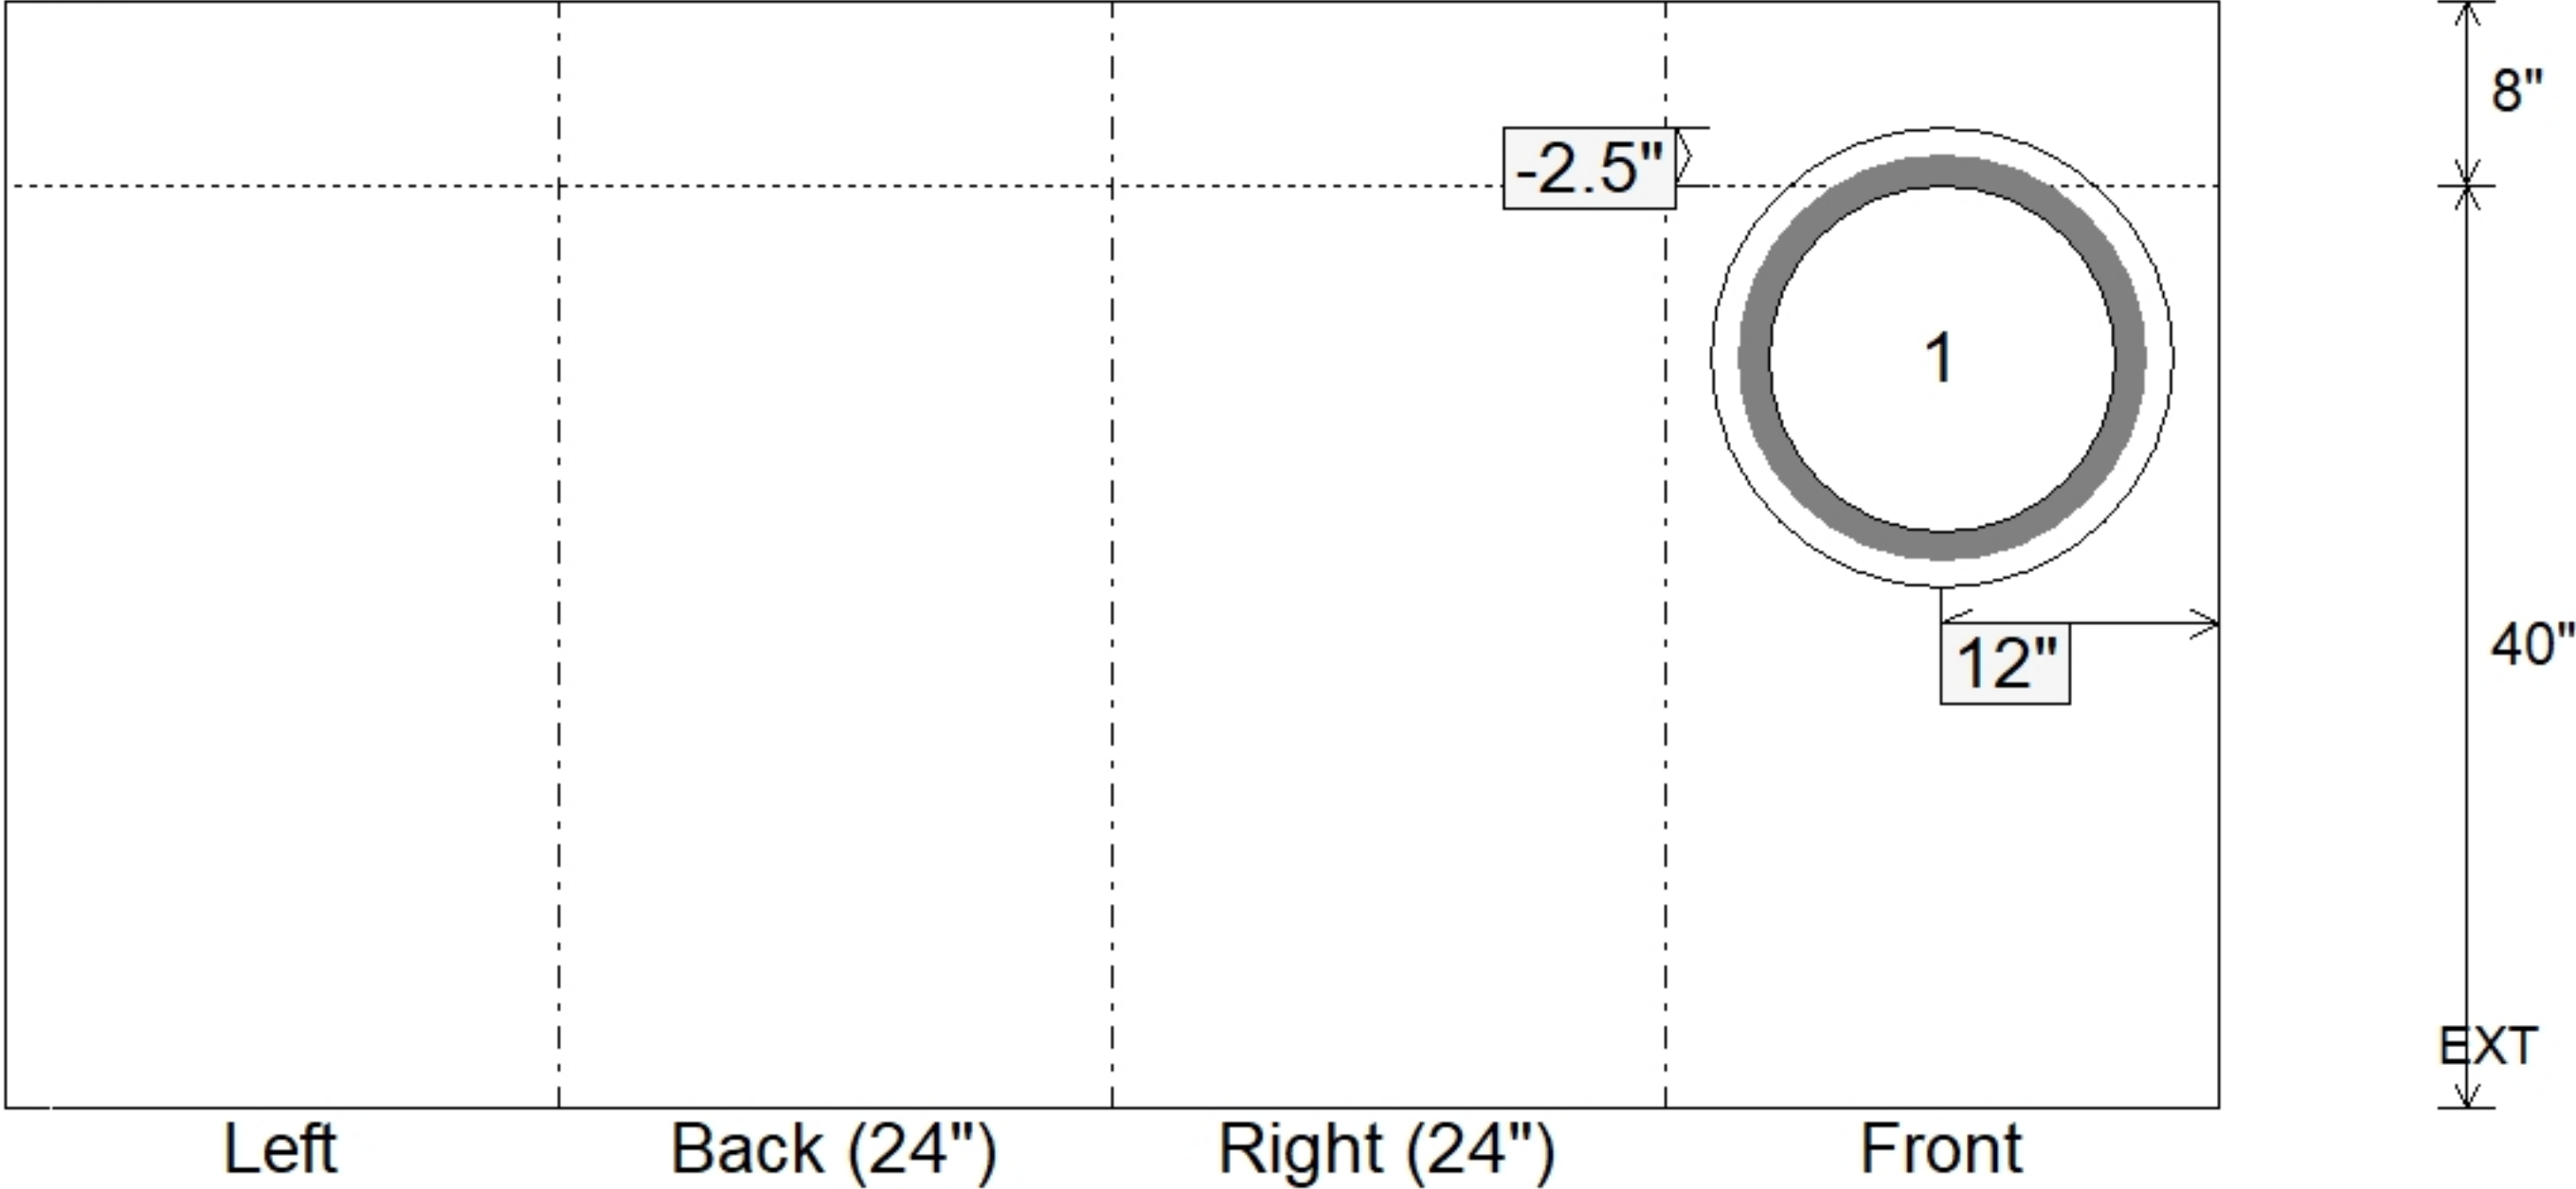


Job Name: 26-1545 - KYTC Boone Co. Camp Ernst Roundabout (ID 3002312)					Plant: 100		Tech: J.Horsley				
Job Location: Burlington, KY					5/13/2026 2:21:46 PM		PC: J. Jarvis				
Contractor: Lawrence Construction & Leasing, Inc.											
Structure ID: D3-7 DBI14											
P1		BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CB FLAT TOP 8"W (HOE KY-210) F/F - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" 1) CASTING - HOE KY-210 F/G (DBI 14) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20					770 lb 4300 lb 178 lb 0 lb 0 lb ----- Structure Total: 5249 lb		Structure Notes: ** KYTC STATE PROJECT** 1. KYTC DBI TYPE 14 / ASTM C913 SPECIFICATIONS 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. DBI-14 F/G CAST INTO TOP SLAB (HOE KY-210 F/G). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 887.78' Rim to Invert: 4.04' Slack: 0.48" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	883.74'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)						
											
INSIDE WALL DIMENSIONS											
Coating (Int):			Seam Up: Flat		Wall Thickness: 8"		Height (Int): 40"		Weight (Net): 4300 lb		
Coating (Ext):			Seam Dn: n/a		Floor Height: 8"		Height (Ext): 48"		Volume (Net): 1.1cu.yd		
