

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Pee wee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

7/22/2026 12:46:52 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 36525-143 MHA

P2 MH048LD12ECC

MH FLAT LID w/24in ECC Hole F/G

- P3) 24" - CASTING HEIGHT - 4"
P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 69"
1) 48" - Con seal CS-102 1.00"
1) 24" - Con seal CS-102 1.00"
2) Hole - 28
1) Hole - 18
6) MH Step ML-10-TDS-NCR - 10"

0 lb
1561 lb
5496 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 7057 lb

Structure Notes:

KYTC STATE PROJECT


1. PER KYTC MH A / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY OTHERS (HOE KY-206 F/C (KY TY1)).
4. INVERT BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60.)


- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W..

- RISER/WALLS (As.12).

- FLOOR (As.31) #5 BARS AT 12" C.C.E.W.

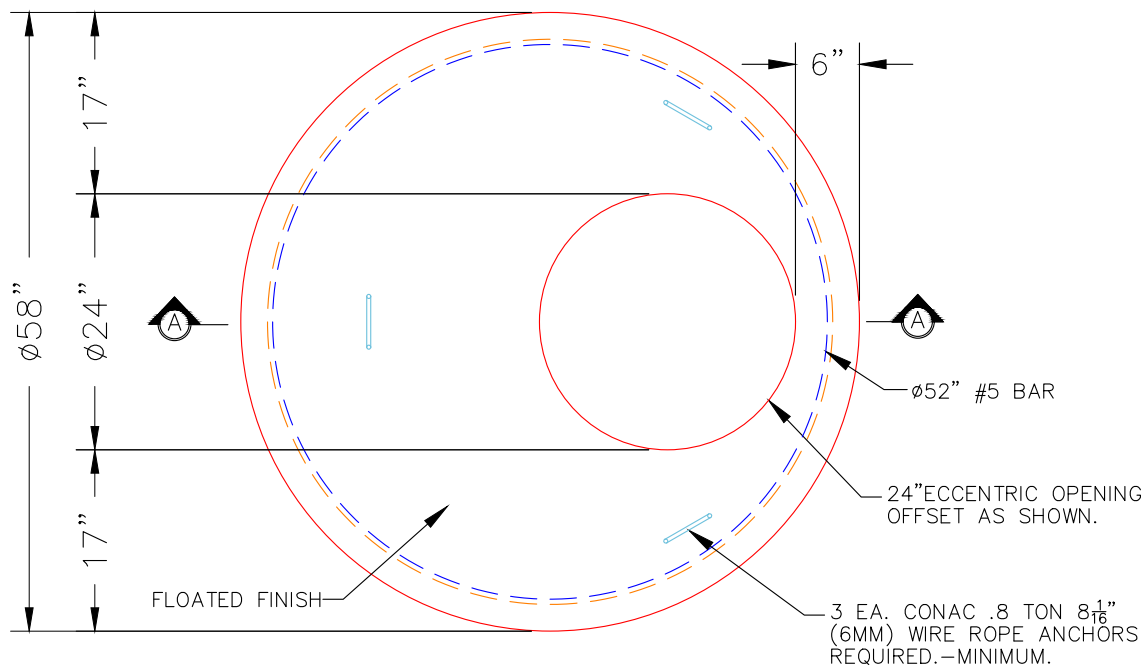

PLAN VIEW

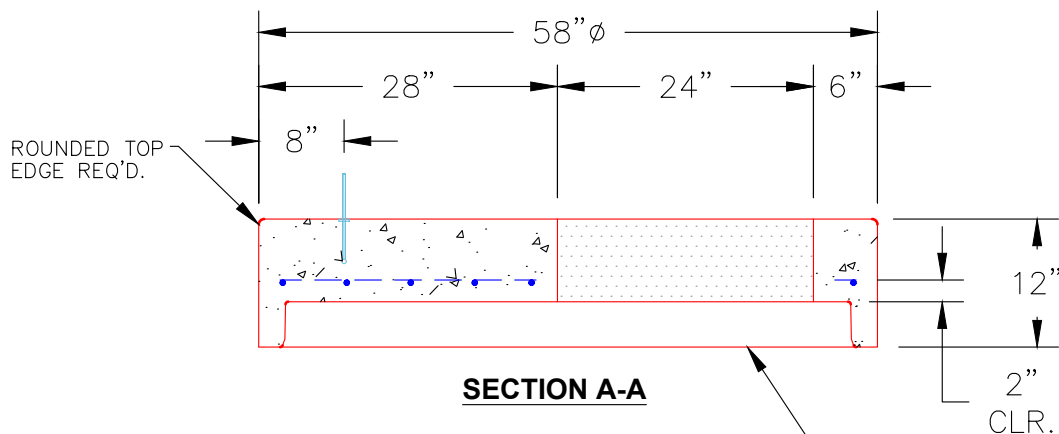

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.4cu.yd
