




Weight (Net): 13098 lb
Volume (Net): 3.35cu.yd


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/22/2026 12:46:24 PM		Tech: Jared - F PC: T. Ryan			
Structure ID: 37887-142 SBIA										
P1 BX4848-08W12FEBAV					BX BASE w/FLANGE 08W/12F/14EF F/n					
P2) 48" x 48" - BX FLAT LID 8inW SOLID F/F - 12" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/14EF F/n - 32" 1) 48" x 48" - Conseal CS-102 1.00" 1) Hole - 16 3) Hole - 8					4124 lb 13098 lb 0 lb 0 lb 0 lb ----- Structure Total: 17223 lb		Structure Notes: **KYTC STATE PROJECT** 1. PER KYTC SPRING BOX INLET A / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. SOLID TOP SLAB - NO CASTING. REINFORCING PER ASTM A615 (GRADE 60.) - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 748.75' Rim to Invert: 3.75' Slack: 3" Sump: 2" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	745'	0°	32"	12" CMP	13"	Hole 16	16"	16"	0"	0"
Invert 2	745'	90°	32"	4" CMP	5"	Hole 8	8"	8"	0"	0"
Invert 3	745'	180°	32"	4" CMP	5"	Hole 8	8"	8"	0"	0"
Invert 4	745'	270°	32"	4" CMP	5"	Hole 8	8"	8"	0"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

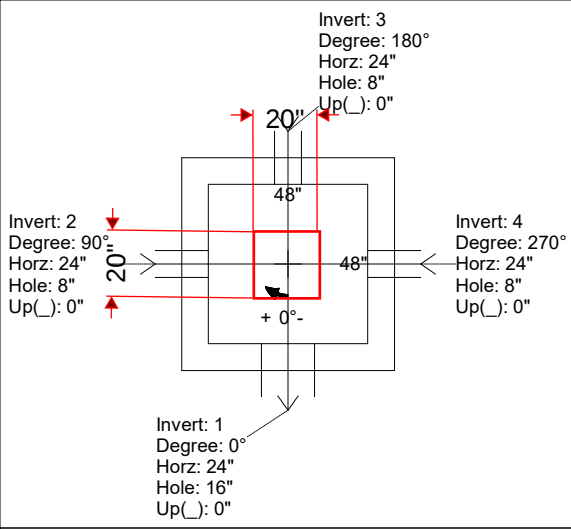

UPSIDE-DOWN VIEW (int. dimensions)


1ST POUR (FLOOR) = 8,120 LBS
2ND POUR (WALLS) = 4,978 LBS



20"x20" Hole through the center of base slab

2ND POUR (WALLS)

INSIDE WALL DIMENSIONS

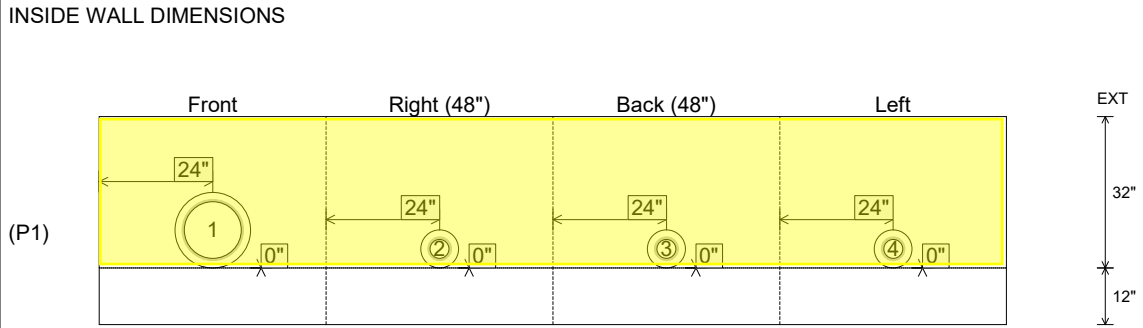

Front	Right (48")	Back (48")	Left
24"	24"	24"	24"
0"	0"	0"	0"

EXT 32" 12"

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 12"	Height (Int): 32" Height (Ext): 44"	Weight (Net): 13098 lb Volume (Net): 3.35cu.yd
----------------------------------	-------------------------------	---	--	---
